

ALIGN Mobilisation and Construction Commencement: CDM Assurance Process

Document no: 1MC05-ALJ-HS-PRO-C001-000034

Revision	Author	Reviewed by	Approved by	Date approved	Reason for revision
C01	Peter Day	Clement Chasset	Neil Hancox	22/08/2019	First Issue
C02	Isabelle Lelievre	Neil Hancox Jon Neale	Daniel Altier	25/02/2020	Update following HS2 comments

Security classification: OFFICIAL

Contents

1	Purpose	2
2	Scope	2
3	CDM Assurance Process flow (CAP5 & CAP6)	4
4	CDM Assurance Process 5 (CAP5) - mobilisation and Construction	5
5	CDM Assurance Process 6 (CAP6) - CDM Regulations Completion	6
6	Readiness Review	6
7	Appendices	11
7.1	Readiness Review Template Document no: 1MC05-ALJ-PM-TEM-C001-000002	11
7.2	Readiness Document Tracker Document no: 1MC05-ALJ-PM-TEM-C001-000003	11

1 Purpose

This procedure defines:

- How ALIGN JV demonstrate with evidence that it has fulfilled the legal requirement of the CDM regulations and comply with the CDM Client Procedure HS2-HS2-HS-PRO-000-000010 P09
- The personnel and functions within the parties who have accountability for the implementation of the processes and responsibilities for completion of the processes and those who should be consulted and informed throughout the completion of the process for the specified activities.

For the purposes of CDM, ALIGN JV is appointed as the Principal Contractor - and Designer where the work scope includes design activities. HS2 is appointed as the Client and Principal Designer. ALIGN JV is therefore responsible to comply with the CDM Assurance Process 5 - mobilisation and Construction – (CAP5) and then CDM Assurance Process 6 - CDM Regulations Completion – (CAP6)

2 Scope


This procedure is applicable to Phase 1 Main Works Civils Contracts (MWCC) for all Stage 1 works (early works) and any Stage 2 works contractually moved to Stage 1. Stage 2 works will only commence at Notice to Proceed.

The headline assets for sector C1 runs from 25km 800m at Colne Valley south embankment to 47km 750m north of Chiltern Tunnel North Portal, a distance of 21.950 kilometres.

The following chart shows the Work Breakdown Structure (WBS) for the C1 Sector (WBS Level 5) and highlights the Sections (Level 6) Lots (Level 7), Primary Assets (Level 8) and other Assets (Level 9) that will be covered by the CDM Assurance Process 5 (CAP5) and the CDM Assurance Process (CAP6).

3 CDM Assurance Process flow (CAP5 & CAP6)

Refer to the Annex 7 of the CDM Client Procedure HS2-HS2-HS-PRO-000-000010 P09. See the extract below:

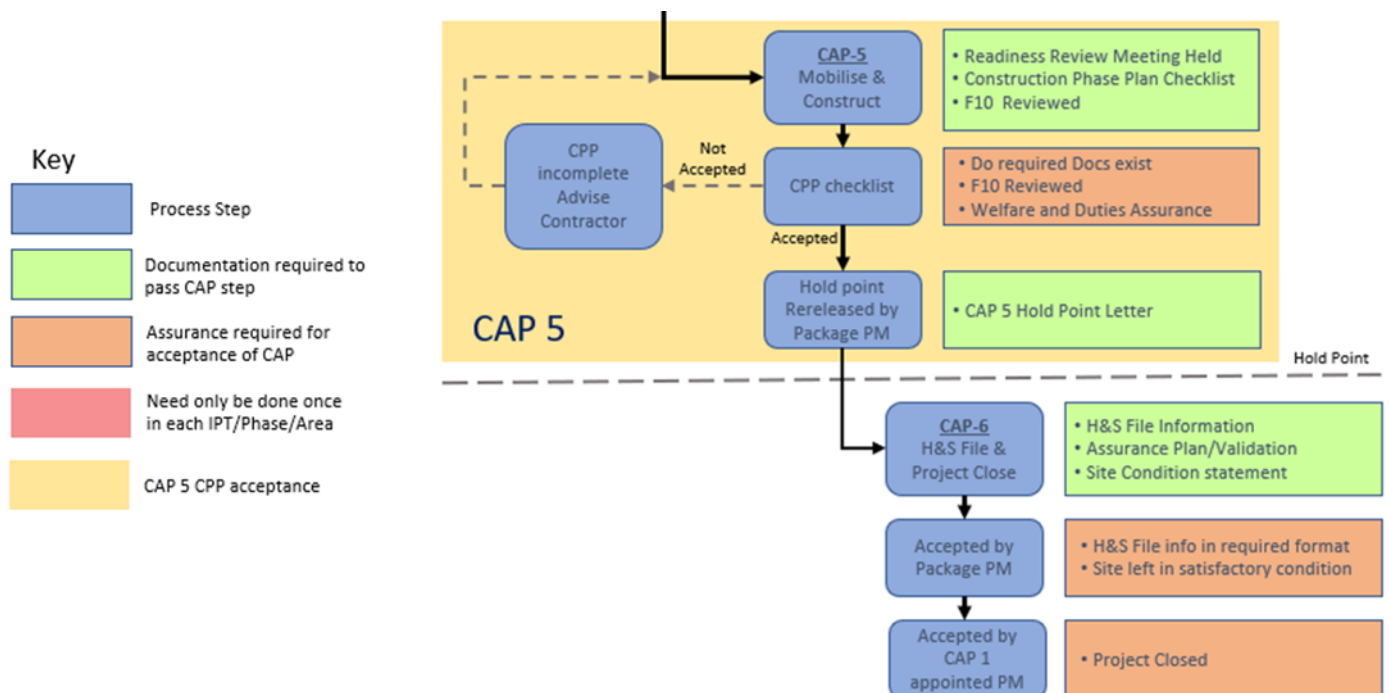

4 CDM Assurance Process 5 (CAP5) - mobilisation and Construction

The Principal Contractor/contractor must provide the minimum content uploaded on to EB for acceptance, such information to include as a minimum:

- **The Construction Phase Plan (CPP)** compliant with the below requirements. Refer to the CPP checklist in Annex 9 of the:
 - o Health & safety aims for the project
 - o Site Rules & Site Induction
 - o Arrangements to ensure cooperation between team members. (meetings etc)
 - o Arrangements for involving workers
 - o Welfare facilities (inc Fire and emergency procedures)
 - o Control of any specific site risks listed in Schedule 3, 12(2) of the CDM regulations where relevant.
 - o Controls for any significant site hazards identified within the Pre-Construction Information.
 - o The front page has been signed as self-assured by a relevant director of the Contractor

- **Minutes from the Readiness Review – Refer to section 6 of this procedure**, with actions from that have been closed

before progression to CAP6 the Client Representative must complete the CPP checklist (Annex 9 of the CDM Client Procedure HS2-HS2-HS-PRO-000-000010 P09).

CAP5 will be updated when there is a substantial change in the work or welfare establishment that is identified within the project assurance plan as requiring a new or substantially amended Construction Phase Plan.

Refer to Annex 5 of the CDM Client Procedure HS2-HS2-HS-PRO-000-000010 P09: CDM Assurance Process - Step 5 (CAP5) - Mobilise and Construct

In addition to this:

- **F10 must be reviewed**
- **Welfare facilities must be adequate**
- **A request of the CDM Assurance Point letter from HS2 after T-2 weeks (CAP 5 Hold Point Letter).** Refer to section 6 of this procedure.

5 CDM Assurance Process 6 (CAP6) - CDM Regulations Completion

At the end of construction and before the contractor is allowed to close the project. The contractor along with the Principal Designer must have provided the Health and Safety File for the project prior to completion of CAP6. As the project is closed at this point it is not anticipated that updates will be required.

Refer to Annex 6 of the CDM Client Procedure HS2-HS2-HS-PRO-000-000010 P09:
CDM Assurance Process - Step 6 (CAP6) - Project Close and Health & Safety File

6 Readiness Review

For each primary asset, and in line with the WBS above and prior to works mobilisation and commencement of construction, Readiness Reviews are organised and led by the relevant ALIGN JV Accountable and Responsible persons. Readiness Review are to utilise the appendix 7.1 and 7.2 documentation associated with this procedure and the Readiness Review is required to take into account the level of risk associated and is to be as detailed as necessary to cover mobilisation for construction, scope of works and proposed key activities at the location.

The readiness review are undertaken in order to obtain the related evidence of compliance to CDM regulations and to demonstrate that the following issues have been considered throughout the Readiness Review process:

- The programme and resources necessary to complete the project
- Health, safety and environmental preparedness
- The need for temporary works design and the arrangements in place, including, where applicable, the Principal Designers role in this
- Licences, consents and permissions necessary to execute the work and their management
- Contractual documentation
- Quality control and inspection
- Materials, plant and equipment

- Third party interfaces and the control of risk

Those personnel and functions with Responsibility and Accountability and those parties who should be Consulted and Informed are identified in the RACI table below:

Readiness Review	RESPONSIBLE	ACCOUNTABLE	CONSULTED	INFORMED
Work Sector (WBS Level 5) and Work Sections (WBS Level 6) are not specifically covered by this procedure The RACI chart is indicative for these activities.				
Sector (Level 5) RDD2	Executive Committee (ExCo) & Align Function Leads	Project Director	The Project Client, Principal Designer and Senior IPT Project Managers	HS2
Work Section WBS Level 6	Align Project Managers	Align Construction Directors	Executive Committee (ExCo), Principal Designer & Align Function Leads	Project Client and Client Team
Readiness Review	Work Lots (WBS Level 7), Primary Assets (WBS Level 8) and Assets (WNS Level 9) are covered specifically by this Procedure			
Work Lots WBS Level 7	Align Project Managers	Align Construction Directors	Executive Committee (ExCo), Principal Designer & Align Function Leads	Project Client and Client Team
Primary Assets WBS Level 8	Align Project Managers	Align Construction Directors	Executive Committee (ExCo), Principal Designer and Align Function Leads	Project Client and Client Team
Assets WBS Level 9	Align Project Managers	Align Construction Directors	Align Function Leads and Principal Designer	Executive Committee (ExCo), Project Client and Client Team

Activity below WBS Level 9 does not require Control Point as defined by CDM Client Procedure HS2-HS2-HS-PRO-000-000010 but Readiness Review process may be used as Project Management for the location or activity. The Project Client / Client Team must be Informed of this activity to allow for assurance attendance at forums				
Activities / Sub-Contract packages & other key activities	Package and Site Managers	Align Project Managers	Align Construction Directors and Align Function Leads	Executive Committee (ExCo), Principal Designer. Project Client and Client Team

Other Readiness Reviews for activities and temporary assets not covered within the Work Breakdown Structure (WBS), but using the format and templates annexed within this procedure may be facilitated by Work Package managers as required by the accountable Construction Directors, Project Managers, Package Managers, Project Managers or Site Managers.

The intention of the Readiness Review forums, planned at 12 weeks, 6 weeks and 2 weeks prior to start of work is to give progressive assurance to ALIGN JV, and ultimately the Project Directors and Project Client that ALIGN JV will be ready to mobilise (Control Point 5) and to commence construction activities (Control Point 6).

- **Construction Commencement / Mobilisation -12 Weeks:** To present first version of the populated 1MC05-ALJ-PM-TEM-C001-000002 Readiness Review Template at a forum with representatives of all relevant ALIGN JV function. Populate the 1MC05-ALJ-PM-TEM-C001-000003 Readiness Review Tracker Document with owners and dates and identify critical issues, concerns and challenges affecting proposed Construction Commencement Dates.
- **Construction Commencement / Mobilisation -6 Weeks:** mid-term update to check progress and update Tracker for formal issue to RACI personnel. Formally discuss critical issues and progress. Invitation extended to additional support as required.
- **Construction Commencement / Mobilisation -2 Weeks:** This is the “Go / No-Go” forum where all parties demonstrate readiness by completion of actions and documentation listed on the Tracker and to prepare to issue a request the CDM Assurance Point letter from HS2 (CAP5 Hold Point Letter). If it is clear at this stage that Readiness will not be demonstrable on the proposed start date, an extended period will be agreed and the start date revised accordingly

Those with roles identified as responsible for Readiness Review in the RACI table above will be required to arrange the forums.

Readiness Review forums will be in the form of workshops and meetings with the Appendix 7.1 Readiness Review Template (Document no: 1MC05-ALJ-PM-TEM-C001-000002) presented as the basis for the forum and monitored by Appendix 7.2 Tracker. The template should be populated by the Responsible Person with the input of those Consulted personnel (Align Function Leads) ahead of each forum.

The outputs from the Readiness Review forums will be formal minutes of meeting with an action list and the Appendix 7.2 Readiness Document Tracker Document no: 1MC05-ALJ-PM-TEM-C001-000003.

Formal minutes of meeting and actions arising shall be recorded on ALIGN JV Minutes of Meeting Document number 1MC05-ALJ-IM-TEM-C001-000019. Minutes of Meeting along with populated Readiness Review template and Readiness Review Tracker shall be distributed within 5 working days in accordance with ALIGN JV Document Control Procedures to The Project Director, All attendees, ExCo, Function leads and relevant Client personnel.

Alongside those identified as Accountable and Responsible for the Readiness Reviews and those persons identified as Consulted and Informed the Project Client, the Principal Designer and the following ALIGN JV functions shall be represented at all forums:

- Align D Design
- Human Resources
- Procurement
- Engineering / Methods / Temporary Works
- Quality
- Health & Safety
- Environment
- Land access
- Commercial
- Project controls / Planning
- Engagement – Stakeholder
- Consents
- Transport and Logistics
- Security

ALIGN Function Leads remain responsible for ensuring the attendance at all forums of relevant persons from within their teams. Issues should be raised within the forum to

allow for actions to be recorded and tracked within the timescales given within this procedure. In the event of exceptional circumstances, non-representation must be authorised in advance by the relevant Construction Director and arrangements made for others to inform requirements or progress updates on the relevant tracked documents and items.

The information included has been provided by various team members and is intended to give a view on how “ready” ALIGN JV are to mobilise and commence construction and may be as detailed as necessary regarding the scope of works.

Management of Change: Should there be a significant change to the scope of works and proposed key activities at the location, the relevant Align JV Construction Director shall assess the need for further Readiness Review in collaboration with Align JV Function Leads and the relevant C1.Align IPT and ExCo representatives. In the case of additional Readiness Review, the RACI personnel for activities below WBS Level 9 activities will be convened at the earliest possible opportunity to allow for sufficient time and resource for an effective Readiness Review to be undertaken

7 Appendices

- 7.1 Readiness Review Template Document no: 1MC05-ALJ-PM-TEM-C001-000002
- 7.2 Readiness Document Tracker Document no: 1MC05-ALJ-PM-TEM-C001-000003
