

Safety, Health, and Wellbeing Management (Construction Phase) Plan

1MC05-ALJ-HS-PLN-C001-000006 C09

Revision	Author	Reviewed by	Approved by	Date approved	Reason for revision
P01	David Tennant	Jon Neale	Jerome Furge	12/10/2017	First Issue
P02	David Tennant	Jon Neale	Jerome Furge	21/12/2017	Updated following HS2 comments
C01	Peter Day	Neil Hancox	Daniel Altier	24/05/2019	General update to suit WI and HS2 strategy changes - Updated for Early Works

C02	Peter Day Isabelle Lelievre	Neil Hancox	Daniel Altier	15/01/2020	General update for Stage 2
C03	Isabelle Lelievre	Peter Day Neil Hancox	Daniel Altier	2/04/2020	Updated following HS2 comments
C04	Isabelle Lelievre	Neil Hancox	Daniel Altier	5/06/2020	Updated following HS2 comments
C05	Isabelle Lelievre	Neil Hancox	Daniel Altier	17/11/2020	General update
C06	Ralph Ashwood	Neil Hancox	Daniel Altier	02/08/2022	General update including CDM Duty holders
C07	Ralph Ashwood	Neil Hancox	Daniel Altier	13/01/2023	Updated following HS2 comments
C08	Ralph Ashwood	Neil Hancox	Daniel Altier	25/01/2023	Updated following DC comments
P03	Ralph Ashwood	Neil Hancox	Loic Menard	10/04/2024	General update, including scope of work to include C1 North
C09	Eleni Kondyli	Neil Hancox	Coralie Peroux	29/05/2025	General Review and edit to remove outdated consultation links

Security classification: OFFICIAL

Handling Instructions: This Plan includes the Construction Phase (Health and Safety) Plan (CPP) which sets out how work is to be planned, managed, monitored and coordinated on site during the Construction Phase in Sector C1 of the UK High Speed 2 line (HS2) programme Phase 1 by ALIGN JV as the Principal Contractor.

Contents

1	Purpose	1
2	Scope	2
3	Definitions and abbreviations	4
4	Description of the project	5
	Assets	5
	Organisation of the project team	6
	Key locations	6
5	Occupational Health and Safety Goals & Objectives	11
	Safe @ Heart	11
	HS2 Health and Safety Strategy	12
	Aim High	16
	ALIGN worker behaviour and engagement	17
	ALIGN JV Aim High Cultural Development Programme	17
	ALIGN 12 Health & Safety Basics	18
	Just and Fair culture	18
	Duty to Stop (SLAM)	20
	Suspension of Works	21
	SLAM & IMPROVE Process	22
6	CDM Duty Holders	23
	Client	23
	Principal Designer	23
	Principal Contractor	23
	Designers	24
7	Pre-construction Information	25
8	Management Arrangements	26
	General Responsibilities	26
	Roles and Responsibilities of Key Personnel	28
9	Management System arrangements	30
	Health and Safety advice	30
	Assurance activities	31
	Communication and Consultation	34
	Exchange of Design Information/Design Changes	36
	Selection and Control of Contractors and Suppliers	37
	Co-operation and Coordination	39

	Undertakings and Assurances	40
	Competence & Fitness to work	40
	Fit for Role Medical	45
	Control of Persons Entering the Site	45
	Welfare Facilities	46
	Notification, Reporting and Investigation of Incidents	47
	Confidential Reporting of Serious Concerns – whistle Blowing	48
	Enforcement Notices	48
	Risk Assessments and Method Statements	49
	Work Authorisation / Permits for Work	52
	Point of Work Risk Assessment (POWRA)	53
	Personal Protective Equipment	54
	Site Rules	57
	Emergency arrangements	57
10	Occupational Health and Wellbeing	59
11	Controlling Significant Site Risks	59
	Dealing with Utility Services	59
	Temporary Works	60
	Working at Height	60
	Scaffolding	61
	Ladders	61
	Mobile Elevating Working Platforms (MEWPs)	61
	Prohibited types of plant/equipment	61
	Pressurised systems	62
	Traffic Management and Segregation of Vehicles and Pedestrians	63
	Protection of work platforms and haul roads to prevent over run	64
	Delivery Vehicles and Logistics.	64
	Unloading/Loading of Materials and Equipment from Vehicles	65
	Loading/Offloading of Mobile Construction Equipment from Vehicles	65
	Poor Ground Conditions	65
	Mobile Construction Equipment	66
	Other Plant and Equipment	66
	Work On or Near Fragile Materials	68
	The Control of Lifting Operations	68
	Excavations	69
	Confined Spaces	69
	Work Near Water Giving a Risk of Drowning	70
	Explosives and Cartridge tools	70
	Housekeeping and Storage of Materials and Work Equipment	70
	Portable Electrical Equipment	70
	Erection of Structures	70

	Severe Weather Conditions	70
	Fire Hazards	71
	Hand Held Work Equipment	71
	Interaction with the Public	71
	Sharp Objects including Barbed Wire and Thorns	72
	Demolition Works	72
	Work in Colne Valley lakes and other bodies of water	72
	De-watering	72
	Piling	72
	Contaminated Land	73
	Asbestos Containing Materials	73
	Control and Use of Hazardous Substances	73
	Unexploded Ordnance	73
	Manual Handling	74
	Noise and Vibration	74
	Exposure to UV Radiation (from the sun)	75
	Substance Abuse	75
	Toxic Plants	76
	Weils Disease and Lyme Disease	76
	Contact / Exposure to Agrochemicals and Fertilizers/ Animal Faeces	76
12	Health and Safety File	76
13	Reference Documents	76


1 Purpose

- 1.1.1 The purpose of the Safety, Health and Wellbeing Management Plan (SHWMP) is to describe in broad terms how the ALIGN joint venture plans to manage health, safety and wellbeing during the course of the Sector C1 Main Works Project (C1MWCC). The C1 sector of HS2 consists of 21.6km of high-speed rail infrastructure in a rural environment.
- 1.1.2 This Plan includes the Construction Phase (Health and Safety) Plan (CPP) which sets out how work is to be planned, managed, monitored and coordinated on site during the Construction Phase in Sector C1 of the UK High Speed 2 line (HS2) programme Phase 1 by ALIGN JV as the Principal Contractor.
- 1.1.3 ALIGN JV is a joint venture of three international and privately-owned infrastructure companies; Bouygues Travaux Publics, a subsidiary of Bouygues Construction, Sir Robert McAlpine, and VolkerFitzpatrick, a subsidiary of VolkerWessels.
- 1.1.4 This Plan includes HS2's requirements defined in the Works Information including but not limited to:
- WI 1100 Health and Safety;
 - WI 1150 Occupational Health is integrated in the Health Management Plan
 - Supply Chain Health and Safety Approach HS2-HS2-HS-STD-000-000006
- 1.1.5 Each contractor delivering work packages for ALIGN JV is required to develop their own Health and Safety Management Plan that states how they intend to meet the requirements of this document and any other legal and/or contractual obligations. The Health and Safety Management Plans will be reviewed and accepted by ALIGN as Principal Contractor for sector C1 before contractors may commence work. In any case, each contractor must comply with any directions given by the Principal Designer or the Principal Contractor and the parts of the construction phase plan that are relevant to that contractor's work on the project.
- 1.1.6 Contractors must inform ALIGN JV in writing in advance of their intention to sublet or enter into any agreement with a sub-contractor to deliver elements of their work. Contractors should await authorisation from ALIGN JV before proceeding. The Contractor arrangements for management of Sub-Contractors must be covered in the Contractors Health and Safety Management Plan. Contractors shall inform ALIGN if they become aware or are aware of any breach of this plan by them or any third party.

- 1.1.7 Contractors shall also comply with the Health Management Plan 1MC05-ALJ-HS-PLN-C001-000003, specifically the more stringent occupational health exposure limits.

2 Scope

- 2.1.1 ALIGN JV has been awarded by HS2 the MWCC contract –design and construction- for the Sector C1 on the 31st of July 2017. This includes stages 1 and 2 with a notice to proceed break between them.
- 2.1.2 Notice to Proceed to deliver the C1 package of HS2 was issued on the 15th of April 2020.
- 2.1.3 The plan also covers all the C1 North Construction site, South Heath Cutting.
- 2.1.4 Safety, Health, and Wellbeing Management within Sector C1 is based upon requirements from within the existing Safety Management Systems of the ALIGN JV Parent Companies, the expectations of HS2 and its approach in:
- Implementing, maintaining and supervising all safety and health measures in connection with the performance and completion of the Work;
 - Ensuring the competence of ALIGN JV staff, Contractors, Sub-Contractors and each individual connected with the project on behalf of ALIGN JV.
 - Developing the right behaviour within the team to achieve the desired results.
 - Ensuring compliance with OHSAS 18001 / ISO 45001 Occupational Health and Safety Management Systems requirements and all relevant local legislation.
- 2.1.5 This Plan describes:
- The system and measures to be implemented with the objectives of protecting the Safety, Health and Wellbeing of all personnel employed within Sector C1 and others who may be affected by the Works.
 - How activities are managed with regards to safeguarding Safety, Health and Wellbeing and it defines the architecture, the permanent and general concepts and the organisation of the occupational health and safety management system to be implemented on the Project.
- 2.1.6 It applies to all employees of the joint venture and all aspects of ALIGN JV work activities and will be updated by any significant changes and re-issued at least annually.

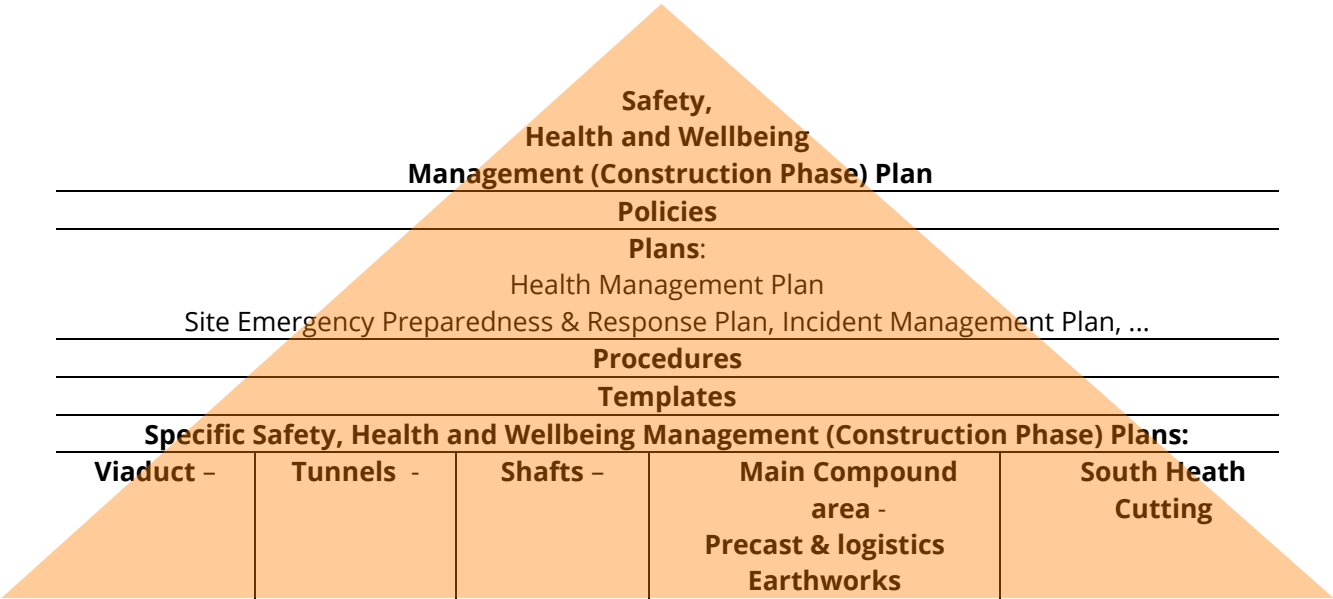

- 2.1.7

In addition to this global Safety, Health and Wellbeing Management (Construction Phase) Plan, the template 1MC05-ALJ-HS-TEM-C001-000057 is populated by ALIGN JV to show the safety, health and wellbeing arrangements specific for each package of work.
- 2.1.8


The management, organisation, and resource necessary to plan, control, implement and monitor the designs for this project is covered in the Design Management Plan 1MC05-ALJ-DS-PLN-C001-000001.

3 Definitions and abbreviations

SHWMP	Safety, Health, and Wellbeing Management Plan
C1MWP	C1 Main Works Project
CPP	Construction Phase Plan
CDM	Construction (Design and Management) Regulations 2015
HS2	UK High Speed 2 line
ALIGN JV	Joint venture of three international and privately-owned infrastructure companies; Bouygues Travaux Publics, a subsidiary of Bouygues Construction, Sir Robert McAlpine, and VolkerFitzpatrick, a subsidiary of VolkerWessels
EDMS	Electronic Data Management System https://alignjv.withbc.com/bc/bc.cgi/0/7962?_meta_feature=recent_projects
PCIP	Pre-Construction Information Pack
CoCP	Code of Construction Practice
AONB	Areas of Outstanding Natural Beauty
OH&S	Occupational Health & Safety
PPE	Personal Protective Equipment
POWRA	Point of Work Risk Assessment
RAMS	Risk Assessment and Method Statement
RIDDOR	Reporting of Injuries, Diseases and Dangerous Occurrences Regulations
SMS	Safety Management System
SSSTS	CITB Site Supervisor Safety Training Scheme (2-day course)
SHWeLT	Safety, Health, and Wellbeing Leadership Team
U&A	Undertakings and Assurances
CCP	Commitments Compliance Plan Document no. : 1MC05-ALJ-SE-PLN-C001-000002
CSCS	Construction Skills Certification Scheme
CPCS	Construction Plant Competence Scheme
CLOCS	Construction Logistics for Cyclist Safety
RTMP	Route-wide Traffic Management Plan

4 Description of the project

- 4.1.1 The project involves the design and construction of the Colne Valley Viaduct - 3.5 km in length, cut and fill earthworks, a culvert and side road overbridge, twin-bored tunnels -16 km in length through the Chiltern Hills with five ventilation/intervention shafts and cross passages connecting up-line and down-line tunnels at agreed intervals in line with final detailed design throughout the tunnel route.
- 4.1.2 The project has been notified to the HSE as a construction project with Notification No. 54647A2D19.

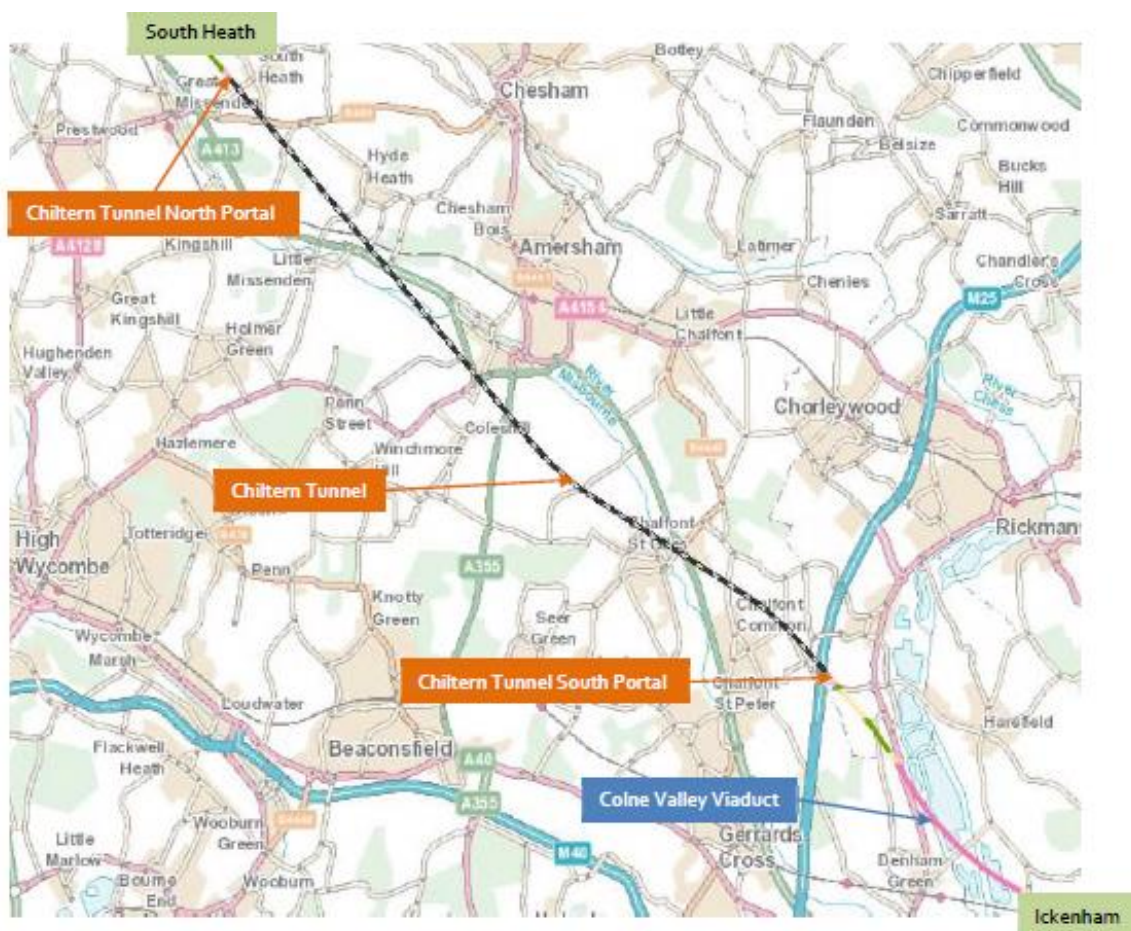

Assets

- 4.1.3 The headline assets for sector C1 runs from 25km 800m at Colne Valley south embankment to 47km 750m north of Chiltern Tunnel North Portal, a distance of 21 kilometres.

- 4.1.4 C1 North site, referred to as South Heath Cutting going onwards, will be at the north of the north portal. The scope of work involves:
- 4.1.5 Area : C South Heath Cutting comprises:
- Structural earthworks and landscape mitigation earthworks at South Heath cutting between 47+750 and 49+780 (approx. 450,000m3)
 - Footpath GMI/12 Overbridge
 - Footpath GMI/2 Accommodation Overbridge
 - Cottage Farm Overbridge
 - Leather Lane Overbridge
 - Havenfield Drop Inlet Culvert
 - Leather Lane Drop Inlet Culvert
 - South Heath MPAT
- 4.1.6 The Primary Assets as described in the ALIGN-D Design Management Plan 1MC05-ALJ-DS-PLN-C001-000001.


Organisation of the project team

- 4.1.7 The global executive and management organisation of ALIGN JV organisation is described in The Project Execution Plan 1MC05-ALJ-PM-PLN-C001-000001 which is the overarching document for the delivery of the project and links together all the ALIGN systems, processes and procedures which are currently deemed necessary to deliver the C1 sector Works.
- 4.1.8 ALIGN JV is the Principal contractor. ALIGN-D is the Designer. HS2 is the Client and the Principal Designer. See [CDM Duty Holders](#).
- 4.1.9 Detailed organisational charts are regularly updated and available in our Electronic Data Management System (EDMS) named [Business Collaborator](#):
- ALIGN JV organisation chart: 1MC05-ALJ-HR-CHT-C001-000001
 - ALIGN-D organisation chart: 1MC05-ALJ-HR-CHT-C001-000003
 - HS2 organisation chart: 1MC05-ALJ-HR-CHT-C001-000002
- Also available on our digital screens, in the HR section.

Key locations

- 4.1.10 Specific organisation and key dates of start and works duration are in the [site-specific construction phase plans](#):

- Viaduct - Package 1 (Design): 1MC05-ALJ-HS-PLN-CS01_CL01-000002
- Tunnel - Package 4 (Design): 1MC05-ALJ-TN-PLN-CS02_CL04-000007
- Cross Passages: 1MC05-ALJ-TN-MST-CS02_CL04-000019
- Shafts - Package 3 (Design): 1MC05-ALJ-HS-PLN-CS02_CL04-000001
- Main Compound area including Pre-cast & logistics and Earthworks - Package 2 (Design): 1MC05-ALJ-CL-PLN-C001-000025
- North Portal - 1MC05-ALJ-HS-PLN-CS02_CL16-000001
- C1 North Area : C South Heath Cutting : 1MC05-ALJ-HS-PLN-CS03_CL05-000002

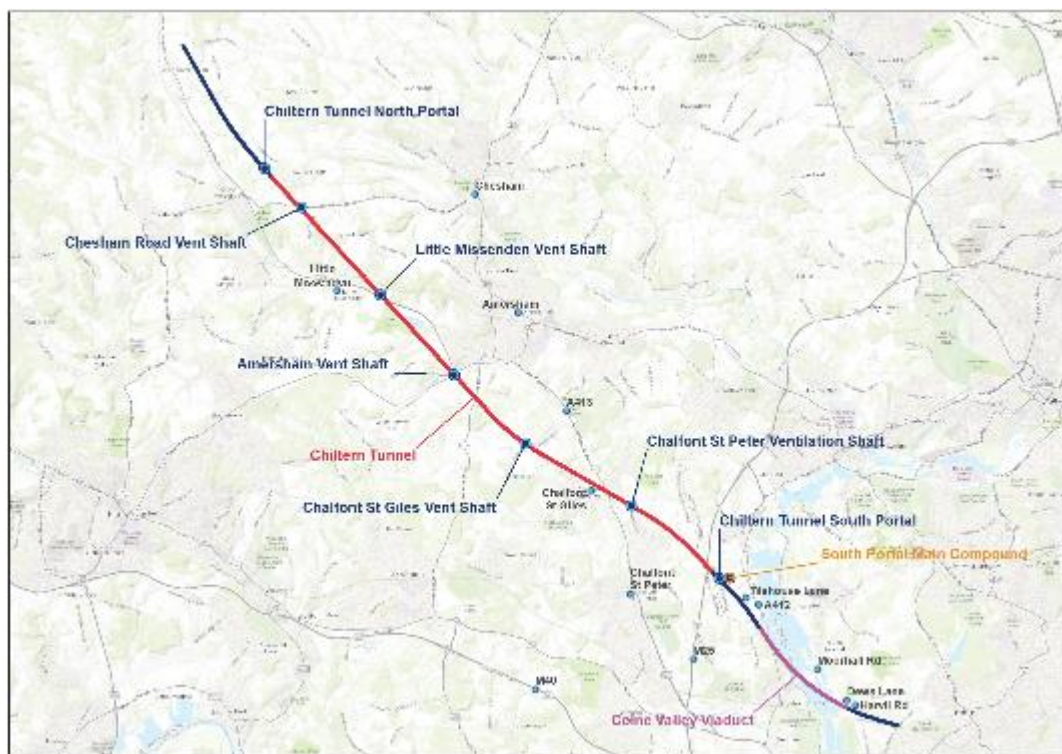

HS2 Site Name	Site Easting	Site Northing	Gate Name	Gate Easting	Gate Northing	Site Address
Colne Valley Viaduct South Embankment	505983	187585	C11G1	506103	187465	Harvil Road, Hillingdon, London Borough of Hillingdon UB9 6JW - What3Words//dome.earth.marked
HP07	505983	187585	C11G1A	506060	187725	Harvil Road, Hillingdon, London Borough of Hillingdon UB9 6JW - What3Words//charmingly.strict.grass
Colne Valley Viaduct Satellite Compound	505579	187801	C11G2	505638	187825	Dews Lane, London Borough of Hillingdon UB9 6JN - What3Words//agrees.grew.cliff
Colne Valley Viaduct Dews Lane Compound	506000	187957	C11G2A	505998	187970	Dews Lane, London Borough of Hillingdon UB9 6JN - What3Words//rear.latest.dusty
Colne Valley Viaduct Storage	504705	188442	C11G3	504665	188450	Moorhall Road, London Borough of Hillingdon UB9 6PB - What3Words//wrong.luck.moss
Colne Valley Viaduct Storage Haul Road Crossing	504705	188442	C11G3A	504696	188475	Moorhall Road, London Borough of Hillingdon UB9 6PB - What3Words//frost.marker.handy
Colne Valley Viaduct Jetty Storage	504754	188582	C11G4	504690	188490	Moorhall Road, London Borough of Hillingdon UB9 6PB - What3Words//device.fits.plant
Colne Valley Viaduct River Colne Access			C11G4A	504055	188539	North Orbital Road, Denham, Buckinghamshire UB9 5HB - What3Words//pasta.cargo.modern
Haul Road access			C11G5	503625	189796	North Orbital Road, Denham, Three Rivers, Buckinghamshire UB9 5HD - What3Words//levels.gross.winks
Colne Valley Viaduct Laydown	503624	189835	C11G6	503626	189817	North Orbital Road, Denham, Three Rivers, Buckinghamshire UB9 5HD - What3Words//gown.linked.final
Colne Valley Viaduct North Launch	503444	189986	C11G7	503381	190049	Old Shire Lane, Denham, Three Rivers, Buckinghamshire WD3 9YD - What3Words//hiding.brands.types
Colne Valley Viaduct North Embankment	503527	190083	C11G8	503580	190064	Old Shire Lane, Denham, Three Rivers, Buckinghamshire WD3 9YD - What3Words//wacky.breath.angle

Colne Valley Viaduct Main Compound	502964	191234	C11G9	503199	190961	Tilehouse Lane, Denham, Three Rivers, Buckinghamshire UB9 5DD - What3Words//wire.years.valid
Colne Valley Viaduct Main Compound	502964	191234	C11G10	502849	191475	Chalfont Lane, Three Rivers, Hertfordshire WD3 9XN - What3Words//bravo.smoke.solo
Chiltern Tunnel South Portal Main Compound	502572	191183	C12G1	502454	191469	Chalfont Lane, Three Rivers, Hertfordshire WD3 9XN - What3Words//cherry.play.fits
Chiltern Tunnel South Portal Main Compound	502572	191183	C12G2	502454	191469	Chalfont Lane, Three Rivers, Hertfordshire WD3 9XN - What3Words//cherry.play.fits
Chiltern Portal	502162	191393	C12G3	502165	191549	Chalfont Lane, Three Rivers, Hertfordshire WD3 9XN - What3Words//will.smiled.oven
Chalfont St Peter Vent Shaft	500084	193153	C12G4 x 3 assets	500132	193184	Chesham Lane, Chalfont St. Peter, Chalfont St Giles, Buckinghamshire SL9 0PJ - What3Words//insert.shower.moment
Chalfont St Peter Vent Shaft	500084	193153	C12G4A	499647	192921	Amersham Road, Chalfont St. Peter, Buckinghamshire SL9 0PA - What3Words//guides.young.harp
Chalfont St Peter Vent Shaft River Misbourne access			C12G4B	499172	193713	Pheasant Hill, Chalfont St Giles, Buckinghamshire HP8 4NL - What3Words//newest.forest.equal
Chalfont St Giles Vent Shaft	497213	194820	C12G5	497179	194734	Bottom House Farm Lane, Chalfont St Giles, Seer Green, Buckinghamshire HP8 4EG - What3Words//mats.toned.bring
Amersham Vent Shaft	495316	196660	C12G6 x 2 assets	495363	196677	Whielden Street, Amersham, Coleshill, Buckinghamshire HP7 0JD - What3Words//beard.lasted.lofts
Amersham Vent Shaft Office	495389	196628	C12G6A	495370	196671	Whielden Street, Amersham, Coleshill, Buckinghamshire HP7 0JD - What3Words//snow.vase.admiral
Uc Whieldon Lane, Amersham [RH-040]			C12G7	495146	196569	Amersham Road, Amersham, Coleshill, Buckinghamshire HP7 0JD - What3Words//united.spun.paused
Little Missenden Vent Shaft River			C12G8	493505	198642	Mop End Lane, Little Missenden, Buckinghamshire HP7 0RJ - What3Words//factor.chest.clash

Misbourne Access						
Little Missenden Vent Shaft	493357	198816	C12G9	493250	198791	A413, Little Missenden, Buckinghamshire, HP7 0RQ - What3Words//tape.drops.alien
Chesham Road Vent Shaft	491217	201144	C12G10	491276	201172	Kings Pond, Frith Hill, Balinger Bottom, Great Missenden, Buckinghamshire HP16 0RD - What3Words//shifting.skipped.seemingly
Chiltern Tunnel North Portal	490322	202083	C12G11	490062	202014	Hill House, Ballinger Road, Balinger Bottom, Great Missenden, Buckinghamshire HP16 9QE - What3Words//basically.tutored.reduce
Chiltern Tunnel North Portal Access Road	489654	201647	C12G12	489661	201603	A413, Balinger Bottom, Great Missenden, Buckinghamshire HP16 9LS - What3Words//sizing.landings.rejoins

5 Occupational Health and Safety Goals & Objectives

Safe @ Heart

5.1.1 ALIGN and HS2 have common aspirations and goals in terms of safety, health, and wellbeing. We all want to work together to build the high-speed railway in a way that does not harm anyone now or in the future. HS2, as the Client and Principal Designer expresses its health and safety approach and values as shown below.



What does safety mean to us?



Safety is...
Caring for our workforce, our passengers and the public, by creating an environment where no one gets hurt.

Good looks like:



HS2 Health and Safety Strategy

Why

- 5.1.2 Why we have a once in a generation opportunity and obligation to raise standards for occupational health, safety and wellbeing higher than any other mega-project.
- 5.1.3 The right of everyone working on or impacted by HS2 to go home safe and well
- 5.1.4 Our duty to lead the way for other to follow
- 5.1.5 Our belief that excellence in health and safety performance is fundamental to how we achieve our mission

How

- 5.1.6 We will deliver a step-change in occupational health, safety and wellbeing for the benefit of our construction workforce, our neighbours, our future passengers and maintenance workforce and wider industry through:

- Safe at heart, our programme-wide philosophy, approach and campaign
- Collaborative health and safety leadership
- Building an inclusive culture
- Setting new and challenging health and safety performance measures

What

- 5.1.7 we commit to deliver during the lifecycle of this strategy to support our belief that everyone working on or impacted by HS2 has the right to go home safe and well.
 - Our 7 health and safety risk focus areas, aligned to our objectives
 - Our 21 Safe at heart commitments which represent the outcomes against which we will measure our performance progress

HS2 7 Health and Safety Risk focus Areas

Occupational Health and Wellbeing

5.1.8 We believe occupational health and wellbeing matters as much as safety. Our commitment is to:

- raise the profile of occupational health and wellbeing;
- design and create positive workplaces that empower our people to thrive; and
- eradicate, wherever possible, and minimise exposure to the top five causes of occupationally acquired illness and/or disease.

5.1.9 Over the next five years we will pursue several key interventions to achieve this. They include: the use of independent research into the causes of those illnesses and diseases; developing next-generation systems that will monitor exposure to health risks in construction; improving worker wellbeing support; and attracting more occupational health professionals into construction.

Workforce safety

5.1.10 We believe every member of our workforce, during the construction and operation of the railway, has the right to go home unharmed. Our commitment is to:

- develop, promote and reward our frontline and operational supervisors for their safety leadership;
- maximise the use of technology and smarter ways of working; and
- develop a Safe at Heart culture across the programme, empowering every individual
- to speak up and make safe decisions.

5.1.11 The interventions we will manage over the next five years include: developing how we measure safety culture; using technology and innovation to improve shared learning; and enhancing leadership and recognition in our supervisor community.

Informed learning

5.1.12 We will measure the impact and effectiveness of our health and safety interventions through robust assurance processes. Our commitment is to:

- undertake risk-based assurance to identify potential issues; and
- develop a learning culture, where people feel empowered to report and where the business takes action to embed learning.

5.1.13 Our emphasis over the next five years will be to further develop our processes and procedures for assurance and shared learning and ensure this is continuously

improved as new contractors join the programme in Phase One and on to Phase Two.

Safe supply chain management

- 5.1.14 We will engage all tiers of the supply chain in transforming health and safety standards, so they contribute to the success of the project. Our commitment is to:
- select and develop our supply chain partners based on their ability to demonstrate shared values and excellent safety leadership;
 - be an empowering client, enabling, incentivising and, where beneficial, partnering with our supply chain to innovate and deliver safely; and
 - hold each other to account for high standards of occupational health, safety and wellbeing.
- 5.1.15 As we continue to procure and manage our growing supply chain over the next five years we will: work with supplier relationship management to develop health and safety improvements; ensure health and safety is embedded into strategic supply chain market engagement; and develop health and safety engagement with suppliers in the tier two and below communities.

Health and safety by design

- 5.1.16 We will set new standards by building our design capability to identify and mitigate health and safety risks in construction, maintenance and the future operation of the railway. Our commitment is to:
- manage the impact of design and specification changes, ensuring health and safety is always our first consideration;
 - wherever possible, design through a virtual environment to 'design out' risk and error and reduce unnecessary design-related site visits; and
 - design infrastructure so all routine, planned trackside maintenance can be carried out outside operational hours.
- 5.1.17 Over the next five years, the interventions we will manage include: improving how we manage temporary works design; improving our knowledge and understanding of health risks during design stages; and facilitating the sharing of lessons in the design community.

Public and community health and safety

- 5.1.18 We respect the people and the places that are affected by our work. We recognise that while the long-term benefits of HS2 will be huge, construction affects the lives of thousands of people. Our commitment is to:

- get to know the communities along the route so we can understand the effects of construction on vulnerable people and respond in the best way we can;
- invest in the communities where HS2 operates, and plan our works to minimise adverse health, safety and wellbeing impacts on communities and our workforce; and
- adopt measures to minimise road-related risks in communities and those driving to work in our supply chain.

5.1.19 The themes we will develop over the next five years are: enhancing our approach to road risk; developing our strategy for supporting vulnerable people affected by our works; and enhancing our approach to specialist security.

Safe operations

5.1.20 We will design and build a railway that is safe for our future operational and maintenance workforce and future passengers. Our commitment is to:

- always protect our workforce when they are required to work on or near the line;
- provide a safe means to access all areas of the infrastructure, including trackside, for future operations and maintenance workforce; and
- design our railway and future train service so they can be operated safely.

5.1.21 Our approach to managing this focus area is in line with the regulator's requirements to bring the railway into safe operation. To achieve this, work areas include: safety assurance processes; design and ergonomics; and continual engagement with Network Rail.

Aim High

C1 ■ **ALIGN**

HS2

Team Charter

HS2 VISION:

To be a catalyst for growth across Britain



C1 MISSION:

Aim High in all that we do to deliver an excellent and sustainable project on time and within budget, and in line with our values, promises and commitments

LEADERSHIP

OUR VALUES AND PROMISES

SAFETY



Everyone home safe
and well every day

RESPECT

Mindful and inclusive
of diverse views,
opinions and cultures



EXCELLENCE

Innovative to exceed the
expectations of our
customers and stakeholders



INTEGRITY

Stakeholder
relationships that
are built on trust



COLLABORATION

One team working
together for the good
of the project



WE COMMIT TO:

- Lead by example to develop a responsible, safe and healthy culture
- Empowering everyone to challenge and contribute to a safe and healthy environment
- Continually improve standards through learning, sharing and promoting best practice

- Engaging all with a culture of equality, diversity and inclusion
- Minimising our impact on the environment, neighbours and communities
- Listen to, appreciate and challenge others to foster change for the greater good

- Aim High to deliver best value that more than satisfies our customer and other stakeholder expectations
- Being innovative and technically excellent to deliver sustainable projects with a legacy we can all be proud of

- Being open, honest and fair in all relationships to maintain trust
- Delivering on our C1 promises and commitments and the HS2 Undertaking and Assurances
- Developing a fair and just culture by appropriate visible leadership

- Working in teams, not alone, to deliver an exceptional project
- Engaging with our supply chain, our people and peers to create a legacy for Britain
- Harnessing a culture of sharing lessons learned, ideas and innovation at all levels

COMMITMENTS

ALIGN worker behaviour and engagement

- 5.1.22 ALIGN requires a high standard of safe working from its employees and requires the same high standards from its contractors. ALIGN will not tolerate poor safety behaviours within the office or at any of its site locations, and in order to develop the behaviours we want on the project, we will be rolling out our Cultral Development Programme

ALIGN JV Aim High Cultural Development Programme

- 5.1.23 As part of Aim High Cultural Deveelopment we will embed the Saipem Foundation Leadership in Health and Safety (LiHS) programme, providing workshops and leadership Tools to support three axis of focus on Leadership, Major Risk and Reward and Recognition.
- 5.1.24 Aspects of Aim High Cultural Development will be incorporated in project branding and routine daily activity such as pre-work briefings for all construction activities, the ALIGN JV observation process, Project induction training and on-boarding processes.
- 5.1.25 Aim High is designed to complement and not to replace existing Contractor Cultural Development programmes. Contractors will be required to implement their own existing Cultural Development programmes throughout the duration of the works.
- 5.1.26 All who work on the project are further reminded of the programme's principles and objectives by attending Safety Day briefing which are delivered on a half-yearly basis. These briefings are bespoke and will be delivered by trained members of staff.
- 5.1.27 The subject matter of each briefing will vary but will always embrace matters and concerns surrounding Safety, Health and Wellbeing.
- 5.1.28 This unique formula of constantly reminding everyone (little but often) of the importance of being vigilant at all times, empowers the workforce to speak up and challenge on all matters of concern. Continually communicating with the work force allows the project to both create and sustain a culture of value and worth where each individual is a committed member of the project team and not just a participant.
- 5.1.29 The Aim High cultural development programme will be embraced and supported by all who work within the ALIGN JV allowing everyone to experience the excellence from being part of a great team that delivers and delivers successfully.

ALIGN 12 Health & Safety Basics

ALIGN has implemented and will assist its contractors in any reasonably practicable way to facilitate the respect of these 12 Health & Safety Basics.



Just and Fair culture

5.1.30 ALIGN JV fair culture is branded as Aim High and is developed to include management of behaviour on site to ensure it meets ALIGN JV expectations with regard to:

- Respect for good site practice and avoidance of horseplay
- Negligent acts
- Breach of Working Area rules
- Abusive behaviour.

5.1.31 Our positive safety culture is supported by our Aim High framework that secures the participation and engagement of our workforce, ensures expectations and accountabilities are clearly defined, and that all our stakeholders are treated fairly

and equitably. This framework provides a charter to equitably manage safety behaviours, inclusive of the reward and recognition of positive safety behaviours, and the consistent and transparent management of any substantiated negative safety behaviours.

5.1.32 Our Just Culture Framework is defined by the following 5 pillars:

1. Informed Culture - Persons are provided the necessary competency, information, instruction, and training
2. Reporting Culture - An organisational culture which fosters all persons proactively reporting all safety observation, dangerous occurrence, incident or hazard and best practices.
3. Just Culture - Trust within our organisation that safety matters will be actioned; underpinned by the two-way transfer of safety critical information
4. Flexible Culture - People have the necessary competency and level of risk awareness to be flexible, adaptable, and vigilant to manage change
5. Learning Culture - Organisational transparency required to learn from safety incidents or failure

Communicating health and safety concerns

5.1.33 All construction personnel are permitted to stop work if they feel at risk. All staff have a responsibility to raise concerns about issues and where necessary stop work immediately if they consider that any aspect of the health, safety and wellbeing of any person is at risk.

5.1.34 All construction personnel are expected to correct unsafe situations immediately if they can and to raise concerns issues to their supervisors or at the Daily Briefings and/or Toolbox Talks.

Safety health and wellbeing Observation Reporting (Aim High App)


5.1.35 ALIGN operates a safety observation report system whereby all personnel is able and encouraged to report any health, safety and wellbeing related observations that may occur. The observation reporting system is also encouraged for the reporting of any good practice or deficiency in any aspect of the delivery including quality, equality, working standards, defects, non-conformance, environment, and sustainability, and follows the Align Values.

5.1.36 The observations can relate to unsafe situations or near misses, but also best practices.

- 5.1.37 Observations are reported by means of a app that can be accessed via mobile phone. The app is used during the on boarding process so all personnel can access this. QR Codes providing a link to the App are also posted on site.
- 5.1.38 Observation cards are also available and can be posted in the boxes provided in canteens and offices.
- 5.1.39 All such submissions are to be reviewed by the appropriate team and escalated appropriately for resolution on a regular basis

Duty to Stop (SLAM)

- 5.1.40 We all work in dynamic environments where the risks associated with our work activities and work environment require us to react to changing circumstances to ensure ours' and others' safety.
- 5.1.41 Align JV empower every individual working on the project with 'DUTY TO STOP WORK'
- 5.1.42 We need everyone's commitment to this programme for use to reduce / eliminate injuries to persons.
- 5.1.43 This commitment is not only be for the individual but also for colleague's and loved ones a home.
- 5.1.44 Our commitment is that Everyone one of us has the right to go home every day to our loved ones in the same condition as when we arrived. This includes both Physical and Mental Health.
- 5.1.45 Every person working on this project will be expected to apply the 'Duty to Stop Works' if they feel the task is unsafe to perform and could cause harm. You have my guarantee that we will support any individual who uses the Stop Work process and endeavour to make working practices safer.
- 5.1.46 As part of the Duty to Stop, we apply the SLAM technique:

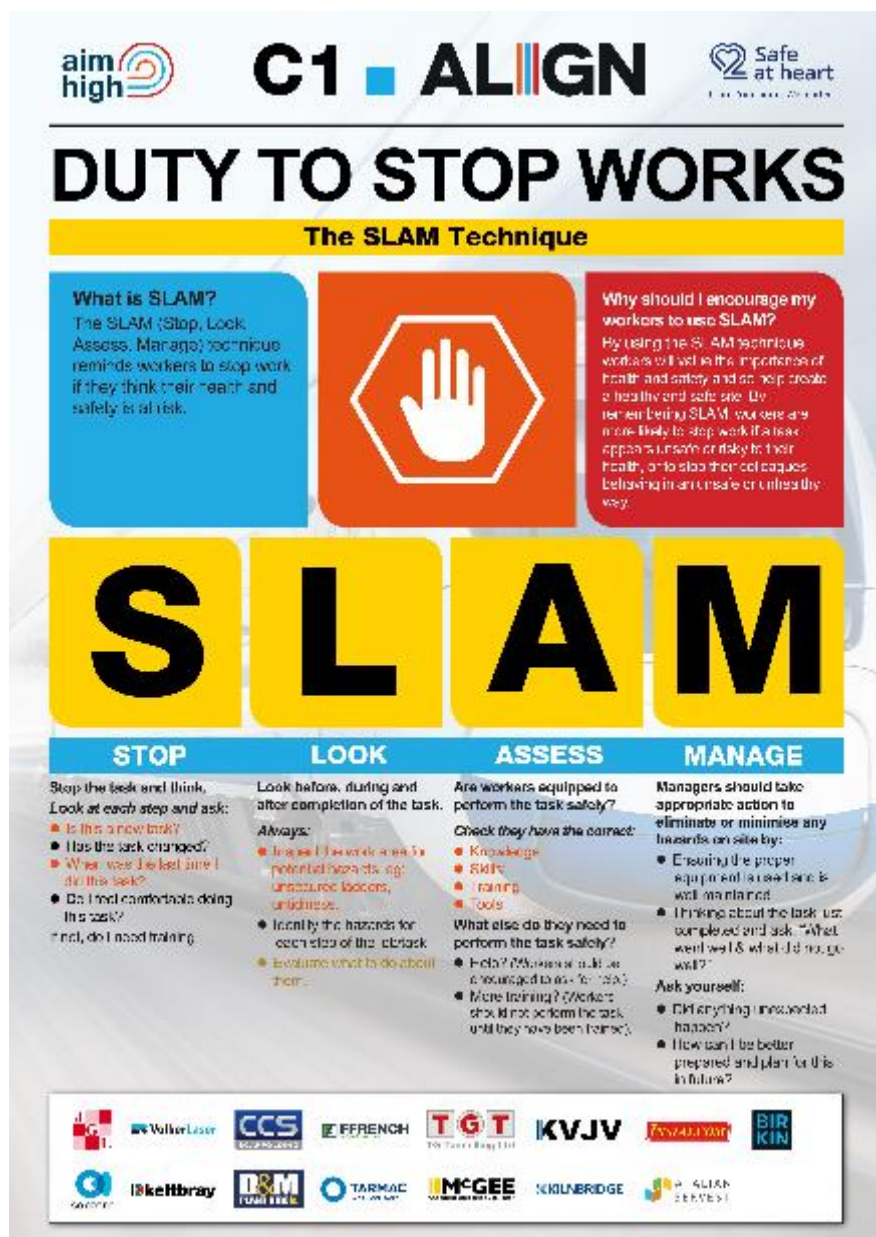

Suspension of Works

- 5.1.47 Where a more formal suspension of works is required, we will follow our suspension of works notice procedure. Document no. : 1MC05-ALJ-HS-PRO-C001-000011
- 5.1.48 ALIGN JV will follow a Suspension of Works Notification (SOWN) procedure to halt specific works where standards fall below the required or expected standard. ALIGN JV will notify HS2 of any SOWN. Where applicable ALIGN JV will work collaboratively with Contractors to correct and improve any breach or shortfall in requirements.

SLAM & IMPROVE Process

- 5.1.49 The SLAM (**Stop: Look: Assess: Manage**) and IMPROVE (**Intervene: Manage: Protect: Raise: Organise: Validate: Engage**) processes have been developed to assist teams in managing change.
- 5.1.50 SLAM was introduced with the aim of by giving all personnel the confidence to achieve our “Duty to Stop Work” when they see, feel something is wrong or changes arise to stop and take the appropriate steps to prevent incidents occurring. The Workforce can do so by raising their concerns “SLAM” on Aim High Observation platform after informing their Supervisor.
- 5.1.51 The introduction of IMPROVE within the process is to put a duty on the leadership and local management team to, not just stop an unforeseen or unsafe event/situation but to take the necessary steps to improve and prevent recurrence by managing the “Change”.
- 5.1.52 Part of the Validation process within IMPROVE is engaging the Package Manager and other Support team (Subject Matter Experts) members in the process to prevent the creation of further risks by ensuring that the proposed corrective and preventive actions by site team and black hat prior for the works to restart and making sure all people involved are aware of the situation and solution decided.
- 5.1.53 The document 1MC05-ALJ-HS-PRO-C001-000038.pptx describes how the process is completed using Dalux.
- 5.1.54 All levels of SLAM & IMPROVE will need to be recorded on DALUX and validated by supervision or management.
- 5.1.55 Identification of situation requiring work to be suspended raised verbally or on the AIM High Platform
- 5.1.56 Level 3: Simple SLAM can be dealt with locally by local supervision or management and recorded on DALUX as closed.
- 5.1.57 Level 2: Suspension of works leading to intervention and validation by management via the DALUX IMPROVE Process
- 5.1.58 Level 1: Suspension of works due to HIPO situation requiring senior management intervention and corrective action at management or subject matter expert

intervention. IMPROVE process to be followed and recorded on the DALUX system by management team

6 CDM Duty Holders

Client

Organisation	High Speed Two Limited
Representative	Mark Clapp
Address	6th Floor, Two Snow Hill, Birmingham, England, B4 6GA
Tel No	07717451491
Email	Mark.Clapp@hs2.org.uk

Principal Designer

Organisation	High Speed Two Limited
Representative	Gary Rogerson
Address	6th Floor, Two Snow Hill, Birmingham, England, B4 6GA
Tel No	07388 850967
Email	gary.rogerson@hs2.org.uk

Principal Contractor

Organisation	ALIGN JV
Representative	Coralie Peroux
Address	Align Compound, Chalfont Lane, WD3 9XN

Tel No	+44(0)7721 812599
Email	c.peroux@alignjv.com

Designers

Organisation	ALIGN JV
Representative	Coralie Peroux
Address	Align Compound, Chalfont Lane, WD3 9XN
Tel No	+44(0)7721 812599
Email	c.peroux@alignjv.com

Organisation	ALIGN-D
Representative	Jim Tinnion
Address	Align Compound, Chalfont Lane, WD3 9XN
Tel No	07790 938447
email	jim.tinnion@jacobs.com

7 Pre-construction Information

- 7.1.1 Pre-construction Information prepared by the Principal Designer, on behalf of the Client, will be formally transmitted to the relevant contractors by the ALIGN procurement team as part of invitations to tender and included in contracts. Confirmation that the contractor has received the most current pre-construction information will be made by the ALIGN Project Manager (or Construction Lead as appropriate) at on-site kick-off meetings and construction readiness reviews.
- 7.1.2 Pre-construction information for the project, known as the PCIP (Pre-construction Information Pack), has been prepared by the Principal Designer (HS2) and is available through our EDMS Business Collaborator (P1C-HS2-HS-REP-C001-000001).
- 7.1.3 Key Safety Hazards and Risks have been identified in the Pre-construction Information Pack. This information will be supplemented by the Health & Safety File information provided by the previous GI campaigns and other works carried out by others that may impact with Align's works and work sites, e.g. EWC, Non-contestable Utility works etc.
- 7.1.4 Pre-Construction Information includes aspects such as known ground contamination, existing assets, archaeology and ecology.
- 7.1.5 ALIGN-D, the design Joint Venture working on behalf of ALIGN, has developed the HS2 Design Risk Registers for each package of work within sector C1. The Design Risk Register for each relevant package, including the route-wide aspects, must be consulted when drawing up the specific Risk Assessments and Method Statements.
- 7.1.6 In addition, the Project H&S Risk Register, through [HORACE](#), in the form of HS2 Hazard Profile template.
- 7.1.7 The Design Risk Registers and Project H&S Risk Register are live documents that are regularly reviewed and updated following regular design review and H&S meetings. It is therefore important that the latest version of each document is consulted, and previously saved versions are not relied upon.
- 7.1.8 Historic information regarding utilities, buried and overhead services is included in the PCIP but must not be considered up to date. Current information on these utility services must be obtained through ALIGN's Utilities Manager, prior to the issue of any Permit to Dig system, Permit to work below over head utilites and Permit to Cross Buried utilites.

- 7.1.9 Security threats are constantly evolving and therefore ALIGN JV Security Manager must always be consulted when drawing up plans for compounds, work sites and making travel arrangements.
- 7.1.10 Construction compounds must follow the requirements laid out in CoCP.
- 7.1.11 The sector crosses and runs alongside a number of highway routes, watercourses, railways lines, third party assets and Areas of Outstanding Natural Beauty (AONB) and archaeological interest. Care must be taken at these locations to ensure compliance with regulations and procedures.
- 7.1.12 The HS2 project is very environmentally sensitive and there are numerous requirements laid down by the client and associated regulators to protect the environment during construction and use of the railway. These are laid out in the Works Information and managed by ALIGN's environmental team, Contractors must refer to the Projects Environmental Management Plan when planning works under their direction.

8 Management Arrangements

General Responsibilities

- 8.1.1 ALIGN JV overall responsibility for Occupational Health and Safety management as Principal Contractor in Sector C1 rests with the Project Director, supported by the Director Responsible for Health and Safety.
- 8.1.2 Each individual working on HS2 has a degree of responsibility relative to their position within the organisation. The Project Director will ensure that each person working on the project, including contractors' s personnel, are made aware of their individual responsibilities detailed under the [ALIGN Health and Safety Policy](#) and the [HS2 ethos of Safe@heart](#).
- 8.1.3 Health and Safety Policy Statement are referenced below.
- Health & Safety Policy 1MC05-ALJ-HS-POL-C001-000001
 - Drug, Alcohol & Substance Misuse Policy 1MC05-ALJ-HS-POL-C001-000002
 - Health and Wellbeing Policy 1MC05-ALJ-HS-POL-C001-000008
- 8.1.4 ALIGN JV will ensure that all front-line supervision and management are:
- Clear about their accountability and individual responsibility for OH&S

- Clear about the part human behaviour has in accident causation and what needs to be done to overcome this
- Clear that they have the right to stop work when they believe safety, health and wellbeing are compromised
- Clear that they never walk past an unsafe act or unsafe condition and that to do so is an unsafe act in itself
- Given skills in observation, intervention, and feedback
- Clear about their own leadership style and how that can influence the performance of a team
- Clear what are the acceptable and unacceptable behaviours
- Involved and engaged in the safety communication process and take an active role in Daily Briefings, Pre-job briefings, Tool Box Talks, Feedback Sessions, etc.;
- and
- Engaged in the reward and recognition that celebrates our successes.

8.1.5 All line management on site including those managers and supervisory personnel employed by Contractors – managers (SMSTS or NEBOSH Construction Certificate), supervisors /non-working foremen (SSSTS/IOSH Managing Safety minimum) and charge-hands/gangers (working foremen SSSTS /IOSH Managing Safety minimum qualification) – are key to ensuring that we achieve our Health & Safety Objectives on this project. Line management must be experienced and competent within their specific discipline and must demonstrate positive leadership qualities by:

- Demonstrating a personal commitment to health and safety matters by means of their attitude and behaviours.
- Challenging unsafe behaviours or conditions and personally taking action to ensure that they are corrected.
- Ensuring that anyone working for them is aware of the agreed safe system of work.
- Ensuring that they fully understand the emergency arrangements for the site and are prepared to take a proactive role in the case of an emergency.
- Supporting any health and safety initiatives that are implemented across the project, by both personal participation and promotion within their respective organisation.

8.1.6 ALIGN expects the personal commitment of our employees and those personnel from all designers, contractors, suppliers, and consultants working in sector C1: Every job will be conducted safely, no matter how important or urgent it is.

- Each of us has a personal responsibility for our own health and safety and for those around us.

- Putting people to work carries a specific responsibility and accountability for safety and health which will be visibly demonstrated.
- Each 'near miss' we learn from reduces the chance of harm next time.
- Each of us will spot, report and deal with hazards to help create a harm free workplace.

Roles and Responsibilities of Key Personnel

The Project Director

8.1.7 The Project Director shall be responsible for:

- The overall direction, coordination, implementation, execution, control, and completion of the Project, including the achievement of the Contract's KPIs.
- Leadership of the Safety, Health, and Wellbeing agenda through a consistent and energised approach.
- Leading the Quality agenda ensuring a "right first time" approach to the way we work.
- Leadership of the Project through establishing a capable leadership team who manage all aspects of the Project scope.
- Leadership of the Project by working effectively with the HS2 organisation to ensure that all stakeholders are effectively managed.
- Ensuring that ALIGN JV is effectively managed and an open and respectful relationship exists between all the organisations.
- Ensuring communication in the Project, with HS2 and the other contractors is consistent and relevant.
- Ensuring clarity between Project scope, budget, and overall deliverables.
- Ensuring that the Project is appropriately resourced.
- Maximising innovation, collaboration, and efficiency.

The Director of Health & Safety

8.1.8 The Director of Health & Safety shall monitor external developments and legislative requirements and translate these into Project Health and Safety Policy to ensure continued compliance and industry leadership and shall:

- Ensure these align with HS2, BYTP, VF and SRM policies, strategies, and requirements
- Develop, implement, and maintain the Health & Safety Management System in all respects to ensure risks to third parties / contractors / stakeholders are understood and controlled.

- Collaborate with other Contractors to ensure creation of coherent and integrated policies and systems that avoid unnecessary duplication and dissipation of effort and to have better achievements.
- Provide advice on interpretation and application of the Health & Safety Management System and include provision of relevant training, briefings, and information.
- Review the Scheme Design and issue comments to improve the health & safety during the site works.
- Manage the programme of audits of the Health & Safety Management Systems and ensure follow up and close out of actions where required.
- Co-ordinate and collate information required to produce scheduled Health & Safety reports and identify trends and early warnings of possible issues and recommend appropriate action.
- Be accountable for effectiveness of the team and develop and ensure capabilities to support the function of the business.
- Be responsible for creating and communicating the Safety, Health and Wellbeing and Contract Review vision and targets.
- Lead major incident /accident investigation.

The Design Director

8.1.9 The roles and responsibilities of those in the design teams are laid out in the Design Management Plan, so the responsibilities of other people can be found there (1MC05-ALJ-DS-PLN-C001-000001). The Design Director has the following responsibilities:

- Accountable for ensuring the engineering scheme design is specified, delivered, and maintained in compliance with HS2 requirements, including WI1100 Health and Safety and WI1150 Occupational Health.
- Principal point of contact regarding design for the project team with the ALIGN -D board, ALIGN, HS2 and stakeholders.
- Contributes to the development of ALIGN -D's strategy across all areas of the project, challenging assumptions, and decision-making as appropriate and providing analysis and guidance on all activities, plans, targets, and project drivers.
- Build, lead, manage and motivate the ALIGN -D project team. Take the lead role in directing all engineering activities and where appropriate prioritises activities in line with project needs.
- Develop and continually review the scheme design to ensure all project deliverables are aligned with HS2 requirements including the Health Hazard Evaluation and Mitigation Plans and information for the Health and Safety File.

Occupational Health / Clinical Lead

- 8.1.10 The Occupational Health lead is an integral part of the Health and Safety Team, supporting strategy development and implementation. Specific responsibilities include but are not limited to:
- Review health information and statistics from design reviews, fitness for work outcomes, health surveillance grouped data, Health Impact Frequency Rates, wellbeing outcomes etc. to assist in the identification of health needs and health assessment activity.
 - With the assistance of the wider occupational health team, create and update HMP, HHEMP and HRAs using all available health data such as; information on worker health outcomes and demographics of the workforce and community.
 - Creation of a monthly report on occupational health outcomes and information for Health and Safety Performance Indicators (HSPIs).
 - Support for Health Hazard Profile (HS2 Assurance) for each active sub-lot / asset
 - Participation in the Health Leadership Forum (HLF).
 - Manage service provision and ensure that outcomes are delivered in line with agreements and standards.

9 Management System arrangements

- 9.1.1 The ALIGN H&S Management System has been developed to demonstrate compliance with OHSAS 18001/ISO 45001.

Health and Safety advice

- 9.1.2 The Principal Contractor has a team of qualified safety, health, and wellbeing professionals, currently made up of the Director of Health & Safety and a team of Health & Safety Managers and Advisors, Occupational Health Manager and Advisors and hygienists. Confirmation of competence for the roles is assured by ALIGN JV requesting and holding copies of the individuals' relevant professional qualifications as part of the on-boarding process.
- 9.1.3 All contractors working on HS2 utilise experienced and qualified health and safety professionals to provide competent advice to their management and workforce. Contractors shall be informed by ALIGN JV where it is expected that such personnel will be required to be engaged within the project on a full-time basis. Contractor's management of safety, health and wellbeing and their resources and contact details shall be described in Contractors Health and Safety Management Plans.

- 9.1.4 Contractors (together with their sub-contractors) must agree with ALIGN, how many contractors and health and safety professionals are required on site, taking into consideration the nature of the work and the number of separate work faces.

Assurance activities

Principal Contractor's Monitoring

- 9.1.5 Individual elements of the ALIGN JV OH&S Management System implemented on the project, e.g., plans, procedures, and policies, will be reviewed periodically to ensure that it remains relevant and appropriate.
- 9.1.6 A schedule of planned worksite inspections is developed to monitor OH&S performance in accordance with ALIGN Contract Quality Plan (1MC05-ALJ-QY-PLN-C001-000001). The schedule will include all health and safety inspections, and safety engagement walks carried out by the Principal Contractor's site team including Construction, Site Operations and the Health and Safety Team.
- The frequency of worksite inspections will be in line with the hours worked on the site and will increase with the risk level of activities on the site. Quality, Environmental and security assurance activities are described in the respective Management Plan.
- 9.1.7 As a minimum weekly site team Health, Safety and Environmental inspections will take place by an appointed member of the site delivery team. In addition to a monthly Health and Safety review by a member of the Health and Safety Team. Inspections and monitoring will be recorded via DALUX with tasks / observations / NCR recorded and allocated to the relevant responsible personnel.
- 9.1.8 The schedule will be communicated to all persons required to undertake an inspection. The Project Director and Director of Health and Safety will ensure that performance against the schedule is continually monitored for compliance and will be regularly reviewed at meetings.
- 9.1.9 The ALIGN JV Construction Team will carry out planned OH&S workplace inspections at locations and a frequency according to the OH&S risk associated with construction activities and in response to any negative trends identified from the analysis of unsafe acts and conditions, incidents, safety inspections and safety engagement tours and construction surveillances. The Director of Health & Safety will maintain a schedule of planned inspections and monitor those inspections are being carried out to plan. The frequency of inspections will be continuously reviewed by the Director

of Health & Safety in line with the risk profile and the results of other monitoring activities both by the Principal Contractor and other Contractors.

- 9.1.10 Copies of OH&S audits carried out on the project by external / client bodies shall be reviewed and maintained by the Principal Contractor's Health & Safety Team.
- 9.1.11 Senior ALIGN & HS2 directors and managers based off-site will visit site monthly and undertake formal Executive Committee (ExCo) Leadership Engagement Tours. They will be accompanied by the most senior member of the Principal Contractor's team on site. Following the tour, the visiting Senior Manager will carry out a de-brief with ALIGN site management to discuss the observations and agree any corrective actions required. A written report will be made of the visit to ensure any actions are assigned and closed out.
- 9.1.12 Actions identified from inspections/tours will be addressed at the time of inspection/tour where possible and added to the project lessons learnt and incident management database, prioritised and regularly monitored to ensure they are closed out. The Site Management Team will develop improvement plans for any areas that require longer term improvements to the systems in use, with the support of the Health and Safety Team.

Contractors' Monitoring

- 9.1.13 Contractors' Managers, Supervisors (working and non-working foremen) and Health and Safety Advisors are responsible for ensuring each day that all work areas are safe before, during and after work activities.
- 9.1.14 Formal health and safety inspections - led by their Managers/Supervisors and supported by their health and safety professionals - will be carried out by all Contractors on a weekly basis as a minimum.

Health and Safety Performance Index

- 9.1.15 ALIGN Director for Health and Safety will report to HS2 against certain measures for calculation of a Health and Safety Performance Index consisting of a Safety Performance Index and Health Performance Index upon such information being made available to ALIGN. All contractors will cooperate with ALIGN in the measurement of health and safety performance as and when reasonably requested.

Statistical Reporting

- 9.1.16 General requirements for statistical reporting are given in HS2's "Supply Chain Health and Safety Approach". ALIGN will measure both leading and lagging OH&S

Key Performance Indicators (KPIs). HS2 will also utilise data from the Online Incident Reporting System (OIRS). (HORACE) to generate Enterprise Safety Performance Indicators (ESPI).

9.1.17 The key H&S statistical data that will be collected is as below:

Fatality
Specified (Major)
>7 (3) Days
RIDDOR Injuries to non-workers (Public)
Total RIDDOR Injuries
Minor Injuries (No Lost-time)
Minor Injuries (Lost-time)
Minor Injuries (All)
Lost time (Days)
All Injuries
Hours Worked
Dangerous Occurrences
Incidents (excluding Service Strikes)
Service Strikes
Near Misses / Close Calls

9.1.18 ALIGN will produce a monthly, annual, and rolling 12-month report on the following statistics:

Accident Frequency Rate (AFR)
12 Month Rolling AFR
Accident Incidence Rate (AIR)
Minor Injury Frequency Rate (IFR)
All Reported Injury Rate (ARI)
All Lost Time Injuries Accident Frequency Rate (LTI AFR) ¹
12 Month Rolling Service Strike Rate (SSR)
Near Miss Frequency (NMF)

Review of the Safety, Health, and Wellbeing Management (Construction Phase) Plan

9.1.19 The Project Director will ensure that this Safety, Health, and Wellbeing Management (Construction Phase) Plan is reviewed and updated on a regular basis to ensure that:

- The objectives and requirements of the Construction Phase Plan are still valid and are being met.

- Future construction activities are reviewed and any necessary amendments to ALIGN JV OH&S management processes or standards are put in place before the relevant work begins.
- OH&S management processes are reviewed to ensure continuing suitability and effectiveness.
- This review will be carried out at least annually or when a significant change is identified.

Communication and Consultation

- 9.1.20 It is recognised that effective, continuous communication is a key element of an effective safety culture, ensuring that everyone involved with the HS2 project is kept informed.
- 9.1.21 A regular “Safety Matters” communication will be cascaded through all teams.
- 9.1.22 Throughout the duration of the project, ALIGN JV will ensure there is regular communication with the workforce, providing information about the progress of the construction works, milestones achieved, upcoming challenges, safety incidents and information about local activities. This information will be shared via Safety Matters newsletters, Team Briefs led by senior management, Black Hat forums, poster campaigns and digital media. Site teams will be briefed regularly by site management and will also take part in safety stand-downs arranged at times around key construction dates, such as the start of a new element of the works, returning from Christmas break. In addition, all personnel will take part in a half yearly Safety Day as part of ALIGN JV Aim High Cultural Development programme.
- 9.1.23 All personnel will be required to attend an updated On-Boarding presentation after eighteen months of continuous working on the project. On-Boarding training will be regularly updated to reflect key activities and risks encountered during the construction of the project.
- 9.1.24 Safety climate surveys will be carried out at least annually with results of such surveys studied and incorporated into improvements and management systems as required.
- 9.1.25 The ALIGN communications team will be responsible for all external communications relating to the ALIGN JV project with the local community and external stakeholders.
- 9.1.26 Any interactions with the media must be directed through the communications team to HS2.

- 9.1.27 General requirements for Contractor workforce consultation are given in HS2's "Supply Chain Health and Safety Approach".

Regular Co-ordination Meetings

- 9.1.28 Coordination meetings will be held regularly with all Contractors on site to ensure that there is a clear understanding of forthcoming scheduled work activities and areas where there will be possible interface issues such as clashes and adjacency hazards. These meetings include:

- Daily coordination meeting (including Black Hat Meetings)
- Weekly coordination meetings
- Weekly progress meeting
- Weekly integration meeting

- 9.1.29 The meetings will be chaired by a representative of the ALIGN JV Construction Team, and will include site supervision, Contractors management and health and safety advisors.

Contract/Progress Meetings

- 9.1.30 ALIGN will hold scheduled contract/progress meetings with each Contractor which will include an in depth discussion of health and safety performance, any current issues and a review of progress in closing out any health and safety-related actions. These meetings will be attended by the management representatives of the Principal Contractor and Contractor, and the Principal Contractor's and the Contractor's Health and Safety Advisers. Contractual communication between ALIGN and its contractors will be through CEMAR.

Safety, Health and Wellbeing Leadership Team (SHWeLT)

- 9.1.31 The C1 SHWeLT is a high-level meeting where Safety, Health and Wellbeing strategy and significant matters for Sector C1 are discussed in the C1 senior leadership team attended by ALIGN, HS2 The meeting is the opportunity to review:

- Develop and feedback on ALIGN policies and strategies in
- HS2's 7 Focus Areas of safety
- ALIGN's Aim High and Wellbeing Plans and Strategy
- HS2's Health Measures
- Security – Cyber and physical
- Highlight C1 activity outputs from related working groups with HS2
- Share best practice and lessons learned
- Review KPIs / HSPIs

- Promote communication between key stakeholders and disciplines – high-level knowledge share.

9.1.32 A series of localised SHWElts and working groups are organised to share information up and down the project management teams.

Tool Box Talks

9.1.33 In addition to daily workforce briefings, all Contractors working on site are expected to carry out regular toolbox talks (at least weekly) proactively with their work force to provide 'refresher training' on topics that are relevant to their current / future work activities.

9.1.34 In addition, contractors will deliver specific briefings created by the Principal Contractor to highlight issues that have been identified during site inspections or audits; or learning that has been established from the investigation of recent incidents.

9.1.35 Records of attendance and the information communicated will be retained by the Contractor organisation delivering the talks and issued to the ALIGN JV Health and Safety Team upon a weekly basis.

Non-English-Speaking Workers

9.1.36 All Contractors working on the project must recognise the challenge that will be faced when communicating with workers for whom English is not their first language. This is particularly important when ensuring that safety-related instructions are being transmitted.

9.1.37 Where team members who do not have English as their first language, there shall always be a supervisor present with an individual, team or gang that can give instruction and translate where appropriate. The ratio of team members who do not have English as their first language to a supervisor with the ability to effectively communicate in English (verbal/spoken) shall never exceed 4:1.

Exchange of Design Information/Design Changes

9.1.38 Exchanges of design information will be carried out as part of the project design review meetings and be formally recorded. All design changes will be handled according to project procedures. Each time the construction method is changed, the risk assessment must be reviewed along with the method statement. Any changes made to the method statement and/or risk assessment must then be briefed to all staff involved in the activity and others potentially affected by the changes.

- 9.1.39 Refer to Sector C1, Pre-Construction Information Package (PCIP) Register P1C-HS2-HS-REG-C001-000001 The design risk register shall be regularly reviewed by the designers to identify risks which may need to be elevated into the strategic or project risk registers and to monitor progress with mitigating design risks previously identified.
- 9.1.40 The provision of design information and the design risk register is detailed in the ALIGN-D Design Management Plan (1MC05-ALJ-DS-PLN-C001-000001).
- 9.1.41 Specific information such as residual risk information will be included on the construction drawings in SHE Boxes and/or in the BIM model representation.
- 9.1.42 Refer to the method statement template 1MC05-ALJ-HS-TEM-C001-000005.

Selection and Control of Contractors and Suppliers

It is vital that the supply chain is fully engaged in with ALIGN JV Aim High expectations in order to achieve our aim of securing a safe working environment where everyone has the right to return home free from injury and ill health effects every day. In particular, ALIGN JV will ensure that:

- The occupational health and safety performance of suppliers and Contractors is key in the selection process.
 - The competence of suppliers and contractors (particularly in relation to CDM) is key in the selection process.
 - That the highest standards of occupational health and safety are specified in the procurement process.
 - Selected suppliers and contractors are engaged early in the OH&S programme.
- 9.1.43 Contractor procurement will be carried out by the procurement team following ALIGN procedures. A health and safety questionnaire is issued to all potential Contractors. Completed questionnaires will be evaluated by the ALIGN Health & Safety Team, to ensure that Contractors meet the minimum OH&S competence requirements prior to being awarded any contract on the project in accordance with the ALIGN procedure.
- 9.1.44 Contractors must have arrangements in place that are satisfactory to ALIGN to ensure that any further subcontractors used are equally competent.
- 9.1.45 Contractor / Supply Chain on Site Kick-Off Meeting and Readiness Review: A contractor / Supply Chain On Site Kick-Off meeting will be held prior to the

commencement of the construction activities of each Contractor company or prior to any significant change in risks in accordance with ALIGN Procedures.

- 9.1.46 Refer to the Pre-start Questionnaire - Sub-Contract Pre-Start Meeting Agenda (template) 1MC05-ALJ-CL-FRM-C001-000002.docx
- 9.1.47 Contractor Review of the Construction Phase Plan: Each contractor appointed to undertake construction work on the project will be provided with a copy of the latest revision of this Construction Phase Plan prior to the On Site Kick-Off Meeting.
- 9.1.48 Within 7 days of receipt, the Contractor's Senior Representative will review this Construction Phase Plan and shall inform the Principal Contractor if any of the Contractor's work activities create key health and safety risks that have not been adequately covered in this plan.
- 9.1.49 Contractor's Health and Safety Management Plan: Each Contractor is required to develop their own Health and Safety Management Plan that states how they intend to meet within their organisation and their sub-Contractors the requirements set out in this Construction Phase (Health and Safety) Plan; which nominates their safety-related appointments; and sets out the responsibilities of their site organisation. These plans will be reviewed and accepted by ALIGN as Principal Contractor before Contractors may commence work on site.
- 9.1.50 Management of delivery: Progress meetings will be held weekly with representatives of ALIGN JV management team and Contractor's management team in attendance. An agenda for these meetings will include an assessment of the project's progress against the Accepted Programme; Technical issues; Health & Safety; Environment; Security etc.
- 9.1.51 Progress of all activities will be part of the PMU (Project Manager's Update) Report each month and will be reported on in the same way as the rest of contract 1MC05. This will include commercial and other aspects.
- 9.1.52 Lessons learned: The results of investigations into accidents, high potential incidents or any other significant experience gained on the project will be shared, initially with the project team and HS2, through HSSE Lessons Learned posters or Alerts, depending on the severity and significance of the information. Following discussion with HS2 the lessons will then be posted on the Horace database and shared with the other HS2 Contractors, Parent Companies and the wider industry if relevant. All ALIGN lessons learned will be held in a database for ease of reference.

Co-operation and Coordination

- 9.1.53 ALIGN JV will liaise with HS2 Ltd, through the Project Manager in a timely manner, regarding any significant health and safety issues which arise during the design and construction stages, which may have an impact on the project or HS2 Ltd.'s activities.
- 9.1.54 ALIGN will liaise with the Principal Designer through the Project Manager on design carried out during Stage 1 and throughout the construction phases. This includes design by specialist contractors, and its implication on the CPP. Weekly Coordination meetings include an agenda item for any issue that needs to be escalated to the Principal Designer (PD) and, equally, for HS2 as the PD to communicate to ALIGN as the Principal Contractor.
- 9.1.55 ALIGN JV activities will have interfaces with several significant other parties including:
- HS2 Ltd as designers of the railway systems
 - HS2 Ltd contract areas S2 & C2 (the shared boundaries)
 - Other Principal Main Works Contractors (Eiffage Kier (EKFB) and Skanska Costain Strabag (SCS)), where ALIGN will take the lead in managing the interfaces
 - Enabling Works Contractor (EWC) (Fusion JV)
 - National Highways and Connect Plus
 - Network Rail and Chiltern Railways
 - Utility providers
 - Canal and Rivers Trust and Inland Waterways Association
 - Members of the public, Private property owners (and/or tenants)
 - Local councils and highway authorities
 - Parish councils
 - Natural England
 - Environment Agency
 - The emergency services
 - Hillingdon Outdoor Activities Centre (HOAC)
 - Affinity Water
- 9.1.56 Senior ALIGN JV representatives and suitable others are to attend HS2 Ltd forums and meetings relating to H&S. These meetings include:
- HS2 Strategic SHWeLT (Align JV Project Director)
 - HS2 Civils Operational SHWeLT (Align JV Operational / Construction Director)
 - C1 SHWeLT (Align IPT)
 - HS2 H&S forum
 - Health Leadership Forum

Undertakings and Assurances

- 9.1.57 It is within the scope of the ALIGN JV to discharge all relevant Undertakings and Assurances listed within the Commitments Requirements Specification and to ensure that Protective Provisions Agreements in Schedule 33 of the Act are complied with during the development of design and construction.
- 9.1.58 The Commitments Compliance Plan 1MC05-ALJ-SE-PLN-C001-000002 describes the governance procedures and the processes therein, to ensure we meet the commitments within the contract.
- 9.1.59 The strategy for compliance for statutory consents is covered in the Consents Management Plan. The plan for compliance with land access and possession is covered in the Land Access Land Possession Strategy. The processes covering compliance with Environmental Minimum Requirements and the Environmental Statement are detailed in the Design Management and Technical Assurance Plan.
- 9.1.60 In the case that a physical constraint on site is stated by the U&A, it is important that operatives on site are fully aware of the constraint and Methods are planned accordingly. In most cases, this is dealt with by including details of the constraint onto Site Establishment Plans so that the constraint is clearly identified. Supplementary to that, necessary activities to guarantee the constraint is not breached, are included in the site RAMS documentation. These are communicated to the site teams via normal site procedure including 'toolbox talks'.
- 9.1.61 Assurance is carried out via weekly progress meetings and via physical auditing by the ALIGN Requirements Engineer.

Competence & Fitness to work

- 9.1.62 General requirements for competency of Contractors and workers are given in the BUILDUK standard on training which reflects the Construction Leadership Council (CLC) approved construction card schemes.
- 9.1.63 ALIGN fully acknowledges its duties under CDM and the duty placed upon Contractors to ensure any individual they employ or appoint to work on a construction site has the skills, knowledge, training, and experience to carry out the work they will be employed to do in a way that secures the health and safety of themselves and others.

- 9.1.64 A training and competence management system has been procured and developed to ensure we know the competencies of all employees and to identify any gaps in skills, knowledge, experience, and training that need to be filled in order for ALIGN to undertake its responsibilities. Training requirements will be fulfilled by either the JV parent companies, HS2 or by ALIGN, depending on the nature of the requirement.
- 9.1.65 The Biosite Knowledge system records competence against an Align specified matrix of requirements and is linked to a biometric access control system to work areas and zones. The data within the system enables access to secured work zones based upon competence.
- 9.1.66 The competencies required for each job role will be established and agreed by the ALIGN Executive Committee (EXCO) and reviewed as necessary against industry and Employer requirements. The complete set of competencies will be established and included in the Biosite Knowledge system.
- 9.1.67 HS2's Safe at heart ethos and values is endorsed entirely by ALIGN. The Align induction process contains the HS2 collateral given to deliver the HS2 Safe at Heart message to be rolled out to all ALIGN employees, supply chain personnel and visitors to Align Work locations.

SKATE

- 9.1.68 The project is dedicated to ensuring Align achieve their strategic objectives and value of 'Everyone home safe and well every day'. Together Brain Candy and Align have built a cutting-edge process and are dedicated to creating a safe working environment for all, reducing potential risk and optimising operational performance.
- 9.1.69 The Brain Candy knowledge builder assessment is unique in that it uses everyday scenarios to assess how an individual would deal with a situation and how certain they are that this would be the right course of action. The results then show a heat map of what an individual understands, but more importantly mis-understands. These results give immediate feedback and suggest learning or training interventions, so whatever the outcome, the employee is armed with the right information and never accesses a site unless they have met the criteria set.
- 9.1.70 The current project is aimed at Plant Operative, Supervisors, and lifting personnel across a range of sites within the Align JV Project and is supported by a joint team from Align & Brain Candy.

Competency Card Schemes and Qualifications

- 9.1.71 The minimum standard for competency for site personnel carrying out construction related occupations is a valid CSCS (Construction Skills Certification Scheme) card or a Partner Card Scheme containing the CSCS logo. Where appropriate, such as for plant operators and personnel undertaking tunnelling aspects of the work, National Vocational Qualifications (NVQ) will be required. There will also be specific training requirements for activities below ground and for those working over water.
- 9.1.72 Where personnel are engaged on non-construction activities and for those roles where there is not a recognised competency scheme ALIGN JV will identify the accepted level of training / competency evidence required.
- 9.1.73 For Partner Scheme information please refer to <https://builduk.org/wp-content/uploads/2020/11/CLC-Industry-Card-Schemes-Recommendation.pdf>
- 9.1.74 The card or qualifications held by individuals must be reflective of the task/works to which they are appointed to undertake.
- 9.1.75 Where security personnel are undertaking general security guard duties, they will hold a valid Security Industry Authority (SIA) card as a minimum which will be presented at the ALIGN on boarding process and display by the individual whilst at work.
- 9.1.76 Security guards with additional duties for example Traffic Marshal/Traffic Management duties will also possess a valid Site Access Traffic Marshal certificate of achievement (CLOCS)
- 9.1.77 In addition to individuals holding a valid CSCS or a Partner Card Scheme containing the CSCS logo, individuals may need to hold supplementary training evidence to operate specific machinery, plant, and equipment. For example, a steel erector required to use a MEWP would hold a valid CSCS card in addition to an IPAF card.
- 9.1.78 In accordance with the HS2 Supply Chain Health and Safety Approach the accepted standard of training for mobile plant operators is CPCS (BLUE) or NPORS (with CSCS hologram) or a Partner Card Scheme containing the CSCS logo. In relation to vehicle banksman training, the CLOCS Vehicle Marshal qualification is the recognised minimum standard of training required for vehicle marshalling upon site.
- 9.1.79 Any plant/equipment operator in possession of a Red CPCS Card (Trained Operative) will be subject to the contractor appointing a named competent supervisor to monitor works under the direction of the said operator.

- 9.1.80 In addition, evidence that the trade related NVQ has commenced will be provided by the contractor prior to Red CPCS card holders being permitted to operate any item of plant or equipment upon any ALIGN site/premises. This is in addition to the completion of the employers' competence statement which forms part of the ALIGN induction process.
- 9.1.81 In relation to Vehicle Banksman training, the CLOCS Site Access Traffic Marshal qualification is the recognised minimum standard of training required for vehicle marshalling upon site, and the use of STOP WORKS BOARDS between the public highway and the construction site entrance.
- 9.1.82 Operatives/Supervisors engaged in the installation, removal and maintenance of traffic management equipment upon a highway, shall have successfully completed the appropriate LANTRA module for the works to which they are undertaking. An operative holding a trainee card will be fully supervised by a competent member of the team holding a fully endorsed LANTRA qualification. Operatives/Supervisors engaged to undertake street works shall have successfully completed the appropriate New Roads and Street Works (NRSWA) module - appropriate to the works they are undertaking.
- 9.1.83 First Aiders - each contractor will provide sufficient trained first aid personnel for works under their direction. For construction related first aiders the required level of training will be the 3 Day First Aid at Work qualification. For Higher Risk Areas a programme to deliver FREC3 trained personnel across the project has been instigated.
- 9.1.84 All Contractors coming to site will map their roles to the Competence and Qualifications framework that will be used to verify that persons working on site are appropriately qualified and competent. Completion of an agreed matrix is a pre-requisite of mobilisation to site.

Working over or near water, minimum training standards

- 9.1.85 ALIGN will ensure the following minimum standards of training for personnel working on, adjacent or above water where full collective protection cannot be provided and maintained or works that are within 3m of the water course:
- 9.1.86 ALIGN acknowledge the supply chain may have higher standards than the above, and in such instances the higher standard will be accepted by prior agreement with ALIGN Health and Safety Team.

Tunnel Personnel

- 9.1.87 A Minimum of the City and Guilds 6151 level 2 qualification will be required for tunnel entry and tunnelling activities and this must be supplemented by the CITB and British Tunnelling Society (BTS) endorsed Tunnel Safety Training Scheme (TSTS) tunnelling qualification. Such qualifications will be required to be updated and maintained in line scheme requirements and certification.

Confined Space work personnel

- 9.1.88 In all cases, the confined space qualifications will be in line with the framework of City and Guilds 6150 and to the appropriate risk and competence level.

Asbestos Training

- 9.1.89 Personnel required to undertake work or surveys where there is a foreseeable risk of ACMs being encountered must hold a valid UKATA approved Asbestos Awareness certificate which is renewed at periods not exceeding 12 months

On boarding / Induction

- 9.1.90 Refer to ALIGN Induction Procedure (1MC05-ALJ-HS-PRO-C001-000003) for full details and requirements relating types of induction.
- 9.1.91 The on boarding and induction process consists of three principles parts
- Online – including safe at heart and capturing competence and medical information
 - On Boarding – A project values based session, introducing those joining the project to our expectations, including EDI, environment, and community engagement, as well as physical and mental health, and worker and public safety.
 - Work Area Induction (Game Board Induction) - Each work area will provide a location specific induction utilising the game board induction. Records of attendance will be provided to the on boarding team
- 9.1.92 Completion of the Site Workers' Induction is mandatory to obtain full and unescorted access to the Project and this will be recorded by the ALIGN On-Boarding Team. The Worker's Code of Conduct is covered during the Project Introduction where inductees agree to this showing their commitment to the ALIGN values and expectations whilst working in the local community.
- 9.1.93 Contractors are responsible for providing all their workforce including sub-contractors with a company induction and site orientation. This ensures that individuals understand the specific rules applicable to the work activities they will

carry out and to reinforce the particular requirements and safety standards of ALIGN, including emergency arrangements. Contractors shall submit copies of their inductions/orientations to ALIGN for review and shall provide records of attendance to ALIGN upon a weekly basis.

- 9.1.94 As part of the ALIGN pre-registration process, 72 Hours in advance of persons attending the ALIGN site induction the following information will be provided for each individual requiring an ALIGN site induction:
- Completed Employee/Employer declaration form
 - Completed Pre placement health questionnaire, with hard copy to be brought to the site induction by each individual
 - Valid skill card
 - Valid safety critical medical if applicable, with at least six months to recorded expiry date
- 9.1.95 Upon the above information being received and reviewed by ALIGN JV, confirmation of induction attendance will be confirmed to the employer along with an Induction date and time slot.
- 9.1.96 **Worker** - A worker is someone who will be carrying out tasks that require a Risk Assessment, Permit to Work or a Work Authorisation (including Generic RAMS's).
- 9.1.97 A worker can be working anywhere on site and may not necessarily be carrying out construction' work or 'manual' labour.
- 9.1.98 **Visitors Non-Working** - Those carrying out tasks that do not require a Risk Assessment, Permit to Work Order or a Work Authorisation (including Generic RAMS)
- 9.1.99 **Delivery Driver/Service Engineer** - Is someone who is delivering/ collecting product/material/goods on a HGV over 3.5tonnes to the project or undertaking plant and equipment maintenance.

Fit for Role Medical

- 9.1.100 Fit for role Medicals must be arranged by the employer and recorded prior specified roles being undertaken. Full details are contained in the Health Management Plan 1MC05-ALJ-HS-PLN-C001-000003).

Control of Persons Entering the Site

- 9.1.101 Biometric access systems will be utilised in all ALIGN JV construction areas.

- 9.1.102 All people (including delivery drivers and Visitors) display a pass (as a means of identity) or have such identification readily available for purposes of identification. ALIGN will refuse entry to or remove from the Working Areas anyone who refuses to supply a means of identity. Access to the site may be withdrawn at any time. For further information on security arrangements for the project refer to the Project Security Plan (IMC05-ALJ-SC0PLN-C001_000003) Access to Working Areas
- 9.1.103 All working areas will have a controlled access point where employees and Visitors pass through and sign in (manual or electronic) on entry. All people attending the Working Areas (for example a delivery driver) are advised of the relevant Working Area risks, control measures and ALIGN's Working Area rules in the form of The Delivery Drivers Briefing issued to them.
- 9.1.104 No one under the age of 16 is permitted in Working Areas. In special circumstances (for example an organised visit from a local school) where people of 16 years or under are admitted to the Working Areas (as Visitors only), ALIGN will carry out a Risk Assessment documenting the controls necessary to safeguard their safety, health and wellbeing. This also applies to passengers in vehicles making delivery to or visiting the Working Area for any other reasons.

Welfare Facilities

- 9.1.105 General requirements for Contractor-provided welfare facilities are given in HS2's "Supply Chain Health and Safety Approach" and in Schedule 2 of the CDM Regulations.
- 9.1.106 Contractors must ensure that there are adequate welfare facilities i.e., canteens, rest facilities, changing and drying rooms, washing and toilet facilities and a supply of fresh drinking water available to their workforce and any subcontractors. The minimum requirement for the welfare should be as per Workplace (Health, Safety and Welfare) Regulations 1992 and associated ACoP.
- 9.1.107 Where contractors provide welfare facilities as part of their contract the proposed facilities will be agreed in advance with ALIGN Management to ensure a satisfactory standard of provisions are provided. Separate facilities will be provided for male and female personnel at all work locations.
- 9.1.108 Sufficient, toilets, showers, changing rooms, lockers, canteen and rest areas will be provided across the project. Details can be found in the specific Construction Phase Plan for each site or work area.

- 9.1.109 As a minimum it must meet the requirements laid out in section 4.4 of the Supply Chain Health and Safety Approach, ALIGN guidance note “Welfare Facilities and Site Set-up” and will be agreed with HS2 in advance of mobilisation.
- 9.1.110 Contractors must ensure that their facilities are maintained to a high standard of cleanliness and repair and the consumable items are replenished at least daily or when required. Records of inspections will be maintained.
- 9.1.111 Particular attention will be paid to ensure that there are properly constructed footpaths, steps, and staircases with non-slip treads and handrails to allow safe access to these buildings. The exposed edges of all steps will be highlighted to prevent trips.
- 9.1.112 All persons must use the welfare facilities provided to change. Changing in car parks is not permitted.

Notification, Reporting and Investigation of Incidents

- 9.1.113 The terms “incident, accident and near-miss” are as defined in OHSAS 18001. Refer to the C1 Align Emergency Response and incident management Plan [1MC05-ALJ-HS-PLN-C001-000041]
- 9.1.114 All work-related incidents (i.e., accidents resulting in personal injury or ill health, or near-misses with the potential for personal injury or ill health) must be formally reported to HS2 by the responsible ALIGN manager by completing an Incident Report in HORACE (HS2’s continuous improvement and incident management tool).
- 9.1.115 Each incident shall also be reviewed to determine if the actual or potential consequence meets the criteria for a Reportable Incident under the RIDDOR Regulations.
- 9.1.116 Onward internal notifications to ALIGN Management and externally to others will be made in accordance with ALIGN’s procedure. Incidents with significant actual or potential consequences will also be notified to the JV partner companies via their own chain of reporting.
- 9.1.117 In addition to its own procedures for reporting any accident to an employee or member of the public, Contractors shall provide a copy of statutory notification Form No 2508, if applicable, and a copy of its investigation report, to ALIGN’s Health and Safety Department. All specified injuries, occupational diseases and dangerous

occurrences as defined by RIDDOR (Reporting of Injuries, Disease and Dangerous Occurrences Regulations, 2013) shall be reported immediately to Align JV.

- 9.1.118 Note: Any RIDDOR notifications to the Health and Safety Executive will be coordinated by ALIGN's Health & Safety team, with submission of the Statutory Notification (F2508) being made by the relevant employer following consultation with the ALIGN prior to any such submission.

Confidential Reporting of Serious Concerns – whistle Blowing

- 9.1.119 Staff should normally initially raise concerns through their Line Supervisor / Manager or direct report if working on a sub-contract basis. If the Health & Safety issue is serious and likely to place staff in imminent danger they shall IMMEDIATELY stop work until the issue is resolved. Raising concerns whether minor or major, can be done without fear of victimisation or detriment. Concerns may be raised either verbally or in writing. If it is felt that the matter cannot be raised with the immediate Line Supervisor / Manager the concerns can be escalated through the Management Team and where necessary, direct to the Project Manager.

'Speak Up'

- 9.1.120 We want to create an ethical culture where everyone feels comfortable in raising concerns. Whistleblowing is speaking up about malpractice (things that are wrong).

How to report a concern:

- To your line manager or HR
- Directly to the Ethics & Compliance Team, at ethics-compliance@alignjv.com
- Via our independent provider, Safecall – 0800 915 1571.

- 9.1.121 Posters and QR codes are located around the site and on digital notice boards.

Enforcement Notices

- 9.1.122 Generic requirements for Contractors to report any enforcement notices are given in HS2's "Supply Chain Health and Safety Approach".
- 9.1.123 Contractors shall inform ALIGN of any regulatory interest that takes place during their works at HS2 or elsewhere.

Risk Assessments and Method Statements

- 9.1.124 Preparation, Review and Acceptance of Risk Assessments & Method Statements (RAMS)
- 9.1.125 The aim of the ALIGN assessment system is to break the work activity down into systematic steps from start to completion, at each step identifying the hazards and where possible eliminating the hazards as far as reasonably practicable. Where elimination is not practicable the controls to be used must be identified. The use of PPE is only to be considered as a last resort, as indicated in the hierarchy of controls.
- 9.1.126 See ALIGN Procedure "Risk Assessment Procedure - 1MC05-ALJ-HS-PRO-C001-000005".

RAMS for Construction Activities

- 9.1.127 All Contractors shall prepare and submit to the Principal Contractor prior to their On-Site Kick-Off Meeting a list of the risk assessments and method statements (RAMS) that they will prepare for their initial works to be carried out on site. This information shall continue to be provided to the Principal Contractor's Site Team during regular progress meetings and used by the Principal Contractor to maintain a register of all RAMS on site.
- 9.1.128 All contractors shall ensure that Pre-Construction information, including residual risks from the Designer Risk Register is incorporated into the health and safety plan and in the RAMS documents.
- 9.1.129 Risk assessments and method statements shall be prepared and submitted to the Principal Contractor at least 14 days (or as stated in the contract) prior to the commencement of all surveys, construction, commissioning and maintenance tasks involving physical work on site.
- 9.1.130 All RAMS shall be reviewed by the Contractor's Health and Safety Professional prior to submission to the Principal Contractor. As part of this review, the Contractor's Health and Safety Professional will identify any safety critical activities/high risks that require hold points be included in the method statement and within the Inspection and Test Plan, requiring notification by the Contractor to the Principal Contractor before proceeding.
- 9.1.131 All RAMS shall be prepared, reviewed and accepted in accordance with ALIGN Project Work Instruction "Procedure for Method Statements" In summary, this work instruction requires the following:

- Both Contractors and ALIGN will prepare RAMS for all their surveys, construction, commissioning or maintenance work tasks on site.
- Contractors will use their own risk assessment process/templates/risk matrices to prepare their risk assessments for their work tasks.
- ALIGN will use its own risk assessment process/templates/risk matrices to prepare its risk assessments for its work tasks.
- By prior agreement, a peer review will be carried out for all high-risk activities.
- All RAMS will be issued as "Fit for Construction" to the Principal Contractor.
- All RAMS will be assessed by the Principal Contractor against risk criteria.
- All RAMS will be reviewed by the Principal Contractor.
- All RAMS, will be formally accepted by the Principal Contractor as Status A – "Accepted" prior to work commencing.
- All RAMS will be itemised on a RAMS register created and maintained by the Principal Contractor.
- Work Authorisations and Permits to Work will only be issued if a Status A – "Accepted" RAMS exists on the RAMS Register.
- All RAMS will be cancelled once the task is completed or if more than 6 months old.
- All current RAMs will be subject to a weekly review between ALIGN and the Contractor to ensure scheduled works are covered within the current revision and foreseeable risks are identified and adequately controlled where such risks cannot be mitigated.

9.1.132 Using a standard method statement template helps reduce the amount of generic information or duplication of content that can mask important task/location specific information. It also aids the authors and reviewers since information is presented in a consistent order to a common standard so speeding up the preparation and review process and helping to identify any omissions.

9.1.133 For complex tasks and at the Principal Contractor's discretion, the ALIGN Project Team will arrange and chair a workshop involving the Contractor and the Principal Contractor's nominated RAMS reviewers and other stakeholders to carry out a team-based risk assessment (TBRA). A TBRA reduces abortive work and delays to the review process by ensuring that RAMS authors and the allocated reviewers have understood the proposed construction method; identified all significant hazards; selected and agreed in principle suitable and practical control measures; and identified any safety critical hold points.

9.1.134 Note: Only in exceptional circumstances (such as to remedy a safety issue or for emergency work that could not have been reasonably foreseen) will RAMS be accepted if issued less than 14 days in advance.

9.1.135 Method statements shall include suitable and sufficient information on the following:

- Task title, start date and duration.
- Description of the works (a step-by-step process for completing an activity).
- Identification of drawings relevant to the task.
- Identification of any permits and consents required.
- Resources required (competent people, Equipment, Plant and Materials).
- Equipment, Plant and Materials to be used and any assessments needed or authorisations for use.
- Assessment of significant health, safety, security and environmental risks and impacts for all tasks and activities.
- Control measures and Safe Systems of Work.
- Personal Protective Equipment.
- Emergency arrangements and initial incident response.
- Temporary amended systems.
- Monitoring and compliance.
- Risk Assessment.
- Specific Equipment required to complete the task.
- Relevant Undertakings and Assurances (U&A's) relevant to the location and planned activity.

9.1.136 Method statements shall also:

- Be expressed in an easily understandable manner using simple language.
- Define clearly and concisely the safe system of work developed by the contractor which integrates the health, safety, environmental, security and ecological control measures identified by risk assessment into the steps required to complete the task.
- Result in effective communication of this safe system of work from a contractor to his workforce via his Supervisors.
- Identify hold points and/or high-risk steps in the task at which interventions/monitoring should take place.

9.1.137 Risk assessments and method statements (RAMS) will only be prepared by person(s) who have received suitable risk assessment training and suitable task knowledge and experience.

9.1.138 Method statements are sometimes lengthy documents which describe either a major activity or a generic task which may be carried out at different times or locations. In these cases, Task Briefing Sheets or similar should be used to break

down the key elements of work described in the method statement for different work groups/teams.

- 9.1.139 Clear communication of accepted work methods and controls defined in risk assessments and method statements must take place prior to work commencing via a pre-job brief. This is to be carried out using a task briefing sheet delivered by a manager or supervisor. The delivery method must be closely matched to the competence and language skills of the recipients to ensure that there is a true understanding of the work method.
- 9.1.140 Briefings will be recorded on signed task briefing sheets in addition to a section being included to question the workforce upon their understanding of the approved RAMs and in particular the identified control measures. For subcontracted work, all Contractors are to retain copies of their lower tier contractor briefing record and a manager is to attend enough briefings to ensure the standard and level of information given is acceptable.
- 9.1.141 Task briefings are in addition to the Contractor's Daily Activity Briefings with his team covering specific hazards such as severe weather conditions, work interfaces and lessons learnt from the preceding shift.
- 9.1.142 The Principal Contractor will identify health and safety interventions/monitoring to confirm compliance with RAMS through planned inspections by the Principal Contractor's Team.
- 9.1.143 Where activities cannot be carried out as per the RAMS, the contractor's Supervisor must ensure that the work ceases until the activity is reassessed and either an addendum to the RAMS is prepared or the RAMS is revised, reviewed by the Contractor Safety Professional, accepted by the Principal Contractor and re-issued.

Work Authorisation / Permits for Work

- 9.1.144 The Principal Contractor will operate a Work Authorisation and Permit for Work System to control all construction, maintenance and commissioning activities in sector C1 in accordance with "ALIGN Permits to Work Procedure – 1MC05-ALJ-HS-PRO-C001-000006", and the generic requirements given in HS2's "Supply Chain Health and Safety Approach".
- 9.1.145 All construction work must have a work authorisation issued by ALIGN and all high-risk work will be subject to the Permit to Work System to include:

- Permit to Break Ground
- Hot Works Permit
- Permit to work
- Permit to cross utilities/work in close proximity of overhead services.
- Permit to remove vegetation
- Permit to work over/near water
- Permit to use ladders/Step Ladder
- Permit for Confined Space Works
- Permit to work on/test electrical equipment

Point of Work Risk Assessment (POWRA)

- 9.1.146 All Principal Contractor and contractor personnel are required to complete a Point of Work Risk Assessment (POWRA) at the workplace prior to commencing any new physical work activity or when conditions change and at least daily
- 9.1.147 The POWRA is the final step in the work planning process. A POWRA is a process to confirm that the work planning process (including risk assessments and method statements) has adequately identified all hazards and control measures to carry out a task safely; or to identify unanticipated hazards and the additional controls required; or deal with changes in conditions/personnel etc. It also ensures that the hazards and controls are fully understood and accepted by the team carrying out the task.
- 9.1.148 The process of developing a POWRA before starting or continuing a work task helps ensure proper OH&S planning by ensuring the team “stop and think”. By involving each team member in task planning before work begins, they are encouraged to think about the hazards involved and controls required and so own the safety process. Developing the POWRA also identifies resources (tools, equipment, materials, and personnel) to ensure their availability at the point of work which improves efficiency and helps prevent the taking of short-cuts or improvisation which often leads to accidents.
- 9.1.149 If, during a task, additional hazards are identified e.g., conditions change (ground conditions or severe weather/environmental conditions), personnel change, or a deficiency in the plan is discovered, work shall stop. The current POWRA is then modified or a new POWRA created to eliminate or control the additional hazards.
- 9.1.150 If the task changes or the POWRA process identifies the need to change the agreed work methodology defined in the method statement, then work cannot continue until a revised method statement has been prepared and approved as above.

- 9.1.151 A POWRA may not be used to justify deviating from the method of working defined in an approved method statement.
- 9.1.152 The POWRA is developed on site at the point of work (not in the office) by the team assigned to perform the work, guided by the supervisor (working or non-working foreman) who leads the discussion.
- 9.1.153 Any objection to the content of the POWRA should be raised with the contractor's Supervisor for discussion and resolution. If the objection cannot be resolved after escalating the objection to the Contractor's Site Management team, then refusal to sign the POWRA constitutes refusal to work on the grounds of safety.
- 9.1.154 In summary, POWRAs are used by competent workers (already briefed by their Supervisor on the RAMS) to check that before starting or continuing a task:
- They understand what it is they're about to do
 - They know how they're going to do it safely
 - There are enough people to do the work
 - They have all tools and equipment they need
 - There are no previously unanticipated hazards
 - Conditions have not changed
- 9.1.155 Each contractor work crew under the leadership of a working foreman (ganger/charge hand/supervisor) must complete a POWRA. Where the team identifies hazards that are not adequately controlled, then they will ensure that the work does not start/continue until the hazard has been suitably controlled. This may involve addressing the hazard at source or reporting to their supervisor.
- 9.1.156 Within 2 hours of the task commencing, non-working contractor foremen/supervisors shall visit each work location and challenge work crews on their understanding of the work activity (and agreed control measures) and shall review and countersign the POWRA. The Point of Work Risk Assessment does not replace the legal requirement for a risk assessment.

Personal Protective Equipment

- 9.1.157 Generic requirements for personal protective equipment are given in HS2's "Supply Chain Health and Safety Approach" and "Personal Protective Equipment"
- Provide Personal Protective Equipment (PPE) in accordance with any risk assessment and mitigation control

- Procure PPE from companies who are members of the Registered Safety Suppliers or similar scheme, such as SEDEX (ethical trading)
- Ensure orange PPE, with long sleeve tops, is worn for all worksite activity
- Develop a process for regular inspection, training and replacement of PPE.

9.1.158 Individual's employers shall provide the following PPE, which will be worn by all individuals when entering any designated PPE zones, within the worksite:

- Safety helmets with 4-point chin strap, that comply with BS EN 13688:2013 Protective Clothing – General Requirements, (although an exception may be made for Sikhs wearing turbans, who do not wish to wear a safety helmet on religious grounds, where risk assessment determines that a turban provides adequate protection from the risk of head injury). Please note; only purpose made hard hat liners are permitted to be worn beneath any hard hat, (hoodies/bobble hats are not permitted).
- Hi-visibility tops (Long sleeved t-shirts or polo shirts, vests, jackets) orange with reflective tape, which complies with EN ISO 20471 (formally EN ISO 471:2003) class 3, in addition to long sleeves.
- Hi-visibility long trousers (working trousers and over trousers) orange with reflective tape compliant with EN ISO 471:2003 class 3
- Safety footwear, which complies with BS EN ISO 20345:2011 Personal Protective Equipment, and also includes:
 - High Support to the ankle
 - Covered toe protection
 - Mid-sole protection
 - [Metatarsal](#) protection (Wellington Boots to be S5 as a minimum)
Rigger boots are prohibited
- Eye protection: That conforms to BS EN166:2002 1.F. Personal Eye Protection Specifications, this is also required for those who wear prescription eye wear.
- Hand protection that conforms to BS EN388:2003 intermediate design (Minimum cut C or above)
- Hearing protection that conforms to BS EN 352, active or passive with filter according to the Mandatory Hearing Protection Policy from 1/09/2020 (18/08/2020) 1MC05-ALJ-HS-POL-C001-000007

9.1.159 Task specific PPE will be subject to risk assessment and may include the following:

9.1.160 Personal head lamps for persons working at night and ATEX rated intrinsically safe equipment for those working in tunnelling and below ground environments

9.1.161 For persons exposed to working in inclement weather conditions, Hi-visibility (EN ISO 20471 class 2) protective equipment which complies with EN 343:2003 Class 3:3

- 9.1.162 For persons working under a hot works permit and/or in close proximity to buried services and electrical installations, all clothing must be Hi visibility flame resistant, antistatic and arc flash resistant PPE which complies with EN ISO 11612 (FR), EN1149 (AS), EN ISO 20471 (HV) and IEC61482 (ARC)
- 9.1.163 For persons working in close proximity to concrete application shall wear similar disposable overalls, together with items identified in the risk assessment
- 9.1.164 For persons engaged in Works Over or Near Water, without collective protection in place, suitable PPE including life-jackets conforming to EN399 (ISO 12402-2) rated at 150 Newtons
- 9.1.165 Where RPE is required the minimum standard to be provided with be FFP3 with all wearers of RPE being subject to Face Fit with evidence of passing the face fit being provided.
- 9.1.166 Suitably coloured safety helmets (identifying the name of the person and their company) will be worn by all persons in the construction areas on site to aid in the identification of key roles as follows:

Role	Safety Helmet Colour
Contractor Working and Non-Working Foremen/Supervisors (gangsters/charge hands)	Black
Medical Staff	Green
Trainees, Apprentices or Young Persons (16 to 18 years old)	Red
All Visitors not carrying out physical work	Blue
All other contractor personnel/operatives	White
All Banksman, Vehicle Marshals	Yellow
Slings/Signallers	Orange

- 9.1.167 First aiders will be identified by a sticker applied to their safety helmet.

- 9.1.168 Drivers of vehicles in the construction areas must wear (or have available) a full set of mandatory PPE; passengers must also wear PPE if they intend to exit the vehicle on site.

Site Rules

- 9.1.169 To help communicate and provide a focus on our key health and safety requirements, ALIGN has introduced the 12 Health & Safety Basics, which incorporate our 5 Major risks and 13 life saving rules.
- 9.1.170 Site Rules and Expected behaviours
- All personnel must have received the HS2/ALIGN site induction before they begin work. Visitors must be accompanied at all times.
 - Mandatory PPE must be worn at all times. Safety footwear, hard hat, high visibility jacket/vest, trousers, gloves, light eye and hearing protection. Other items of PPE should be worn on a risk assessment basis.
 - Follow instructions, risk assessments and method statements.
 - Do not undertake any work where there is a risk to health and safety unless you are satisfied that adequate control measures are in place.
 - Permits to work are required for certain high-risk activities or access to high-risk areas (permit to break ground, hot works and confined space entry)
 - Plant must only be operated by trained, competent, authorised personnel.
 - Do not work at an unguarded edge without adequate fall protection.
 - Always use designated pedestrian routes.
 - High standards of housekeeping are required at all times.
 - All accidents, incidents, near misses and spillages must be reported to your supervisor and to ALIGN.
 - Horseplay or inappropriate behaviour is not acceptable on site.
 - Working under the influence of alcohol or drugs is not permitted on site.
 - Use of mobile phones is prohibited while driving, working at height, using machinery etc. Mobile phones must only be used only when you are in the welfare facilities or designated mobile phone location, or standing still in a segregated pedestrian area.
 - Do not interfere with, or misuse any item of plant or equipment provided

Emergency arrangements

Planning

- 9.1.171 ALIGN has developed an Emergency Response and Incident Management Plan 1MC05-ALJ-HS-PLN-C001-000041. This is an overarching document setting out the

organisation, planning and expected response to incidents as defined in the works information.

- 9.1.172 Each work area will prepare a specific emergency plan.
- 9.1.173 For specific activities, for example confined space, emergency procedures for that activity will be contained in the Method Statement.
- 9.1.174 The emergency arrangements will be regularly tested and practised. Emergency exercises will be conducted to demonstrate the adequacy of the emergency arrangements, and all staff, contractors and visitors involved with the project shall participate in the exercise programme as required. Contractors will need to prepare and execute a programme of drills and exercises to cover the risks identified in their working areas.

Fire Safety

- 9.1.175 Fire Safety Risk Assessments and the "Sector C1 Fire Safety Plan", that detail the site-wide fire safety arrangements for sector C1 have been developed by ALIGN using procedure "Provide Fire Prevention and Fire Safety Arrangements", the Regulatory Reform (Fire Safety) Order 2005, the Fire Protection Association Fire Protection on Construction Sites, and the Joint Code of Practice on the Protection from Fire of Construction Sites and Buildings Undergoing Construction. For the early works) the fire plan as developed by ALIGN will apply to the Compound Managed directly by ALIGN. With remote work locations being subject to a fire risk assessment being undertaken by the appointed contractors engaged at the said work location. ALIGN will review the compliance of those Fire Risk Assessments
- 9.1.176 The locations of external fire assembly points will be displayed on site notice boards. These must be brief during site induction and updated regularly at tool box talks. Contractors will need to identify suitable fire assembly points for their working areas.
- 9.1.177 Fire risk assessment have been completed for all such areas and form part of the Fire Plan for each Works Location- This shall be referenced in each specific Safety, Health and Wellbeing Management (Construction Phase) Plan

Emergency Medical/First Aid Response

- 9.1.178 ALIGN will operate a coordinated Emergency Medical/First Aid Response to all persons on site utilising resources available on site from ALIGN and all Contractors.

- 9.1.179 First Aid kits shall be provided by the contractors in all their site offices, mobile construction equipment with enclosed cabs and in site vehicles where determined within specific first aid risk assessments. First aid facilities will be clearly identified with signage.
- 9.1.180 Requests for First Aid/Medical Emergency response to anywhere on the ALIGN site will be made by contacting the ALIGN emergency numbers as detailed in the local emergency response plan.

10 Occupational Health and Wellbeing

- 10.1.1 Align JV will provide an comprehensive occupational health facilities and staff on site. These services will be made available to all personnel working on the project.
- 10.1.2 The OH team will provide services at remote sites on a scheduled basis.
- 10.1.3 Occupational Hygienists will provide a programme of monitoring and assurance based on the Health Risk Assessments for each work area.
- 10.1.4 Refer to the ALIGN Health Management Plan (1MC05-ALJ-HS-PLN-C001-000003) for more comprehensive details.

11 Controlling Significant Site Risks

- 11.1.1 Generic requirements are given in HS2's "Supply Chain Health and Safety Approach"

Dealing with Utility Services

- 11.1.2 ALIGN is clear that buried services present one of the most significant hazards on the project. For this reason, there is a team dedicated to obtaining and providing utilities information and the associated permits for any occasion when our operations require the ground to be penetrated or broken. ALIGN's procedures for dealing with buried services during the Ground Investigation works are described in H14 - Safe Working Procedure for Working in the Vicinity of Underground Services. In addition, all works requiring the breaking of ground for any purpose will be subject to full controls as defined within the ALIGN Permit Procedure 1MC05-ALJ-HS-PRO-C001-000006.
- 11.1.3 Avoiding overhead services: In conjunction with our Permitting procedures, ALIGN requires all contractors to follow the HSE's guidance document "Avoiding danger

from overhead power lines" Guidance Note GS6, which can be downloaded for free from the HSE website.

- 11.1.4 Refer to ALIGN Permit to Work Near Overheads/Crossing Utilities - 1MC05-ALJ-HS-FRM-C001-000114

Temporary Works

- 11.1.5 Refer to 1MC05-ALJ-CL-PLN-C001-000018 Temporary Works Management Plan

Working at Height

- 11.1.6 A work place is 'at height' if a person could be injured falling from it, even if it is at or below ground level (i.e., excavations and service pits). RAMS for work activities involving work at height shall define the safe system of work that will ensure that:
- All work at height is properly planned and organised
 - All work at height takes account of weather conditions that could endanger health and safety
 - Those involved in work at height are trained and competent
 - The place where work at height is done is safe
 - Equipment for work at height is appropriately inspected
 - The risks from fragile surfaces are properly controlled
 - The risks from falling objects (including tools) are properly controlled. Tools and equipment used at height which represent a foreseeable risk of being dropped/falling from height will be tethered.
 - Persons working at height are in visual and verbal contact
- 11.1.7 Work at height access equipment must be suitable for the task and of good condition.
- 11.1.8 Safety nets, air bags or other similar devices shall not be used as the only means of fall protection.
- 11.1.9 An emergency rescue plan shall be in place whenever fall restraint, fall arrest or safety nets are used; and a safe means of rescuing promptly a fallen worker or incapacitated worker shall be always available. The emergency rescue plan can be defined in the RAMS or in a separate plan and must include the provision of rescue resources for work at height, either for rescue of an incapacitated person by others, or self-rescue of an individual without additional assistance.

- 11.1.10 If any Work at Height is found to be necessary, it will be subject to the ALIGN Work at Height Procedure.

Scaffolding

- 11.1.11 Particular attention must be paid to the strength and stability of all types of scaffolding. This includes the provision of guardrails and toe boards and the quality of supporting timber.
- 11.1.12 Written confirmation is required to demonstrate that a person independent from those directly responsible for the design has checked designed scaffold details and calculations. This check may be carried out in the same office by someone not involved in the design. This confirmation shall be in place before work commences. For complex or high risk designed scaffolds, details of the qualifications and professional indemnity insurance of the person designing or checking the design shall be in place before work commences.

Ladders

- 11.1.13 Stepladders shall not be used as working platforms unless a risk assessment has demonstrated that mobile towers or podium scaffolds cannot be reasonably used for the proposed work. Step ladders may only be considered for non-complex activities of short duration. Short duration but repetitive task e.g., cable tying or fitting brackets, multiple lamps changing or bracket installation on pipe runs would be seen as one activity and as such the risk assessment would have to justify why a platform had not been provided for the extended works. Any step ladder used must have collective protection built into the apparatus. Ladders are only permitted when they form part of a proprietary access system with full collective protection being maintained.

Mobile Elevating Working Platforms (MEWPs)

- 11.1.14 All works involving the use of a Mobile Elevated Work Platform will be undertaken in full compliance with the ALIGN Mobile Elevated Work Platform Procedure 1MC05-ALJ-HS-PRO-C001-000030 in addition to task specific Status A RAMs being in place.

Prohibited types of plant/equipment

- 11.1.15 The following items of plant and equipment are prohibited upon any ALIGN works site:

- Ladders unless they form part of a propriety access system or under permit to work
- Traditional forward tipping dumpers
- Angle Grinders with a diameter less than 230mm are prohibited. Substitute with alternative authorized tools or those grinding tools approved and fitted with innovative guards and protective devices,
- The use of Acetylene is prohibited upon all ALIGN work sites. Substitute with specialist gases such as Apachi+™ which is a high purity fuel gas offering substantial benefits in oxy-fuel cutting, high velocity oxy-fuel (HVOF) spraying and brazing.
- The use of 'bulldog clamps' for lifting purposes or retaining.

Pressurised systems

11.1.16 The use of any pressurised air/gas or similar product is only to be considered where no safer alternative method is available (ie: use of water)

11.1.17 Prior to the use of any pressurised air/gas or similar product where the above criteria cannot be met the following must be in place:

- An approved fully robust operating procedure covering all elements of the planned activity
- A schematic diagram of all pressurised systems and labels on control valves showing positive and negative pressure on and off
- Pressurised systems must have a minimum of 1 fail safe valve preventing the build-up of excess pressure within any system
- The pressurised product is provided at the lowest possible pressure to complete the scheduled task, achieved through but not limited to low pressure supply (de rated bottles) and low rated regulators upon bottles/canisters
- All components and fittings within the pressurised system must be in receipt of valid evidence of strength and integrity with a suitable safety factor applied
- Pressurised systems are subject to a pressure test / leak test" in a controlled environment and a pre use check witnessed by a supervisor with records of such tests recorded
- All persons involved in the planned activities must be competent and have received suitable training in the use of and handling of compressed air/gas
- All supervisors/managers involved in the planned activities must be competent and have received suitable training in the use of and handling of compressed air/gas

Traffic Management and Segregation of Vehicles and Pedestrians

11.1.18 Site Traffic Routes will be contained in the site specific traffic plans.

11.1.19 Align will comply with the HS2 Safe Plant Operation Standard.

11.1.20 They key elements of the standard include.

- Work Planning
- Risk Identification, perception, and awareness
- Plant Selection and Specification including technology and innovation.
- Operator Competence
- Effective Supervision
- Change identification and communication
- Standardisation and definition of working areas

11.1.21 ALIGN have implemented a coloured zonal guidance including the use of coloured barriers to identify temporary transit and traffic routes as follows:



- White Barriers - A non-construction (white) zone - Areas where no construction control (e.g., PPE) is required. For example, designated welfare and private vehicle parking areas.
- Green Barriers - A protected and segregated environment for navigating around or through a red or amber (restricted or controlled) zone. For example- designated pedestrian routes on and through sites.
- Amber (Yellow) barriers - A controlled (amber/yellow) zone – Access control systems in place to allow only those trained to operate in or persons authorised by the areas Black Hat. For example - pilling operations, plant activities where access is required under controlled conditions.


- Red Barriers - A restricted (red) zone – Unambiguous physical demarcation and no pedestrians allowed. For bat/badger exclusion zones, contaminated land, confined spaces where no access is required, work areas where remote controlled plant is in use.

11.1.22 Transitional points will be identified with red hooped barriers with sprung loaded gates and zonal signage being clearly displayed.

11.1.23 Where possible permanent barriers and gates will be installed.

Protection of work platforms and haul roads to prevent over run

11.1.24 Work areas and traffic routes will be adequately protected to leading edges as to prevent mobile plant and equipment from over running work platforms and haul roads. Upon raised working platforms and haul roads where there is a foreseeable risk of overrun such works areas and transit routes will be protected by a bund or similar, a minimum of half the height of the largest wheel or tracked items of plant/equipment being operated within the zone as to prevent over run. See examples below:

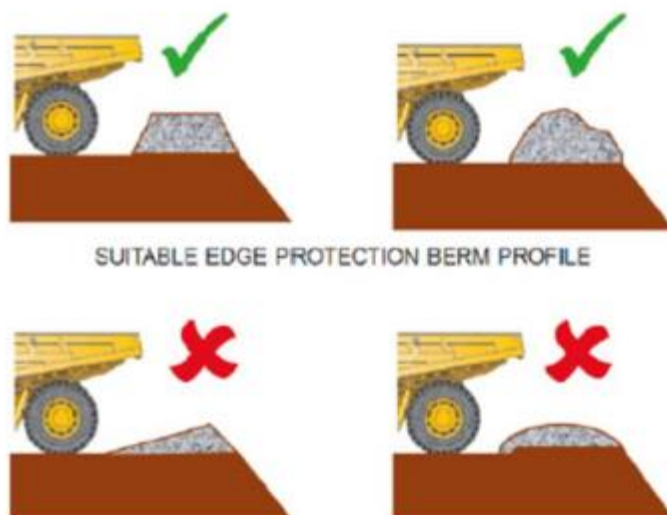

Delivery Vehicles and Logistics.

11.1.25 For full details on arrangements for delivery drivers, traffic routes FORS and CLOCS Compliance please refer to the Logistics Environmental, Sustainability & Safety Management Plan (ESSMP) (1MC05-ALJ-CL-PLN-C001-000017)

Unloading/Loading of Materials and Equipment from Vehicles

- 11.1.26 Unloading and loading of materials and equipment from vehicles for the ground investigation works shall be specifically covered in the RAMS for the work. However, all vehicle operators and those responsible for vehicle loading and unloading must be trained and competent in loading and unloading their vehicles and trailers. The Driver and Vehicle Standards Agency has produced the useful guide on this subject which can be found at the following link:
- 11.1.27 <https://www.gov.uk/government/publications/load-securing-vehicle-operator-guidance/load-securing-vehicle-operator-guidance>
- 11.1.28 Where there is a need to access the rear of any trailer then edge protection will be provided along with a safe means of access and egress.
- 11.1.29 For any lifting refer to ALIGN lifting Procedure [1MC05-ALJ-HS-PRO-C001-000031](#)

Loading/Offloading of Mobile Construction Equipment from Vehicles

- 11.1.30 In addition to the general requirements refer to “Specific Risk Assessment - Workshop - Loading and Unloading Vehicles”.

Poor Ground Conditions

- 11.1.31 The local ground conditions will be assessed as part of the point of work risk assessment (POWRA) and taken into account when planning a safe method of work, which will include assessment of the type of vehicle, track matting, alternative permitted routes etc. All of the above will be considered when deciding to proceed with the work at that time and location. On no account will the safety or health of people be put at risk due to poor ground conditions.
- 11.1.32 RAMS will include a generic method for extricating vehicles and other equipment that may have become bogged down in poor ground.
- 11.1.33 At any location where construction vehicles enter or leave the highway, the contractor shall ensure that mud and other debris is not deposited on the highway. This may require the use of a jet wash or similar method of removing mud etc. from the body and wheels of vehicles using the access. If the highway does become contaminated in such a way, the contractor shall ensure that it is cleaned immediately and at no point is left in a slippery or other condition that could become

a hazard to passing motorists or other road users. The contractor will have an arrangement with a road sweeper to keep the carriageway clean as and when necessary.

Mobile Construction Equipment

- 11.1.34 Mobile Plant will meet the standards set out in the in the Safe Plant Operation Standard.
- 11.1.35 A full record of mobile plant currently upon the project will be maintained by each appointed contractor for all plant under their control and that of their supply chain.
- 11.1.36 All items of plant and equipment are to be in receipt of:
- 11.1.37 Thorough examinations (LOLER) for lifting equipment, (COSHH) for Local Exhaust Ventilation equipment, PSSR for Pressure Vessels / equipment above 250 Bar/litres
- 11.1.38 NB: CE Certification will suffice for new portable equipment; Where Safety relies on installation a Thorough Examination is required post-installation; A or B defects detailed on Thorough Examination Reports should have evidence of rectification
- PAT test for portable Electrical Equipment (Electricity at Work)
 - Fitters check sheet (PUWER) for all Plant (wheeled or static)
 - Competent Person Check-sheet for Personal Fall Protection Equipment (PUWER / Work at Height Regulations)
 - Evidence of Fitter's Check (e.g., a sticker) for Portable Equipment (PUWER)
 - Evidence of Calibration (e.g., a sticker) for measuring equipment (PUWER, Quality)
- 11.1.39 All mobile plant being delivered to any ALIGN site/premises will be subject to checks and verification in accordance with the Mobile Plant Delivery and Authorised Use Process 1MC05-ALJ-HS-FRM-C001-000563, shown in the next page and will display an in-date Plant Identification Poster, in date plant tags and pre use/daily and weekly in-house checks by trained user / operator or supervisor should be in-date

Other Plant and Equipment

- 11.1.40 In accordance with the HS2 Supply Chain Health and Safety Approach, the accepted standard of training for mobile plant is CPCS or NPORS (with CSCS hologram) or a Partner Card Scheme containing the CSCS logo.

- 11.1.41 In relation to the undertaking of vehicle marshal duties upon a highway the required standard of training is LANTRA 12D.
- 11.1.42 To ensure clear communication links are maintained between mobile construction plant operators and persons who are employed to direct and monitor safety critical times of mobile plant, for example:
- Communication between cranes and slinger/signallers
 - Communication between concrete pump operators and nozzle men
 - Excavators/Dozers and appointed banksman
 - Telehandlers and vehicle marshals
- 11.1.43 Contractors will employ a 2-way communication system such as Duplex Dect Comm11 to ensure continual communication between operators and safety critical personnel is maintained.
- 11.1.44 Restriction upon forward tipping dumpers: The use of forward tipping dumpers is not permitted upon any ALIGN works site. Contractors will source alternatives such as:
- Hydrema - all round visibility dumper with cab
 - Wacker Neuson - Dual View with swivel driver's seat cabbed dumper
- 11.1.45 Quick Hitch restriction upon HS2/ ALIGN sites is as follows: All semi-automatic and First-Generation Manual Hitch attachments are prohibited upon at all work locations. Only direct connection or fully automatic quick hitch attachments are permitted upon any ALIGN site.
- 11.1.46 Wheeled/tracked plant under 5T will need director and safety team approval before use. Where excavators under 5T are used, any attachment must be directly attached to the boom. Quick hitches must not be used on excavators below 5T.
- 11.1.47 Concrete and pump lines: The primary method of cleaning out any concrete or grout line will be with the use of water. Contractors are to ensure they have a robust documented risk assessment for such tasks with the mandatory use of a ball (pig) catcher attachment and a means of constant communication between the pump operator and assistant.
- 11.1.48 However, where there is no other practicable alternative to clean out such lines in the conventional method using water the use of compressed air is permissible with the following in place:

- Fully robust RAMs having been submitted and approved in advance
- Eye protection is replaced with a full-face visor
- No personnel are within close proximity of the pipe line and in particular at the discharge end
- All flexible hoses are removed (does not apply to CFA ground hoses)
- Pipe line is secure and supported
- No bends within the final 15m of the pipeline
- Ball catcher attachment must be fitted to the discharge end
- The compressed air must be introduced gradually and not exceed 7 bar
- A competent assistant is appointed to assist the pump operator

11.1.49 Accommodating Adjacent Land Use: Land Access is arranged by ALIGN on a permitting basis through HS2. No access is permitted to any land that is not:

- A public right of way
- Land covered by a current valid permit issued to ALIGN
- Land expressly identified as prohibited access in the contractor's permit to work issued by ALIGN

11.1.50 Landowners: Landowners requiring access to their land through land occupied by ALIGN and its contractors will be accommodated as far as reasonably practicable and if safe to do so. The Landowner requiring access should contact the ALIGN Community Engagement Team in the first instance to raise a request. The request will be passed to the Construction Management Team and meetings held, if necessary, between the landowner and site team to plan the provision of access to the landowner. All further dealings with the landowner may be carried out directly by the site team but will be monitored by the Community Engagement Team. Access will only be granted to the landowner if it has been properly planned in advance, all risks associated with the interaction assessed and mitigated, and the site team briefed on the plan.

Work On or Near Fragile Materials

11.1.51 No fragile materials are expected to be encountered

The Control of Lifting Operations

11.1.52 Lifting Operations are managed following the Lifting Operations Procedure (1MC05-ALJ-HS-PRO-C001-000031) This standard defines the minimum and essential requirements for the safe planning, organisation, coordination, supervision, and execution of all lifting operations to be undertaken at all C1 ALIGN Works sites

- 11.1.53 All contractors (including their supply chain) and any other organisation and or personnel who are engaged with the planning, organisation, coordination, supervision, and execution of lifting operations must adhere to or exceed the requirements of LOLER 98, & BS7121 suite of documents and this procedural document.
- 11.1.54 ALL Contractors may use their own company lifting operations management procedures; however, these procedures must meet all requirements of this document. ALIGN shall monitor and ensure compliance with this across all lifting operations undertaken on C1 Align Works sites. ALIGN prohibit the use of single use slings/lifting accessories. Whilst ALIGN encourage the use the use pre-slung loads all lifting accessories will be certified with evidence of certification (individual or batch) being provided.

Excavations

- 11.1.55 In addition to the general requirements refer to “H14 Safe Working Procedure for Working in the Vicinity of Underground Services”.
- 11.1.56 Contractors undertaking any works involving the breaking of ground will ensure a Cat B PAS 128 survey has been completed prior to works commencing, with the ALIGN Permit to Break Ground being used for all such works.
- 11.1.57 All formed excavations will be adequately protected to prevent persons and plant from falling within any formed excavation, with specific details to be identified within the Contractors RAMs.
- 11.1.58 ALIGN uses the following guidance notes to ensure safe excavation practices:
- ALIGN Excavations and Ground Support Systems
 - ALIGN Safe use of Excavators

Confined Spaces

- 11.1.59 All such works will be undertaken in accordance with ALIGN Confined Space Procedure Confined Spaces Procedure1MC05-ALJ-HS-PRO-C001-000027 with personnel required to enter a confined space being training to City and Guilds 6150 and to the appropriate risk and competence level.

Work Near Water Giving a Risk of Drowning

- 11.1.60 In addition to the general requirements ALIGN's detailed procedures and training requirements for personnel working within 3m of the water's edge, and for those working over water, are detailed within the ALIGN Work on or Over Water procedure - 1MC05-ALJ-HS-PRO-C001-000012

Explosives and Cartridge tools

- 11.1.61 Contractors shall not bring onto the site explosives or explosive devices including cartridge operated tools without prior written consent of the Principal Contractor. Contractors shall be responsible for obtaining all necessary licences or permits for such items of equipment.

Housekeeping and Storage of Materials and Work Equipment

- 11.1.62 In addition to the general requirements, Contractors will provide suitable storage areas for materials and work equipment without exception.
- At all times safe access and egress around stored items must be maintained.
 - Particular attention must be given to storage of items and their stacking height to ensure that hazards from falling objects are removed.
 - All loose materials and components are to be stored in crates or stillage's as to reduce the potential of trip hazards.

Portable Electrical Equipment

- 11.1.63 In addition to the general requirements, all items of electrical equipment used upon the construction areas will be subject to 3 monthly PAT with current test information to be made available and items of equipment displaying current information.

Erection of Structures

- 11.1.64 During site mobilisation, there will be a requirement for contractors to establish site compounds. Contractors shall ensure that all lifting operations and work at height activities are carried out in accordance with HS2's "Supply Chain Health and Safety Approach" and "Work at Height"

Severe Weather Conditions

- 11.1.65 Effective arrangements to be detailed within Contractors RAMs to include but not limited to Risks Associated with Flooding and severe weather conditions.

- 11.1.66 Adverse Weather controls are detailed within the ALIGN Adverse Weather Procedure - 1MC05-ALJ-HS-PRO-C001-000016, with the detailed control measures and precautions being applied to all works under the direction of ALIGN and appointed contractors.

Fire Hazards

- 11.1.67 Rubbish or other materials must not be allowed to accumulate to prevent potential fire hazards. In particular cabin heaters must be kept clear of clothing and other electrical items turned off at the end of each shift or when the premises are unattended.
- 11.1.68 All exit routes will be kept clear at all times and access to emergency exits maintained.
- 11.1.69 Fire hazards in the locations of intended works must be considered in the risk assessments and method statements. Contractors must assess each work location and implement appropriate fire precautions as appropriate.
- 11.1.70 Every site compound shall be subject to a specific Fire Risk Assessment every six months carried out by a competent person. Fire hazards will also be incorporated into weekly health and safety inspections and other monitoring of all offices and site compounds.

Hand Held Work Equipment

- 11.1.71 All hand tools will be subject to compliance with Provision and Use of Work Equipment Regulation 1998 (PUWER) including but not limited to pre use inspections.

Interaction with the Public

- 11.1.72 All communications with the public must be done through the Communications Team and Community Engagement Team. The only exceptions to this are the Community Safety Champions and in the event of an emergency, which requires direct involvement with the public in order to save harm, injury or damage to property. The strategy for community engagement is laid out in the Community Engagement Plan.
- 11.1.73 Refer to the Community Safety Plan – draft outline document. 1MC05-ALJ-HS-PLN-C001-000008

- 11.1.74 The instruction provided during the induction is as follows:
'If approached by anyone you do not recognise and are asked questions about the HS2 project do not discuss the project. They could be protesters, local community, criminals, or the media, looking to gather information. Please refer them to the HS2 Helpline number on your card'

Sharp Objects including Barbed Wire and Thorns

- 11.1.75 All areas where personnel may come into contact with barbed wire or other sharp objects shall be assessed and suitable precautions put into place. Particular attention will be paid to the likelihood of fly tipping at or near ALIGN work areas. A point of work risk assessment will be undertaken for any instance of fly tipping that needs to be managed by ALIGN contractors. This will include the assessment of the presence of sharp objects, including hypodermic needles, blades of any kind and thorns. This requirement shall be included as part of the risk assessments and method statements developed by the contractors

Demolition Works

- 11.1.76 None normally required during this stage of the works; however, some demolition survey works will /may be undertaken (i.e., Asbestos Surveys and structural stability surveys). Where demolition works are needed it is covered by a specific demolition plan / RAMS.

Work in Colne Valley lakes and other bodies of water

- 11.1.77 The Colne Valley viaduct passes over several water courses and lakes and will necessitate a large amount of work in close/3m proximity to water and at height over water. Materials and other resources will be delivered to viaduct pier locations using waterborne transport. Protection of water bodies and water courses will be explained in the specific section of the appropriated RAMS as and when required.

De-watering

- 11.1.78 Pumping tests will be properly designed, planned and executed.

Piling

- 11.1.79 Test Pile/Load Pile works to be controlled in accordance with Approved Status A RAMs which will be made available to HS2 for review and comment in advance of such works commencing.

Contaminated Land

- 11.1.80 It is likely that the scope of this Contract will involve access to, or intrusive investigation of, land which is classed as Contaminated. Sites have been classified for the purpose of H&S by HS2 Ltd in accordance with the Guidance for Safe Intrusive Activities on Contaminated or Potentially Contaminated Land (BDA, 2008). Refer to Section 4.14 for HS2 Ltd Phase One environmental statement volume 2: community forum area reports and map books for baseline information gathered for the Environmental Statement.

Asbestos Containing Materials

- 11.1.81 The asbestos risk for all works, including demolition and excavation in made ground, needs to be assessed and controlled by Contractors in accordance with the Control of Asbestos Regulations 2012 and the Approved Code of Practice.
- 11.1.82 Details of areas of potential asbestos will be contained in the site-specific Construction Phase plans.
- 11.1.83 Personnel involved in works or supervising works which could uncover potential ACMs will be in receipt of a valid asbestos awareness qualification (UKATA).
- 11.1.84 Contractor's RAMS will include arrangements for dealing with suspected ACMs during their works, in addition to compliance with the ALIGN Unidentified Finds Procedure – 1MC05-ALJ-HS-PRO-C001-000015

Control and Use of Hazardous Substances

- 11.1.85 Any use of hazardous substances, including hazards resulting as a by-product or waste from processes such as welding, will be managed through the use of COSHH risk assessments based on the Material Safety Data Sheets from the manufacturers and an assessment of the way in which the substance will be used. Refer to ALIGN procedure COSHH, which describes the hierarchy of control to be applied when there is a potential need for a hazardous substance to be used on an ALIGN site. COSHH storage will be identified on the Site Plan and records will be maintained at the site location.

Unexploded Ordnance

- 11.1.86 The available unexploded Ordnance (UXO) maps for the length of the route have been obtained and they indicate a low risk of encountering unexploded ordnance

(Zetica 2012). Mapping is only at a regional scale and relates to bombs dropped, not bombs stored.

- 11.1.87 A map of the unexploded ordnances in Sector C1 with reference 0615-ZET-GT-REP-000-000001, to assist in identifying any areas of risk in the Zetica Report was used to support completion of a detailed risk assessment.

Manual Handling

- 11.1.88 Contractors must ensure that they comply with the Manual Handling Regulations by following this simple hierarchy:
- Avoid hazardous manual handling operations likely to cause injury so far as is reasonably practicable
 - Assess any hazardous manual handling operations that cannot be avoided
 - Reduce the risk of injury so far as is reasonably practicable by implementing appropriate controls
 - Manual handling must be a specific consideration in every risk assessment produced for activities on the project and a specific manual handling assessment produced by competent persons.
 - Appropriate controls should consider the use of mechanical means to reduce exposure to muscular skeletal disorders and repetitive strain injury including advancements in available technology.
- 11.1.89 Contractors must ensure that their personnel and those of their sub-contractors have received adequate Manual Handling training with evidence being provided to ALIGN if manual handling works are to be undertaken.

Noise and Vibration

- 11.1.90 Detail of the management of occupational Noise and Vibration exposure are detailed in the Occupational Health Management Plan, 1MC05-ALJ-HS-PLN-C001-000003
- 11.1.91 Where possible exposures to these physical hazards will be designed out, alternative tools sought, or through management controls. Monitoring will be undertaken as necessary to demonstrate compliance with the occupational health exposure limits detailed in the works Information WI1150

Exposure to UV Radiation (from the sun)

- 11.1.92 Exposure to UV Radiation (From the Sun) will be managed with a cover up campaign being implemented along with personnel protection advice being available to the inherent risks associate with such exposure.

Substance Abuse

- 11.1.93 Everyone working on the ALIGN project shall comply with the ALIGN "Alcohol and Drug Policy" 1MC05-ALJ-HS-POL-C001-000002.
- 11.1.94 Workers must come to work fit for duty and ensure that they are not intoxicated by alcohol and are free from the effects of any illegal drugs when they report for work, or when called out during a period of standby, and that they remain so whenever they are at work or when driving vehicles on project business.
- 11.1.95 Workers must not drink alcohol during working time. No alcohol or illegal drugs shall be consumed by workers at any of the ALIGN project work locations.
- 11.1.96 The use, possession, storage, transportation, promotion and/or sale of illegal drugs or drug equipment is forbidden during working time, in the workplace or at the worksite.
- 11.1.97 Where workers are prescribed medication or are taking over-the-counter medicines or herbal remedies that may affect their work performance or the safety of themselves or others, they must advise their Employer or the organisation for whom they are providing the contracted service in addition to informing ALIGN Management.
- 11.1.98 Each Employer shall ensure that personnel under his control submit themselves for unannounced, post incident or 'with cause' testing for alcohol and/or illegal drugs if requested by ALIGN's site management. Testing shall be carried out in accordance with ALIGN "Drugs and Alcohol Policy"
- 11.1.99 Each Employer shall ensure that entry to the Site is refused to any of its visitors or employees who appear unfit through substance abuse. Illegal drugs or alcohol shall not be brought onto the site.
- 11.1.100 Anyone found in possession of illegal drugs will be reported to the police, and will be removed from site. They will be prohibited from working on any elements of the ALIGN project.

Toxic Plants

- 11.1.101 Refer to Pre-construction Information and Environmental Management Plan for the locations of toxic plants along the route and include them in relevant Risk Assessments and Method Statements.

Weils Disease and Lyme Disease

- 11.1.102 Contractors are to ensure that precautions are taken to ensure that all their personnel are made aware of the hazards associated with Weils Disease and Lyme disease and the course of action to be taken in the event of developing flu like symptoms having worked on the site.

Contact / Exposure to Agrochemicals and Fertilizers/ Animal Faeces

- 11.1.103 Contractors are to ensure that necessary precautions are taken to ensure that all their personnel are made aware of the hazards associated with coming into contact with or being exposed to agrochemicals, fertiliser, animal faeces and ensuring that suitable sanitary measures are in place such as alcohol hand washes.

12 Health and Safety File

- 12.1.1 Details of ALIGN's requirements for Health & Safety File information will comply with the requirements laid out in the Construction (Design & Management) Regulations 2015 and in HS2's WI1100 Health and Safety.
- 12.1.2 Arrangements for the collection and gathering, storage of information and H&S file approvers & stakeholders Arrangements for the Collection and Gathering of Information will be added to this Construction Phase Plan in due course.
- 12.1.3 A template is available on Business Collaborator: ALIGN Health and Safety File
1MC05-ALJ-HS-TEM-C001-000072

13 Reference Documents

#	Document Title	Reference
1	WI 1100 - Health and Safety Works Information	1MC01-HS2-PR-ITT-000-000471
2	WI 1150 - Occupational Health Works Information	1MC01-HS2-PR-ITT-000-000504
3	Supply Chain Health and Safety Approach	HS2-HS2-HS-STD-000-000006

#	Document Title	Reference
4	Health Management Plan	1MC05-ALJ-HS-PLN-C001-000003
5	Specific Safety, Health and Wellbeing Management (Construction Phase) Plan Template	1MC05-ALJ-HS-TEM-C001-000057
6	Design Management Plan	1MC05-ALJ-DS-PLN-C001-000001
8	Project Execution Plan	1MC05-ALJ-PM-PLN-C001-000001
9	Suspension of Works Notification Procedure	1MC05-ALJ-HS-PRO-C001-000011
10	Pre-construction Information Pack (PCIP)	P1C-HS2-HS-REP-C001-000001
11	ALIGN Contract Quality Plan	1MC05-ALJ-QY-PLN-C001-000001
12	Communications Management Plan	1MC05-ALJ-HR-PLN-C001-000005
13	Method Statement Template	1MC05-ALJ-HS-TEM-C001-000005.
14	Pre-start Questionnaire - Sub-Contract Pre-Start Meeting Agenda	1MC05-ALJ-CL-FRM-C001-000002
15	Commitments Compliance Plan	1MC05-ALJ-SE-PLN-C001-000002
16	Align induction procedure	1MC05-ALJ-HS-PRO-C001-000003
19	ALIGN Procedure "Risk Assessment Procedure"	1MC05-ALJ-HS-PRO-C001-000005
20	ALIGN Permits to Work Procedure	1MC05-ALJ-HS-PRO-C001-000006
21	ALIGN Emergency Response and incident management Plan	1MC05-ALJ-HS-PLN-C001-000041
22	ALIGN Permit to Work Near Overheads/Crossing Utilities	1MC05-ALJ-HS-FRM-C001-000114
23	Temporary Works Management Plan	1MC05-ALJ-CL-PLN-C001-000018
24	ALIGN Mobile Elevated Work Platform Procedure	1MC05-ALJ-HS-PRO-C001-000030
25	Route-Wide Traffic Management Plan	HS2-HS2-CL-PLN-000-000002
28	ALIGN lifting Procedure	1MC05-ALJ-HS-PRO-C001-000031
29	ALIGN Work on or Over Water procedure	1MC05-ALJ-HS-PRO-C001-000012
30	ALIGN Adverse Weather Procedure	1MC05-ALJ-HS-PRO-C001-000016
32	ALIGN Unidentified Finds Procedure	1MC05-ALJ-HS-PRO-C001-000015
33	UXO Desk Study and Risk Assessment	0615-ZET-GT-REP-000-000001
34	Ground Investigation Noise Risk Assessment	1MC05-ALJ-EV-REP-C001-600001
35	Alcohol and Drug Policy	1MC05-ALJ-HS-POL-C001-000002
36	ALIGN Health and Safety File template	1MC05-ALJ-HS-TEM-C001-000072
37	Mandatory Hearing Protection Policy	1MC05-ALJ-HS-POL-C001-000007
38	Mobile Plant Delivery and Authorised Use Process	1MC05-ALJ-HS-FRM-C001-000563
39	Health, Safety and Wellbeing Plan (Construction Phase) Plan for the Colne Valley Viaduct	1MC05-ALJ-HS-PLN-CS01_CL01-000002
40	Specific Construction Phase Plan - Vent. Shafts	1MC05-ALJ-HS-PLN-CS02_CL04-000001
41	Specific Construction Phase Plan South Portal - Main Compound area	1MC05-ALJ-CL-PLN-C001-000025
