

1MC05 - MWCC - C1 -Chiltern Tunnels and Colne Valley Viaduct

Specific Construction Phase Plan

South Portal - Main Compound area

Document no: 1MC05-ALJ-CL-PLN-C001-000025

Revision	Author	Reviewed by	Approved by	Date approved	Reason for revision
P01	Mick O'Hare / ALIGN Package Leads	Isabelle Lelievre	David Whiteford	07/09/2020	Initial document
C01	Mick O'Hare / ALIGN Package Leads	Isabelle Lelievre	David Whiteford	23/11/2020	General review and 1 st issue to HS2
C02	Kevin Long	Chris Winters	Neil Hancox	09/09/2022	Updates current works
C03	Kevin Long	Muhammad Sufyan	Mick O'Hare	31/01/2024	Update to include Decommissioning BP1/ TPC

Security classification: OFFICIAL

Handling Instructions: N/A

Contents

1	Purpose	1
2	Scope	2
2.1	Work breakdown structure	2
2.2	Key activities	2
2.3	Location	4
3	Compound and welfare facilities	5
4	Description of the works	9
4.1	Decommissioning	9
5	Hazard Profile	11
6	Risk Assessments / Method Statements (RAMS)	13
7	Project team organisation	13
7.1	Simplified Chart	13
7.2	Appointments	14
7.3	Key contacts details	15
7.4	Emergency Response and Incident Management	16
8	Appendices	17
8.1	Reference documents	17

1 Purpose

This document is intended to provide specific information related to South Portal - Main Compound area {including Pre-cast, logistics and Earthworks - Package 2 (Design)}.

It shall be read in conjunction with the overall plans:

- Safety, Health and Wellbeing Management (Construction Phase) Plan - Document no.: 1MC05-ALJ-HS-PLN-C001-000006
- The Health Management Plan - Document no.: 1MC05-ALJ-HS-PLN-C001-000003

A Safety, Health and Wellbeing Management (Construction Phase) Plan – Quick Reference Guide for ALIGN JV Managers and Supply Chain is available on Business Collaborator - Document no.: 1MC05-ALJ-HS-PRE-C001-000001. It is regularly updated and present the key H&S requirements on HS2 C1.


This document shall be updated as often as necessary, in compliance with the CDM Assurance process, following changes in the scope of works or in the organisation and communicated to all persons involved in its implementation within HS2 C1 under ALIGN JV (Principal Contractor).

Refer to ALIGN Mobilisation and Construction Commencement: CDM Assurance Process - Document no.: 1MC05-ALJ-HS-PRO-C001-000034.

It replaces the Construction Phase Plan Stage 1 Planned Works Document no: 1MC05-ALJ-CL-PLN-C001-000005.

2 Scope

2.1 Work breakdown structure

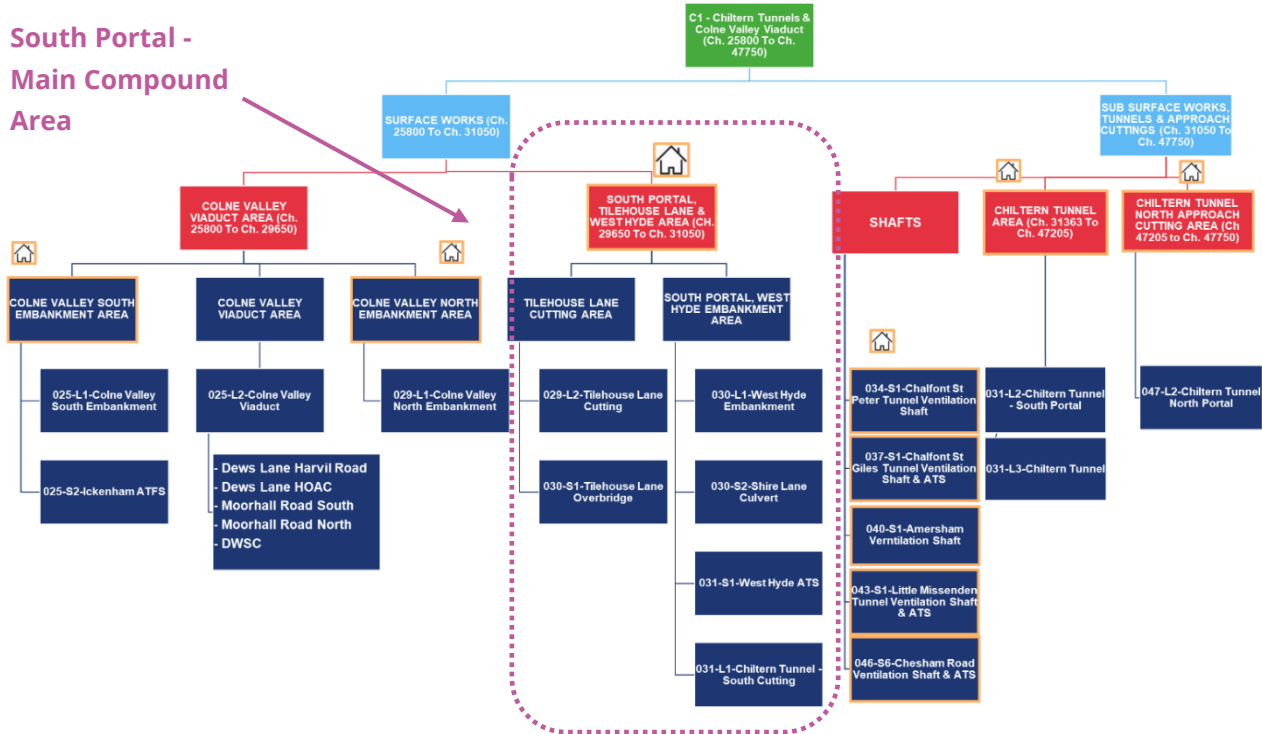

This Work breakdown structure is extracted from the 1MC05 Construction Management Plan – Stage 2 Works Document no: 1MC05-ALJ-CL-PLN-C001-000027.

2.2 Key activities


Key activities undertaken are:

- Earthworks
- Chalk Cake Placement Haul Road Installation
- Stockpile and Concrete Crushing
- Pugmill Operations
- Electrical Assets
- Concrete Production
- BP1 Decommission
 - Mobilisation of Operation Team
 - Electrical Decommissioning
 - Mechanical Decommissioning
 - Removal


- Radial Conveyor & Hopper
 - Water Tanks & Fuel Tanks
 - Fibre Dispenser system
 - Cladding
 - Aggregate Bins
 - Incline Conveyor
 - Screws
 - Plant Towers
 - Generator & Fuel Tank
 - Control Cabin
 - Silo Staircase
 - Silos and Platforms
 - Ancillary items
- Demobilisation from Site
- Tunnel Precast factory Removal
 - Removal of C1 + C2 flying buckets and running rails between the 2 factories & BP1.
 - Pre-Storage 2 Decommissioning
 - Carousel 2 Decommissioning
 - Pre-Storage 1 Decommissioning
 - Carousel 1 Decommissioning
 - Boiler Room 1 & 2 Decommissioning

2.3 Location

The South Portal – Main Compound area is located in Chalfont Lane, WD3 9XN.

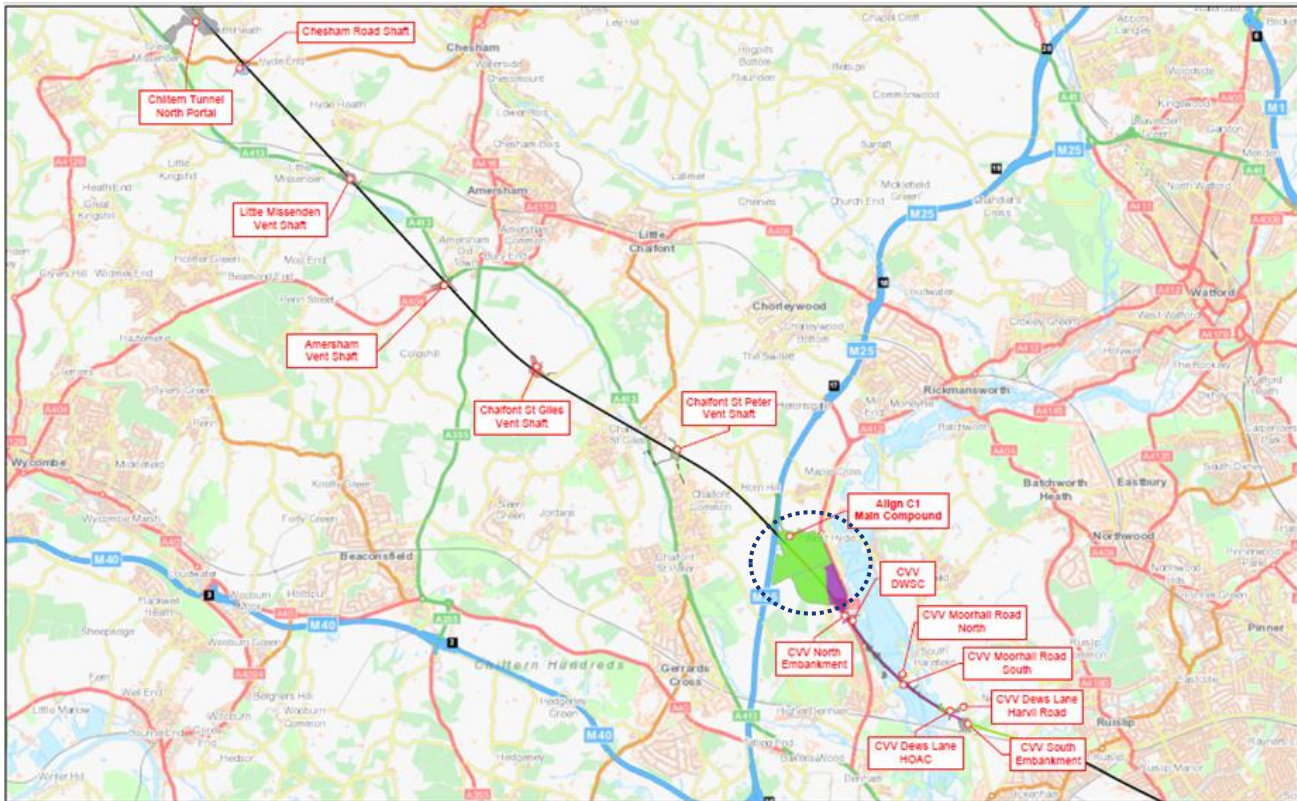

3 Compound and welfare facilities

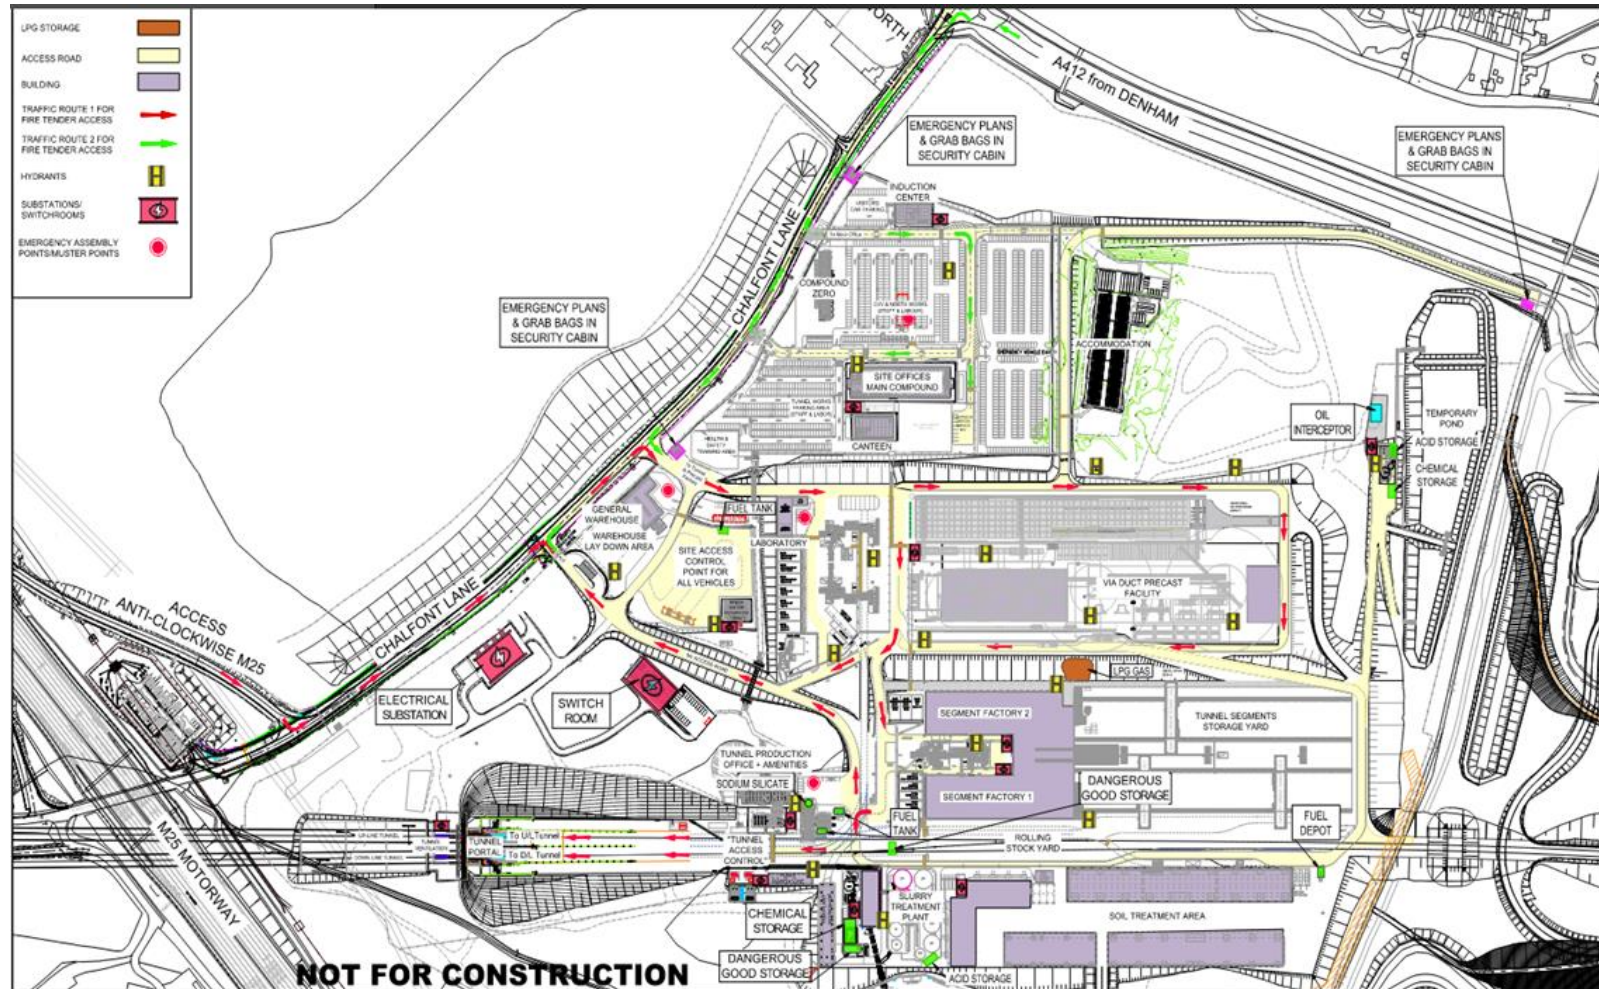

Main buildings are:	Main buildings continued:
• Compound Zero • Main Compound Site offices • Canteen • Tunnel Offices • General Warehouse • Public Engagement and Induction centre • Health and Safety Training Facilities • Overnight Accommodation 1 and 2 • Wellbeing Facilities including Gym • Batching plant 1,2,3 and Tarmac Office • Tunnel Pre-Cast Segment Factory 1, 2 and Storage Yard • Slurry Treatment Plant and Water Treatment Plant • Tunnel Laundry Facilities • Landscape Pods • SOCOTEC Concrete Labs	• General Laundry Facilities (Next to Compound Zero) • New WTP upgrade to existing structure

Refer to South Portal Construction Logistics Plan Document no: 1MC05-ALJ-CL-PLN-CS02_CL03-000001, which focuses specifically on on-site construction logistics, the supply chain and how their impact on the road network can be reduced and managed on site. Also refer to Working Area Security Plan South Portal Earth Works Document no: 1MC05-ALJ-SC-PLN-C001-000013.

Compounds have been designed taking into account the number of workforce personnel and the location, as shown below:

Compound Ref.	Compound Reference Name	Start Date Operations Date	End Date Operations Date	No. of Staff	No. of Align-D Staff	No. of HS2 Staff	Total No. of Staff	No. of Staff (+10%)	No. of Labourers at Peak from Workforce Breakdown	No. of Labourers at Peak
0210/07	Main Compound	27-Mar-20	02-Jan-25	250	10	30	290	319	553	581
0210/08	Chiltern Tunnel Main Compound	27-Mar-20	02-Jan-25	150	0	20	170	187	604	634
0210/07	Batching plant 2&3 pod	13-Mar-20	31-Jul-23	5	0	0	5	6	20	21
0210/07	Viaduct precast yard pod	06-Oct-20	19-Sep-23	10	0	0	10	11	160	168
0210/08	Slurry Treatment Plant pod	26-Nov-23	17-Apr-24	5	0	0	5	6	15	16
0210/08	Tunnel Precast yard pod	01-Jul-20	08-Feb-24	5	0	0	5	6	30	32

Offices facilities, common areas and welfares are designed as below. Ratio for Female/Male percentage is estimated 5% for the workforce, 30% for the office staff.

		Site Amenities Bill of Quantities																																									
		Offices Facilities										Common Areas				Canteen		Canteen & Offices Welfare				Washblock/Changing Welfare																					
		Bespoke Offices Comments										Large Kitchen / Seated area Small Kitchen / Seated area Faith room Staircases Reception				Large Canteen (900pp / 3 seats) Medium Canteen (600pp / 3 seats) Small Canteen (300pp / 3 seats) Professional Kitchen		Off. Disabled Toilet Off. Small Fem. toilet room Off. Large Fem. toilet room Off. Small Male Toilet room Off. Large Male Toilet room				Store Rooms Off. Multicultural Toilet Wd. Small female toilet Wd. Large female toilet Wd. Small Male Toilet Wd. Large Male Toilet Female Shower rooms Male Shower rooms Female lockers Male lockers Entrance lobby																					
Designation																																											
Enabling works offices and welfare facilities		35	-	3	-	1	-	-	1	-	Proj Dir, HS2 Ops, HR, Security (2*), IT server (2*), Mothering recovering room, Safety (PPE), Printers (4*7.5m2), Hot desk area (30pp/30m2)										1	-	-	1	-	-	1	-	1	-	2	cubicles 2 toilets	1	-	-	1	-	-	2	cubicles 2 toilets			
CVV Main Compound Main offices		290	5	12	5	-	1	10	2	13	Proj Dir, HS2 Ops, HR, Security (2*), IT server (2*), Mothering recovering room, Safety (PPE), Printers (4*7.5m2), Hot desk area (30pp/30m2)										1	4	1	4	-	-	-	-	4	2	-	-	-	-	-	-	-	-	-	-			
CVV Main Compound Washblock Changing facilities		-	-	-	-	-	-	-	-	-	Proj Dir, HS2 Ops, HR, Security (2*), IT server (2*), Mothering recovering room, Safety (PPE), Printers (4*7.5m2), Hot desk area (30pp/30m2)										-	-	1	-	-	-	-	-	-	-	-	2	480	68	4	2	6	-	2	-	2		
OPTION CVV Main Compound Merged Solution Main offices + Washblock Changing facilities		290	5	12	5	-	1	10	2	13	Proj Dir, HS2 Ops, HR, Security (2*), IT server (2*), Mothering recovering room, Safety (PPE), Printers (4*7.5m2), Hot desk area (30pp/30m2)										1	4	2	4	-	-	-	-	4	2	2	480	68	4	2	6	-	2	-	2			
CVV Main Compound Canteen - Option 1		-	-	-	-	-	-	-	-	-	-										1	-	-	1	-	1	3	-	2	-	1	-	-	-	-	-	-	-	-	-	-		
CVV Main Compound Canteen - Option 2		-	-	-	-	-	-	-	-	-	-										1	-	-	1	-	2	-	1	-	1	-	-	-	-	-	-	-	-	-	-	-		
Visitor/information center & Induction/Training center		5	-	2	-	-	2	-	-	2	Security, Safety (PPE)										1	-	-	-	-	1	-	1	1	-	-	-	-	-	-	-	-	-	-	-	-		
Tunnel Offices & Washblock Changing facilities		130	5	5	2	-	1	5	2	2	IT server, Safety (PPE)										1	6	1	-	-	-	-	2	1	-	2	2	2	637	73	3	2	4	-	1	1	2	2
Tunnel Offices Canteen - Option 2		130	5	5	2	-	1	5	2	2	IT server, Safety (PPE)										1	6	1	-	-	1	1	-	-	3	2	2	637	73	3	2	7	-	2	-	2	2	
Slurry Treatment Plant pod		5	-	-	-	-	-	-	-	-	-										-	-	-	1	-	-	-	1	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Tunnel Precast yard pod		5	1	-	-	1	-	-	-	-	-										-	-	-	1	-	-	-	1	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Batching plant 2&3 pod		5	-	-	-	-	-	-	-	-	-										-	-	-	1	-	-	-	1	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Viaduct precast yard pod		10	1	-	-	1	-	-	-	-	-										-	-	-	1	1	-	-	-	-	3	-	1	-	-	-	-	-	-	-	-	-	-	

4 Description of the works

Refer to [section 2](#) for the Work breakdown structure and key activities. A 3-Week Look ahead Working Programme is communicated weekly.

The key hazards and control measures are described in the related Hazard Profile. [Refer to section 5.](#)

Activities are DETAILED in the related RAMS. [Refer to section 6.](#)

The related Design Risk Register for the works is the CDM Risk Register - Package 2 Document no: 1MC05-ALJ-HS-REG-CS02-200156.

4.1 Decommissioning

The Decommissioning of Batching Plant 1 will be based on the Disassembly Sequence issued by Tarmac, document "Disassembly Sequence Chiltern Tunnel South Portal Batching Plant BP01 – HS2 BD_DR_GEN_010 P1". This works will be assisted by the Tarmac "Decommissioning Phase Plan".

The Decommissioning of the Tunnel Precast Factories 1 & 2 will be based on the Disassembly Sequence issued by David Andrews (ALIGN), document "Tunnel Precast Factory Planning - Demobilisation. Rev. 1".

Programme of Works:

#	Description of Works	Date
[1]	Flying Hopper Rails & Bucket - Removal	22/01/2024 ~ 26/01/2024
[2]	Mobilisation	01/02/2024
[3]	Electrical Decommissioning	08/02/2024
[4]	Mechanical Decommissioning	10/02/2024
[5]	Radial Conveyor & Hopper - Removal	10/02/2024
[6]	Fibre Dispenser system - Removal	29/02/2024
[7]	Cladding - Removal	19/02/2024
[8]	Aggregate Bins - Removal	05/03/2024
[9]	Incline Conveyor - Removal	10/04/2024
[10]	Screws - Removal	20/04/2024
[11]	Plant Towers - Removal	21/04/2024

Site Layout

NOT FOR CONSTRUCTION

5 Hazard Profile

Activity	Specialist Sub-Contractor	Key Hazards	Principal Control Measures
Temporary Works			
Western Valley Slope Temporary Drainage	Align	Underground Services Plant and People Interface	Safe System of Work Permit to Dig Segregation
Pugmill Activities	Align	Working at Height Dust	POWRA Plant Operator Edge Protection Face Fit Testing
Haul roads installation and Bulk fill works	Align / D&M	Plant and People Interface Overturned Plant Dust	Segregation Road bunds, speed limit Water suppression
Material Movement	Align / D&M	Plant and People Interface Overturned Plant Sinking Plant	Logistical Plant Planning Separate Haul Road for ADT's Road Scraping
Soil Stabilisation	SSM	Dust Contact with other Plant	Safe System of Work Dust suppression
Stockpiling	Align	Risk of Plant Overturn Risk of Material Falling	Stockpile inspections SSOW
Field Trials	Align D&M	Plant Movement Underground Services	SSOW Permit to dig
Permanent Works			
Security	OCS Group	Protestors Trespassers	24/7 Security Operation CCTV ID Restricted Access
Laundry Facilities	Select	Working at height Electricity	SSOW LOTO (Lock out tag out) system

Activity	Specialist Sub-Contractor	Key Hazards	Principal Control Measures
Concrete Production	Tarmac	Pressure systems Vehicle Movement	Safe systems of Works Maintenance procedures Design Plant LOTOTO
Concrete Labs	Socotec	Noise, Vibration, Dust Chemicals Manual Handling	Safety Procedures Monitoring Mechanical Aids
Warehouse and Yard	Align	Falling Material Plant and People interface	SEMA Inspection/ internal Segregation by colour coded
Logistic Holding area	Align, Servest	People and vehicle interface Collision	SSOW Traffic Management plan Segregation
Vehicle Maintenance and Cleaning Facilities	Align	Spills, Crush injuries, Overinflation	Emergency Procedures Spill kit training SSOW
CVV Mock-up and Pre-cast area	Kilnbridge	Working at height Chemical burns	SSOW Approve lift Plan, COSHH Assessment
Tunnel Precast Factory	Align, VGC, Danny Sullivan,TGT	Lifting of equipment. Moving machinery.	Approved lift plan. Barriers & enclosures Segregation
Utilities: Electrical IT Network Water Network	PBE Various Instalcom	Work at Height Underground hazard	SSOW POWRA Permit to dig
Soil Treatment area	D&M	People plant Interface Plant collision	SSOW People Plant Segregation Dust suppression
Electrical Assets	PBE & Ryan Williams		LOTO SSOW
Thames Water Sewer Diversion	Instalcome	Underground services Confined Space	Permit to work system

Activity	Specialist Sub-Contractor	Key Hazards	Principal Control Measures
Tilehouse Lane Overbridge & Shire Lane Culvert	Volker Fitzpatrick	Foundation cutting stability	Monitoring points will be installed, and the foundation cutting will be monitored on regular intervals.
Decommissioning			
Batching Plant – Decommissioning	Tarmac	Working at Height Lifting People Plant Interface Access/Egress Cold Weather	Safe Systems of Work POWRA Approved Lift Plans Permits to Load Segregation
Tunnel Precast Factory – Decommissioning	Align	Working at Height Lifting People Plant Interface Access/Egress Cold Weather	Safe Systems of Work POWRA Approved Lift Plans Permits to Load Segregation

6 Risk Assessments / Method Statements (RAMS)

A schedule of current and forthcoming Risk Assessments and the required Method Statements (RAMS) for principal activities will be maintained within Business Collaborator (BC) and kept up to date by The Project Manager and the team responsible for the work. Pre-Construction information, including residual risks from the Design Risk Register is incorporated.


South Portal RAMS Schedule Document no.: 1MC05-ALJ-QY-SCH-CS02_CL03-00001

7 Project team organisation

Detailed organisational charts for HS2 C1 are regularly updated and available on the digital screens on site and on Business Collaborator.

7.1 Simplified Chart

Specific detailed chart related to the scope of works may be included in the appendices.

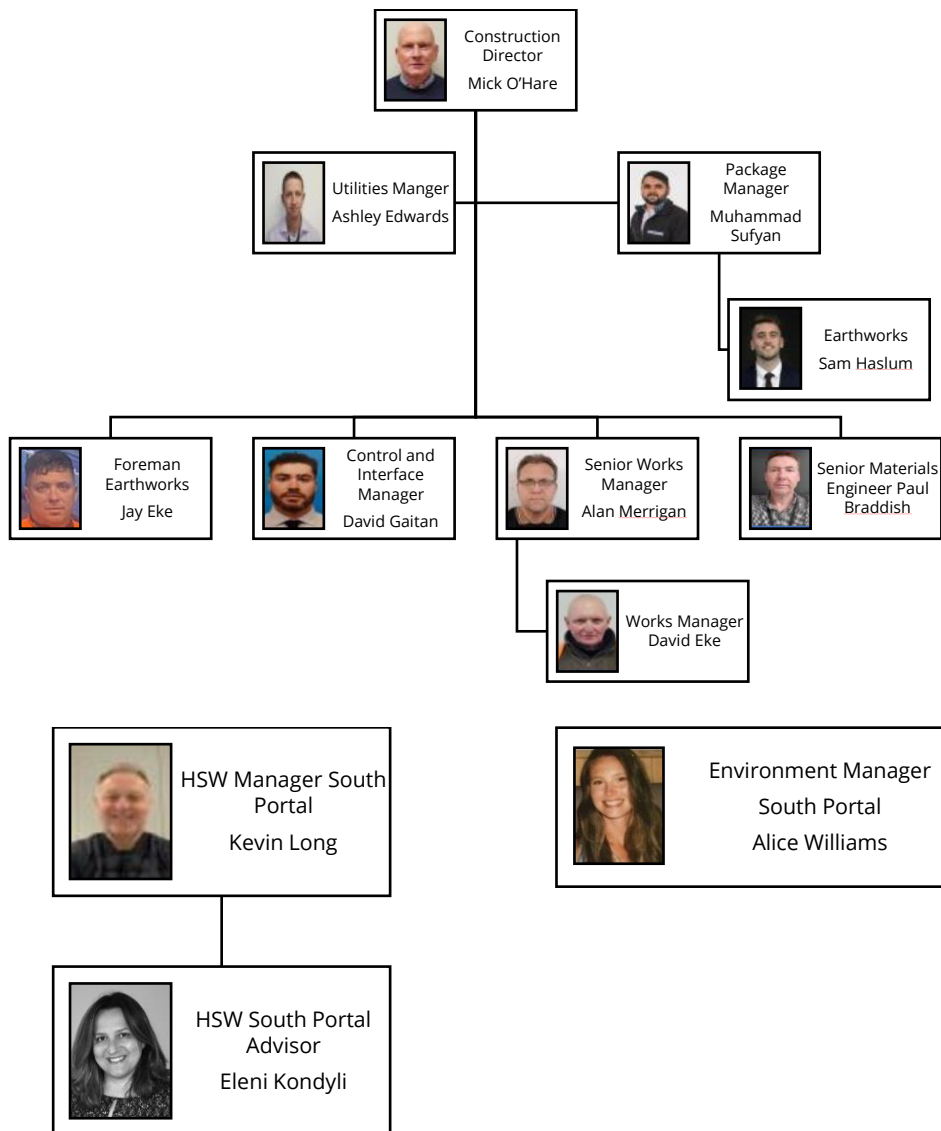

7.2 Appointments

It falls on the Project Manager's responsibility to appoint people in due time and update the Appointed Person (AP) Register as often as necessary.

Appointments are to be done for:

- First Aiders / Fire Marshall
- Emergency and Rescue Team including Incident Management

- Temporary Works Designer (TWD) / Temporary Works Coordinator (TWC) / Area Temporary Works Coordinator (ATWC) / Temporary Works Supervisor (TWS)
- Lifting Operations (Appointed Person - Lifting, Lifting Supervisor, Deputy Lifting Supervisor, Lift Planner, Deputy Lift Planner, Crane Co-ordinator).
- Electrical / Hot works / Confined Space / Mechanical
- Excavations – “Permit to Break Ground”
- Traffic and Access Management
- COSHH Controller
- Authorised Person “Permit to Clear”
- Authorised Person “Permit to Work Near Overhead Utilities and Cross Buried Utilities”

Appointed Persons (AP) Register - South Portal Document no.: 1MC05-ALJ-HS-REG-C001-000004

7.3 Key contacts details

Name	Role	Phone number
Mick O'Hare	Construction Director South Portal	07384 234480
Muhammad Sufyan	Package Manager	07392 134086
David Eke	Works Manager South Portal	07747 765753
Alan Merrigan	Senior Works Manager	07876 876135
Lee Taylor	Security Manager	07943 079367
Alice Williams	Environment Manager	07393 765932
Alex Gaston	Quality Advisor	07833 439267
Kevin Long	Health and Safety Manager	07833 289254
Eleni Kondyli	Health and Safety Advisor	07826 992966
For Decommissioning		
David Andrews	ALIGN Tunnel Precast Manager	07341501134
Gary Russon	ALIGN Works Manager	07867416303
Carl Murphy	Tarmac Senior Project Manager	07590780740
Jonathan Cockerline	Tarmac Regional HSE Manager	07483142045
Alex Harris	Tarmac Subcontractor – Bulldog Project Manager	

7.4 Emergency Response and Incident Management

The Emergency Response and Incident Management is being organised as below:

- Overarching Emergency Response and Incident Management Plan
 - Set out guide to expected incidents and the general response
 - Contract wide response
 - Key Personnel at contract level
 - Key contacts for services etc.
- Work Site Emergency Response and Incident Management Plan
 - Details the worksite specific emergency response plan
 - Details key response procedures
 - Developed as risk / activities change
 - Location maps
 - Key Personnel for the site

Refer to

C1 Emergency Response and Incident Management Plan	1MC05-ALJ-HS-PLN-C001-000041
South Portal Emergency Response and Incident Management Plan	1MC05-ALJ-HS-PLN-CS02_CL03-000003

Refer to the Incident Management Diagram (notification time, communication method, actions)
- in Appendix 8.0.

8 Appendices

8.1 Reference documents

#	Document Title	Reference
1	Safety, Health and Wellbeing Management (Construction Phase) Plan	1MC05-ALJ-HS-PLN-C001-000006
2	Health Management Plan	1MC05-ALJ-HS-PLN-C001-000003
3	Site Emergency Preparedness and Response Plan	1MC05-ALJ-HS-PLN-C001-000032
4	Incident Management Plan	1MC05-ALJ-HS-PLN-C001-000041
5	Safety, Health and Wellbeing Management (Construction Phase) Plan -Quick Reference Guide for ALIGN JV Managers and Supply Chain-	1MC05-ALJ-HS-PRE-C001-000001
6	ALIGN Mobilisation and Construction Commencement: CDM Assurance Process	1MC05-ALJ-HS-PRO-C001-000034
7	South Portal Construction Logistics Plan	1MC05-ALJ-CL-PLN-CS02_CL03-000001.
8	Working Area Security Plan South Portal Earth Works	1MC05-ALJ-SC-PLN-C001-000013
9	CDM Risk Register - Package 2	1MC05-ALJ-HS-REG-CS02-200156
10	South Portal RAMS Schedule	1MC05-ALJ-QY-SCH-CS02_CL03-000012
11	Appointed Persons (AP) Register - South Portal	1MC05-ALJ-HS-REG-C001-000004
