

# Supply Chain Summit

## 19 June 2025



# Agenda

- Introduction – Coralie Peroux
- Ice Breaker – John Simon Neal
- HS2 Reset Update – Billy Ahluwalia
- The Unexpected Event – Alan Swann
- Comms and Engagement Strategy – Laura Roberts
- Completion Strategy – Richard Thomas
- Occupational Health – Melody Gilbert
- 5 minute Stretch and Flex
- SPIP2 – Derek van Rensburg
- Closure
- Lunch

# **Welcome Introduction – Coralie Peroux**

# **Icebreaker – John Simon Neal**

# **The Unexpected Event – Alan Swann**

# THE UNEXPECTED EVENT

Thursday, 19th June 2025



# THE FREE LESSON



# OUR PEOPLE




# SEE SOMETHING, SAY SOMETHING



# BACK 'THE' BASICS



# TALES OF THE UNEXPECTED

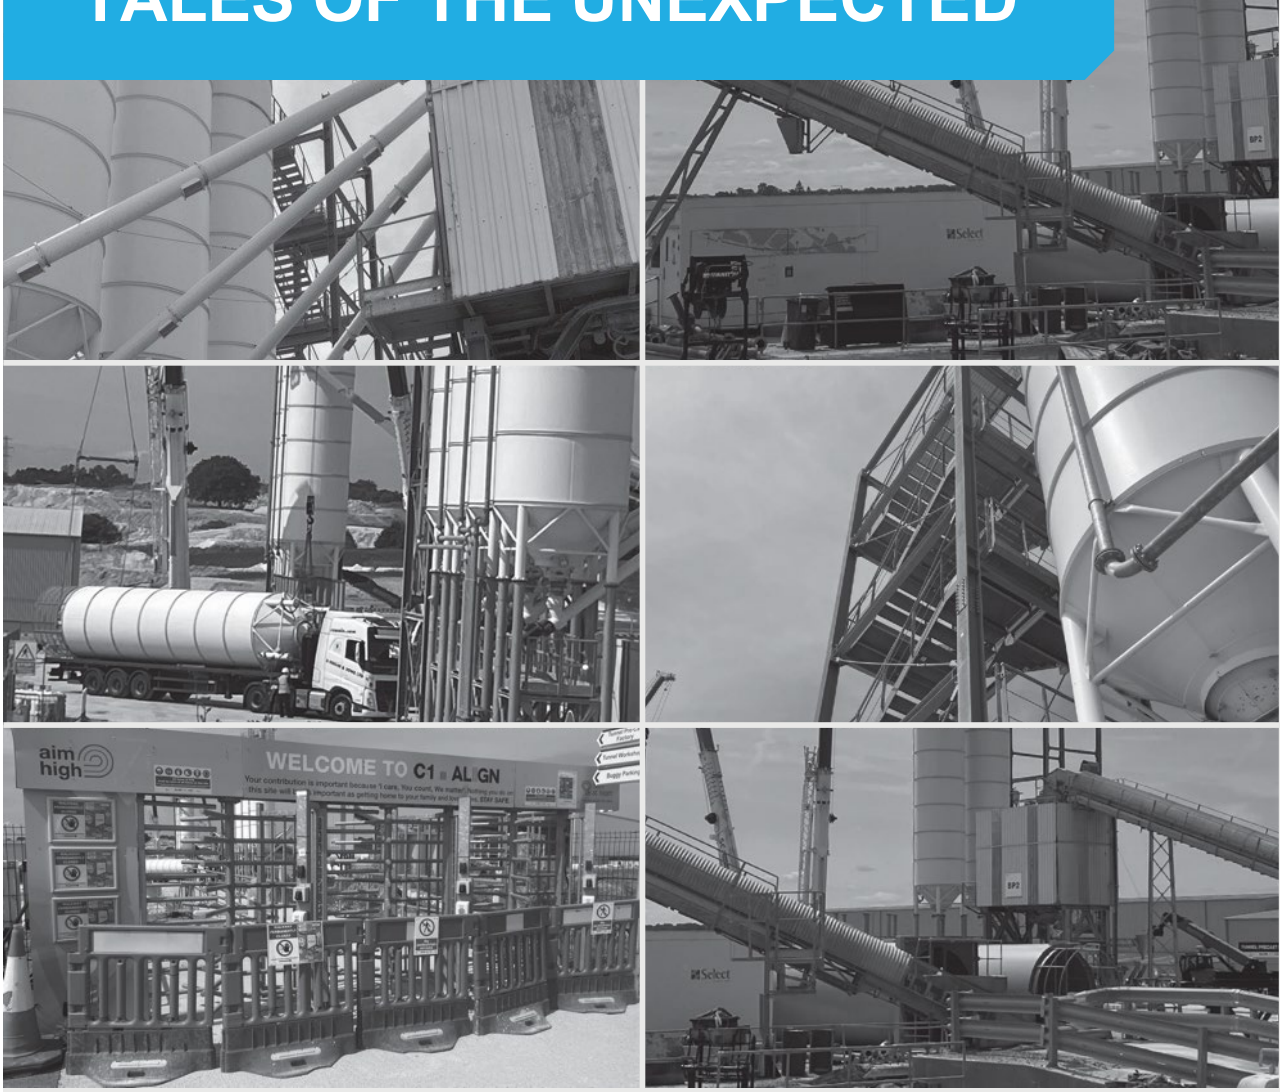

# **HS2 Reset Update – Billy Ahluwalia**



# The reset

# What is the reset?

- We are resetting the HS2 programme to **break the cycle of cost increases and schedule delays.**
- The reset will:
  - provide a realistic and achievable cost and schedule;
  - put activity across the route into the correct sequence;
  - set the core railway for initial services;
  - reshape our commercial relationships with contractors; and
  - make sure HS2 Ltd is set up to deliver the programme and works well with government.
- It will allow us to **deliver HS2 on time and on budget for the lowest reasonable cost.**
- It's a major task of unique size and complexity, but it isn't an end in itself – **the reset is critical to unlocking the prize offered by HS2: economic growth and better rail journeys.**



HS2

# The four taskforces delivering reset

- We've set up **four reset taskforces** to look at the key areas:
  - **One – the programme taskforce** is developing a new cost and schedule, and revised delivery strategy. It is looking at the best way to deliver the opening railway between Birmingham and Old Oak Common, west London.
  - **Two – the supply chain taskforce** is seeking a better deal with our main works contractors. The new deal must boost productivity, control cost, and provide value for taxpayers and industry.
  - **Three – the company taskforce** is looking at ways to make us more efficient, less bureaucratic and leaner – focused on performance and outcomes rather than processes.
  - **Four – the government taskforce** is focusing on improving our relationship with the Department for Transport (DfT) and wider government, ensuring there is mutual trust and transparency and that we work towards a shared goal.

# Reset stages

- **Stage One** has been completed – the initial assessment of cost and schedule, our commercial arrangements and our organisation.
- **Stage Two** will be completed in the summer. This is when we will confirm with government our approaches and timelines for the reset.
- **Stage Three** by the end of autumn will establish realistic plans and strategies to deliver the new programme. We will also have outlines of how to reflect this revised delivery strategy in our ways of working and set-up. Timeline for
- The entry and exit criteria for **Stage Four and Stage Five** in Spring 2026 will be confirmed at the end of Stage Two.



2025/26

# Our priorities

## Improving **controls**

Strengthening our decision-making and reporting lines for better financial control, risk management and performance monitoring.

## Boosting **safety** and **productivity**

Working safely and boosting productivity in 2025/26 so we can prove to government that we can keep the programme on schedule.

## Delivering the **reset**

Providing recommendations to government on the programme and the supply chain, including an achievable cost and schedule.

**HS2**



# What we'll gain from the **three priorities**

- Create a **clear, realistic budget and timeline** for HS2 that the government supports.
- Show we can **safely control the programme**, prove our competence and build trust.
- **Rebuild our relationship with suppliers** to work together efficiently with shared goals.
- Make our organisation **less bureaucratic**, quicker at making decisions and more focused on what matters.
- **Confidence in our ability to deliver** a high-speed railway that sets the standard of a modern rail network, boosting growth and benefiting passengers.

**HS2**

# **Comms and Engagement Strategy – Laura Roberts**

# Communication Strategy

Our goal/objective:

Re-gain control of the narrative through:

- Improved understanding of the completion/construction milestones/caretaking process
- Elevate confusion and minimize noise by being as transparent as possible
- One voice
- Continue to support safety improvement plans/actions
- More timely recognition – celebrate all the wins
- Encouraging everyone to ask questions



# C1 Align Internal Communication Channels



**C1 Align Team Update**  
Monthly  
Face to face with online element

18 June: Handover update




**Black Hat Forum**  
Monthly  
Face to face



**Supply Chain Directors Forum**  
Monthly  
Face to face



**New: Coffee and conversations**  
Bi-weekly  
Face to face

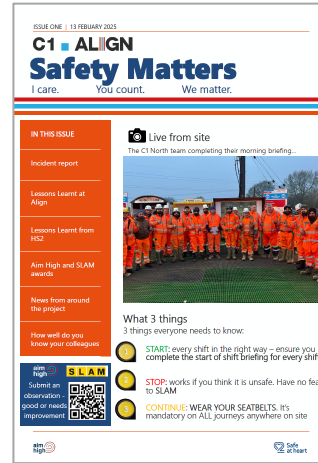

**Safety Matters**  
Bi-Weekly  
Email & Print




**ExCo tour**  
Monthly  
Face to face




**C1 Align emails**  
As required  
Email



**HS2 News**  
Quarterly  
Print



**Digital screens & AlignTV**  
Weekly  
Online






# External Comms



Alignjv.com



Awards

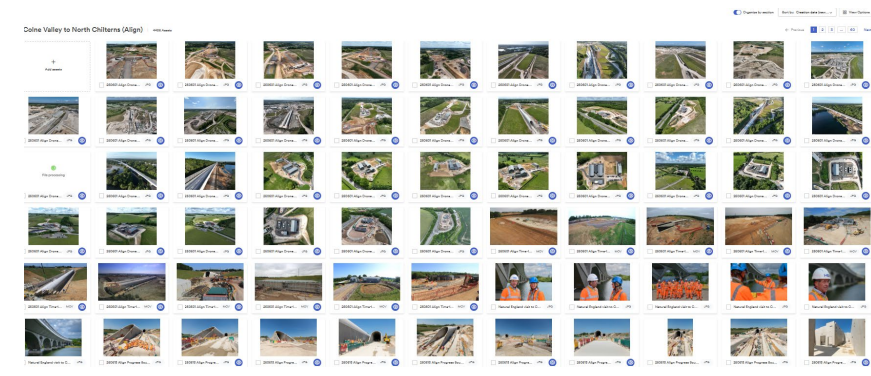

Approved images

# Over to you...

- Our ask: Please share success stories and recognition – we want to amplify these!
- What is your ask? Are we missing anything? What other information do you want?



# **Completion Strategy – Richard Thomas**

# Completion



Time to gradually hand over  
our assets after all the great  
work we've done

# What & When are the Handover Key Dates?

Overall  
completion  
September  
2027

| Handover Key Date/<br>Key Date | Key Date Scope (Contract)                                                      | Planned completion<br>(as of June 2025) |
|--------------------------------|--------------------------------------------------------------------------------|-----------------------------------------|
| HKD 07                         | Chiltern Tunnels (incl. South Portal structure, 'Trace' 30+350 to Portal)      | 24/07/2025                              |
| HKD 04 (incl. HKD 2)           | Colne Valley Viaduct (incl. South & North embankment, ATFS, 'Trace' to 30+350) | 13/08/2025                              |
| HKD 03                         | Chalfont St. Giles Ventilation Shaft                                           | 05/11/2025                              |
| HKD 05                         | Amersham Ventilation Shaft                                                     | 09/12/2025                              |
| HKD 01                         | Chalfont St. Peter Ventilation Shaft                                           | 24/12/2025                              |
| HKD 06 (incl. HKD 9)           | Little Missenden Shaft<br>Chesham Road Ventilation Shaft                       | 23/01/2026                              |
| HKD 08                         | North Portal and completed demobilisation of the Main Compound                 | 18/05/2026                              |



# Achieving an HKD

C1 Align defines the achievement of a Handover Key Date, as the completion of the constructed asset.

In addition to completing the constructed asset, we provide the “Red List” of deliverable evidence.

This information provides the opportunity for a Principal Contractor transfer of the HKD defined area.



**Handover  
Team**

## **Handover Key Date (The Red List)**

Inspection and Test Plans  
Defects Notifications (In Progress)  
U&A Compliance Checklist  
Environmental documentation  
Health and Safety File  
Material Acceptance Forms  
Consents Register  
Assumptions Register  
Departures Register  
Temporary Works - TL3 Certs  
Testing & Commissioning Plan

# What do we do after HKD?

## Production / Quality Teams

### Date + 4 weeks (Quality Complete)

Records of Inspections and Tests  
Configuration Status Report  
Construction Records  
Consolidated Outstanding Works List  
(COWL)  
Defects Notifications (complete)

## Technical Teams

### Date + 12 weeks (Technical Assurance Complete)

Third Party Construction Acceptance  
Survey and Monitoring Records  
Design and Verification Certificate  
Verification and Validation Matrix  
Data Acceptance Certificate  
Systems Safety Status Report  
Asset Info Model  
ICD (Design) - Sector C1  
Factory Acceptance Tests  
O&M Manual  
Testing and Commissioning Records  
Construction Compliance Certificate

= Technical Assurance Completed



# What happens next?

| Item                                | What we know                              | What we don't know                                |
|-------------------------------------|-------------------------------------------|---------------------------------------------------|
| <b>Align's Handover Key Dates</b>   | Physical work complete                    | Rail System mobilisation dates                    |
| <b>Snagging / Documentation</b>     | Continues after HKDs                      |                                                   |
| <b>Caretaking &amp; Maintenance</b> | Someone will have to do it                | Exactly what it will be                           |
| <b>South Portal site</b>            | Some facilities remain (office, car park) | Rail System mobilisation dates                    |
| <b>HS2 cost audits</b>              | Ongoing currently                         | Full extent of queries                            |
| <b>South Heath works</b>            | Completion Sept 2027                      |                                                   |
| <b>Caretaking</b>                   | Someone will have to do it                | Exactly what it will be (but, we have an idea...) |



# Caretaking and Maintenance likely scope

- Security
- Maintaining office facility
- General reactive site maintenance
- Environmental maintenance
- Water Treatment Plant
- Tunnel and Shaft safety systems
- Water monitoring


# **Occupational Health – Melody Gilbert**

# Why Health Matters

Melodie Gilbert

Align Occupational Health Lead

# What are we talking about?



# What are we talking about?

## Our Primary workplace health risks

- Dust and respiratory exposures
- Noise
- Vibration
- Manual Handling



These are outlined in our health hazard profiles



# Why are we talking about this?

- 13,000 people a year die from Occupational Disease (caused by exposure at work)
- Equivalent to more than capacity at Cardiff arms park or the population of Chorley Wood.....


And long term health conditions?

- 12,000 with work related hearing problems
- 543,000 suffering from Musculoskeletal disorders
- 450 new HAVS cases



# Why are we talking about this?

- Over 5000 occupational cancer cases arise each year as a result of past exposures in the construction sector.
- In 2023 The construction sector reported around **2.6 million working days lost**
  - 20% due to workplace injury
  - **80% due to work-related illness**

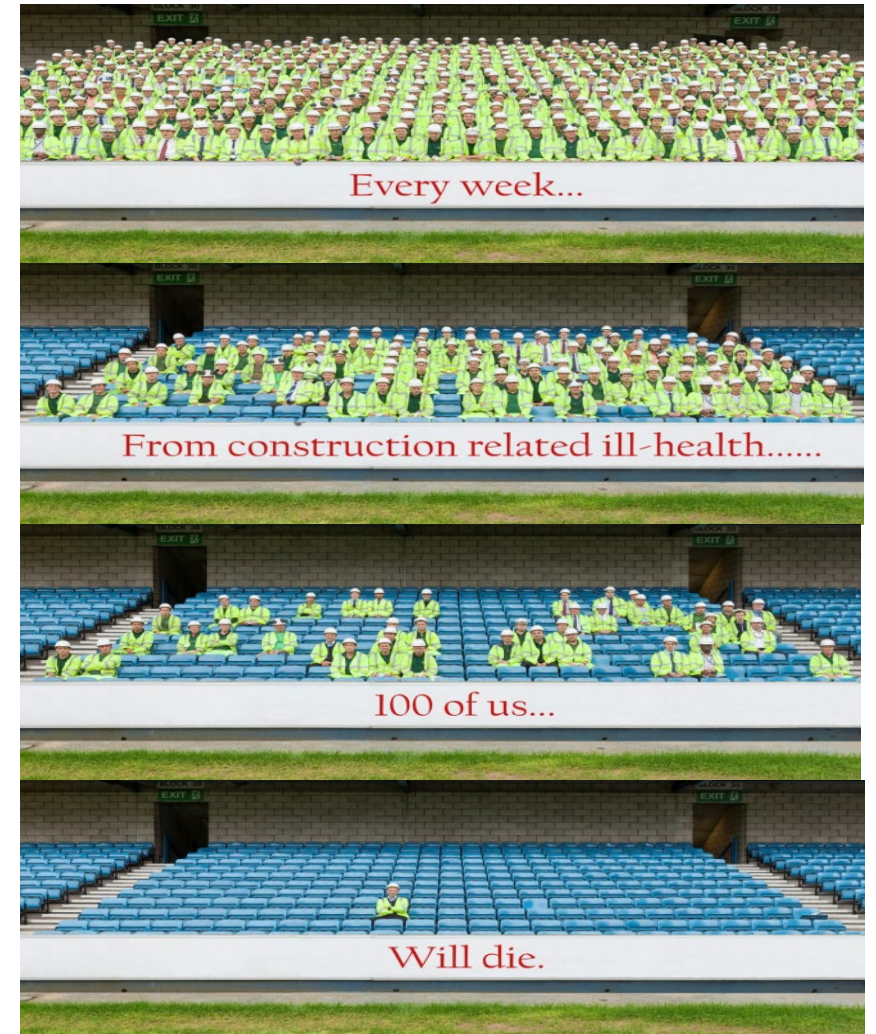

# The Challenge of Health

- Health perceived as *difficult* compared with other management topics
  - Latency - causes not obvious
  - Interventions not perceived as easy
  - Reasons
    - Lack of *information*
    - Lack of *knowledge* – domain of doctors and nurses
- Positive outcome not *immediately* obvious
- ‘the slow accident’



# Asking the WHY Question



# Why are we talking to you?



What shadow will you cast?



# Making Health MATTER at Align

- **'Ill-health can be prevented'** - health hazard profiles
- **'Treat health like safety'** - health incident recording
- **'Everyone has a role to play'** - clear guidance and training at all levels
- **'Control the risk, not the symptoms'** - exposure matters - look for ways to remove it
- **'Manage risk, not lifestyles'** - not just safety critical medicals but health surveillance



## **5 minutes - Stretch & Flex**

## **SPIP2 - Derek van Rensburg**

# **Align Supply Chain Summit**

## Safety Performance Improvement Plan I.2



# (1) Align Project Team Re-structure (Leadership)

**Action owner** – Coralie Peroux      **Action Group** – Coralie Peroux, Derek Van Rensburg, Steve Meecham, Melissa Solano, David Andrews, Neil Hancox

| Actions to be applied*                                                                                                                                                            | Time frame |     |     |     |     |     |
|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------|-----|-----|-----|-----|-----|
|                                                                                                                                                                                   | Jan        | Feb | Mar | Apr | May | Jun |
| PIP action plan completion                                                                                                                                                        |            |     |     |     |     |     |
| Internal review of Delivery and H&S Team structures including review on all process and procedures to identify improvements needed - action report to be produced and implemented |            |     |     |     |     |     |
| Appointment of alternative Align Project Director                                                                                                                                 |            |     |     |     |     |     |

**Notes** - To re-structure the existing Leadership Team - Review the roles and responsibilities of the EXCO function to ensure continued effective project leadership.

To review the existing Delivery and HS&W teams org charts to ensure teams have appropriate resources to deliver their targets / Re-structure as required the leadership functions / Determine roles and responsibilities to ensure clear line management structure.

## Progress tracker -

- Align JV Project Director change implemented January '25
- HSW resource supplemented by return of HSW Director and support from JV Parent Company Senior HSW Professional
- Review of management systems, digitised tools, and implementation in progress with enhancements to internal assurance team in progress. PIP Plan presented, formerly issued and in progress



## (2) Utilise the data available to drive safety management (Leadership)

Action owner – Neil Hancox Action Group – Safety Team, Derek Van Rensburg, Steve Meecham, John Aberra

| Actions to be applied*                                                                  | Timeframe |     |     |     |     |     |
|-----------------------------------------------------------------------------------------|-----------|-----|-----|-----|-----|-----|
|                                                                                         | Jan       | Feb | Mar | Apr | May | Jun |
| Review AIMHIGH application so that it feeds into risks and hazards that can be trended. |           |     |     |     |     |     |
| Ensure all safety data is available and signposted to production teams                  |           |     |     |     |     |     |
| Provide system training to new joiners alongside refresher training                     |           |     |     |     |     |     |
| Identify resources required to analyse and treat data. Commission those resources.      |           |     |     |     |     |     |
| Update Dalux workflow with re-structured org charts                                     |           |     |     |     |     |     |

**Notes** – Optimise H&S data utilisation (Aim High, Dalux, POWRA, LAMBO,...) to identify trends and adapt quickly our H&S strategy to current concerns from the site teams. Identify quicker any new trend in an area or across the project for targeted actions. Communicate on it in a “you said, we did” spirit.

### Progress Tracker -

- Aim High change proposal submitted and reviewed. Test run for 3 weeks (till end of Feb-25) and new app deployed beginning of Mar-25.
- Dalux workflows are under review between HSW, Delivery Teams, and the Align JV Digital / BIM Team.
- Support for the HSW team with a proposed enhanced organisation and enhanced training for HSW data team is in progress



# (3) Align Leadership Excellence Seminar (Leadership)

Action owner –John S Neal

Action Group – Align EXCO, Safety Team, Laura Roberts, Production Leaders

| Actions to be applied*                                                                                                | Time frame |     |     |     |     |     |
|-----------------------------------------------------------------------------------------------------------------------|------------|-----|-----|-----|-----|-----|
|                                                                                                                       | Jan        | Feb | Mar | Apr | May | Jun |
| Develop Leadership Excellence seminar and create seminar activities that address cultural and relationship challenges |            |     |     |     |     |     |
| Build a seminar action plan for the team to commit to                                                                 |            |     |     |     |     |     |
| Review action from seminar after 3 months                                                                             |            |     |     |     |     |     |

**Notes** -Leadership seminar to support Senior Works Managers/Engineers/Package Managers/Senior Leaders in project delivery and safety management. 1 day event: Just and Fair Culture to be covered in stand alone session. Safety Team to be included in the event. JV Board and EXCO to attend + Supply Chain rep x 1 from key suppliers

## Progress tracker

- The Denham Grove hotel booked for 2 seminars on Tuesday 4<sup>th</sup> and Wednesday 5<sup>th</sup> March 2025
- Attendee list being drawn up by Derek Van Rensburg and Coralie Peroux
- Seminar schedule determined and session facilitators have been confirmed



# (4) Re-empower the role of senior works managers (Leadership)

Action owner – Derek Van Rensburg

Action Group – Alan Swann, Coralie Peroux, David Andrews, Dean Graham, Steve Meecham, Melissa Solano

| Actions to be applied*                                                                                                                                                     | Timeframe |     |     |     |     |     |
|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------|-----|-----|-----|-----|-----|
|                                                                                                                                                                            | Jan       | Feb | Mar | Apr | May | Jun |
| Determine superintendant group to support actions and mitigation, as well as development of in-depth coordination and management of activities in interface between teams. |           |     |     |     |     |     |
| Provide Mentoring and coaching to the Superintendents (senior works Manager) group                                                                                         |           |     |     |     |     |     |
| Review the existing Blackhat resource to ensure adequate resources for works to be delivered across the project in this changing phase of works.                           |           |     |     |     |     |     |
| Appoint a 3rd party safety advisor to support 'out of hours' and weekend working safety standards                                                                          |           |     |     |     |     |     |

**Notes** – The role of our senior works managers is crucial to the success and safe delivery of our works. Re-emphasize the importance of their role to the wider team and their perimeter of action. They have a strong cultural role in supporting the relationship between leadership strategy and workforce delivery. Building trust and respect amongst the teams is a crucial element of what they do. Direct line of communication with the construction directors.

## Progress tracker –

- Senior Works Managers have been identified and review of their respective teams of senior supervision is completed
- Appoint a Senior Superintendent to lead all SWM on site and drive safety, co-ordination, interfaces, consistency and one team approach across C1 Align and C1 North
- Bi-Weekly SWM meeting established and will be led by Senior Superintendent
- Developed a clear Senior Manager structure for each section of the project that includes correct reporting lines – there needs to be a few organisational changes to empower the SWM and these are in planning at S Portal and Tunnels
- Bespoke Just and Fair culture training to be given to SWM by HR and Safety Directors to enable empower SWM to correctly manage site resources – training is booked for 10th April
- A third-party safety advisor to support out of hours and weekend working standards has been appointed, who has now completed all tunnelling safety entry training.
- Presenting with excellence course to be run for the Senior Superintendent and Senior Works Manager to improve their confidence with presenting to the team – to be run in April
- Bespoke support to be given to each SWM to help them with areas of development that have been identified as development areas through 1-2-1 engagement with the coach. - starting in April



# (5) Review LAMBO / POWRA (Communication)

Action owner – Alan Swann

Action Group – Dean Graham, David Andrews, John S Neal

| Actions to be applied*                                                                        | Timeframe |     |     |     |     |     |
|-----------------------------------------------------------------------------------------------|-----------|-----|-----|-----|-----|-----|
|                                                                                               | Jan       | Feb | Mar | Apr | May | Jun |
| Develop and improve our start of shift briefings (POWRA/SOS)                                  |           |     |     |     |     |     |
| Use LAMBO & data analysis to drive actions and improvements                                   |           |     |     |     |     |     |
| Ensure all language barriers are addressed to ensure total understanding of works requirement |           |     |     |     |     |     |
| Ensure there is a robust shift to shift handover process                                      |           |     |     |     |     |     |

**Notes** – Implement consistency in POWRA delivery across all work areas. Assess start of shift briefing delivery consistency - SURVEY workforce for feedback on briefings - create consistency across project and ensure workforce has a voice. 6 Major risks to be covered regularly.

## Progress tracker –

- Reduction of point of work risk assessment documents i.e Take 5, LOTOTO (Lock Out, Tag Out, Test Out) and SLAM booklets are now designed, printed and distributed.
- Point of work risk assessment training is now being developed with one of Align senior works manager at CVV and a pilot course is to be undertaken on the **18<sup>th</sup> February**. The measurement of all point of work briefing will require an effective and revised **LAMBO**. An Align Construction Manager has arranged a black hat forum open session to consult with all Align black hats at the **end of February**.
- Each point of work risk assessment booklet will be translated into the **9 languages** present on the project and drafts will be available **mid February**.



# (6) Develop HS&W Weekly Bulletin for workforce (Communication)

Action owner – Laura Roberts

Action Group – Derek Van Rensburg, Lisa Lewis, Lisa Bonds, Alan Swann, Rebecca Archer

| Actions to be applied*                                                                                 | Timeframe |     |     |     |     |     |
|--------------------------------------------------------------------------------------------------------|-----------|-----|-----|-----|-----|-----|
|                                                                                                        | Jan       | Feb | Mar | Apr | May | Jun |
| Consult with managers and supervisors on format of communication                                       |           |     |     |     |     |     |
| Prepare sample communication and get feed back                                                         |           |     |     |     |     |     |
| Prepare statement on use of the bulletin and responsibilities for delivery to the work force           |           |     |     |     |     |     |
| Support those using the bulletin to critically analyse the data and to brief as necessary to the teams |           |     |     |     |     |     |
| Put together a draft and submit to EXCO for review and comment                                         |           |     |     |     |     |     |
| Senior Works Managers to review and comment                                                            |           |     |     |     |     |     |
| Present at Black Hat forum for 1st comments                                                            |           |     |     |     |     |     |
| Issue weekly and take comments and feedback from teams to develop                                      |           |     |     |     |     |     |

**Notes** - Develop weekly workforce safety bulletin to communicate existing and emerging safety trends. HS2 wide safety information and other JV safety incidents to be included as required. Produced by Align Comms Team with inputs from Alan Swann and safety/production teams. Produced weekly (forming a comms habit). Delivered by Managers and Supervisors.

## Progress tracker –

- Initial bulletin draft prepared with input from working group
- Meeting arranged with Senior Works Manager's to discuss format
- Attended Align BH forum to introduce bulleting concept and delivery process
- 1st bulletin will be issued 13/02



# (7) Re-commission GMR Human Factors (Culture)

Action owner – Alan Swann

Action Group – GMR Team, David Andrews, Steve Meecham Melissa Solano, Derek Vrensburg

| Actions to be applied*                                                              | Timeframe |     |     |     |     |     |
|-------------------------------------------------------------------------------------|-----------|-----|-----|-----|-----|-----|
|                                                                                     | Jan       | Feb | Mar | Apr | May | Jun |
| GMR to undertake safety audit of tunnelling operations then expand to wider project |           |     |     |     |     |     |
| Engage with GMR safety specialists for technical review of tunnelling activities    |           |     |     |     |     |     |
| Audit will conclude end of Feb 2025                                                 |           |     |     |     |     |     |
| Commence site survey and safety threat workshops through Feb/Mar 2025               |           |     |     |     |     |     |

## Progress tracker -

"Leadership, Culture, Procedure Optimisation, Workplace Engagement, Data & LFE, Competence & Resource are at the centre of our human factor safety improvement, the aim of this collaboration is to improve the quality of **work as done** intelligence on the project thereby, reducing **the drift** that can lead to unplanned events, LTI's & RIDDOR's."

- **Procedure Optimisation – February 2025** – What we write and what people understand can be two entirely different things. – Visits/engagement commenced w/c 3<sup>rd</sup> Feb.
- **Workplace Engagement – February/ March 2025** – With reporting numbers high but quality low, this piece of work will focus on boosting reporting quality using the Threat & Error Management approach. – Commenced 6<sup>th</sup> Feb.
- **Data & Learning From Experience (LFE) – March 2025** – For LFE to be effective it needs intelligent interpretation of data. Trends beyond the usual methods will be used to improve risk-based decision making.
- **Competence & Resource – April 2025** – Competence & Resource is affected from the initial onboarding impression created on day 1 through to how we select, recruit, promote and retain our staff.
- **Leadership – March 2025** – Key foundations for driving forward with a shared vision must involve how an understanding of collaboration, is an essential component for any leader to succeed.
- **Culture – March/April 2025** – Reinforcing the focus on learning rather than blaming will be key part in creating psychologically safe spaces to perform.



## 01 ALIGN PROJECT TEAM RESTRUCTURE



- 1. PROJECT DIRECTOR IN PLACE ✓
- 2. SAFETY TEAM RESTRUCTURING COMMUNICATION COMPLETE ✓
- 3. RE-FOCUS ON MAJOR RISKS ✓

## COMMISSION GMR HUMAN FACTORS 07



PROCESS PROCEDURE OPTIMISATION REPORT COMPLETED AND BRIEFED TO TUNNELLING LEADERSHIP - 14th MARCH ✓

TEM WORKSHOPS COMPLETED - 18th MARCH ✓

SHAFTS / CVV THREAT & ERROR MANAGEMENT WORKSHOPS - MAY 2025 ✓

## 02 UTILISE & ANALYSE THE DATA AVAILABLE TO DRIVE SAFETY MANAGEMENT



- 1. SIMPLIFIED AIM HIGH APP LIVE ✓
- 2. NEW AIM HIGH (POWER BI) REPORT RELEASED ✓
- 3. FOCUS ON OBSERVATION NUMBERS REQUIRED ✓

## 03 DELIVER ALIGN LEADERSHIP EXCELLENCE SEMINAR



- 1. DELIVERED ON 4th / 5th MARCH ✓
- 2. CREATION OF MASTERPLAN MAY 2025 ✓

TEAM RESTRUCTURE 01

HUMAN FACTORS 07

DATA & SAFETY MANAGEMENT 02

WEEKLY BULLETIN 06

LEADERSHIP EXCELLENCE SEMINAR 03

LAMBO / POWRA 05

ALIGN  
PERFORMANCE IMPROVEMENT PLAN

SENIOR WORKS MANAGERS 04

## 04 RE-EMPOWER THE ROLE OF SENIOR WORKS MANAGERS



- 1. SENIOR WORKS MANAGERS STRUCTURE COMMUNICATED - COMPLETED ✓
- 2. SPECIALIST COACHING MENTORING PROGRAMME WITH EDDIE WOODS - UNDERWAY ✓


## DEVELOP HS & W WEEKLY BULLETIN FOR WORKFORCE 06



6 NEWSLETTERS PRODUCED AND BRIEFED SITEWIDE ✓

BRIEFING TO TEAMS TO MONITOR CONSISTENTLY ✓

## REVIEW LAMBO / POWRA 05



POWRA TRAINING PACK COMPLETED ✓

POWRA ROADSHOW TRAINING COMPLETED ✓

LAMBO DATA MANAGEMENT LIVE ✓



# SPIP 1.2

## KEY FOCUS AREAS

### 1. Masterplan Workshop Outputs – Coralie Peroux

- Follow on from Excellence Workshops in SPIP 1
- Completion, Key dates, Caretaking, Handover & Demob

### 2. Senior Work Managers


- OH training and awareness
- POWRA focus around our top 3 Health hazards

### 3. GMR – 6 Principals to simplify processes

### 4. Middle Managers Empowerment

- Drive the data findings from LAMBO, POWRA, HIPO and Safety Incidents in their weekly team meetings
- Bridge gap between Supervision and Senior Management
- Embed learning from Lesson learnt and continuous improvement within their teams

### 5. Supply chain commitments -

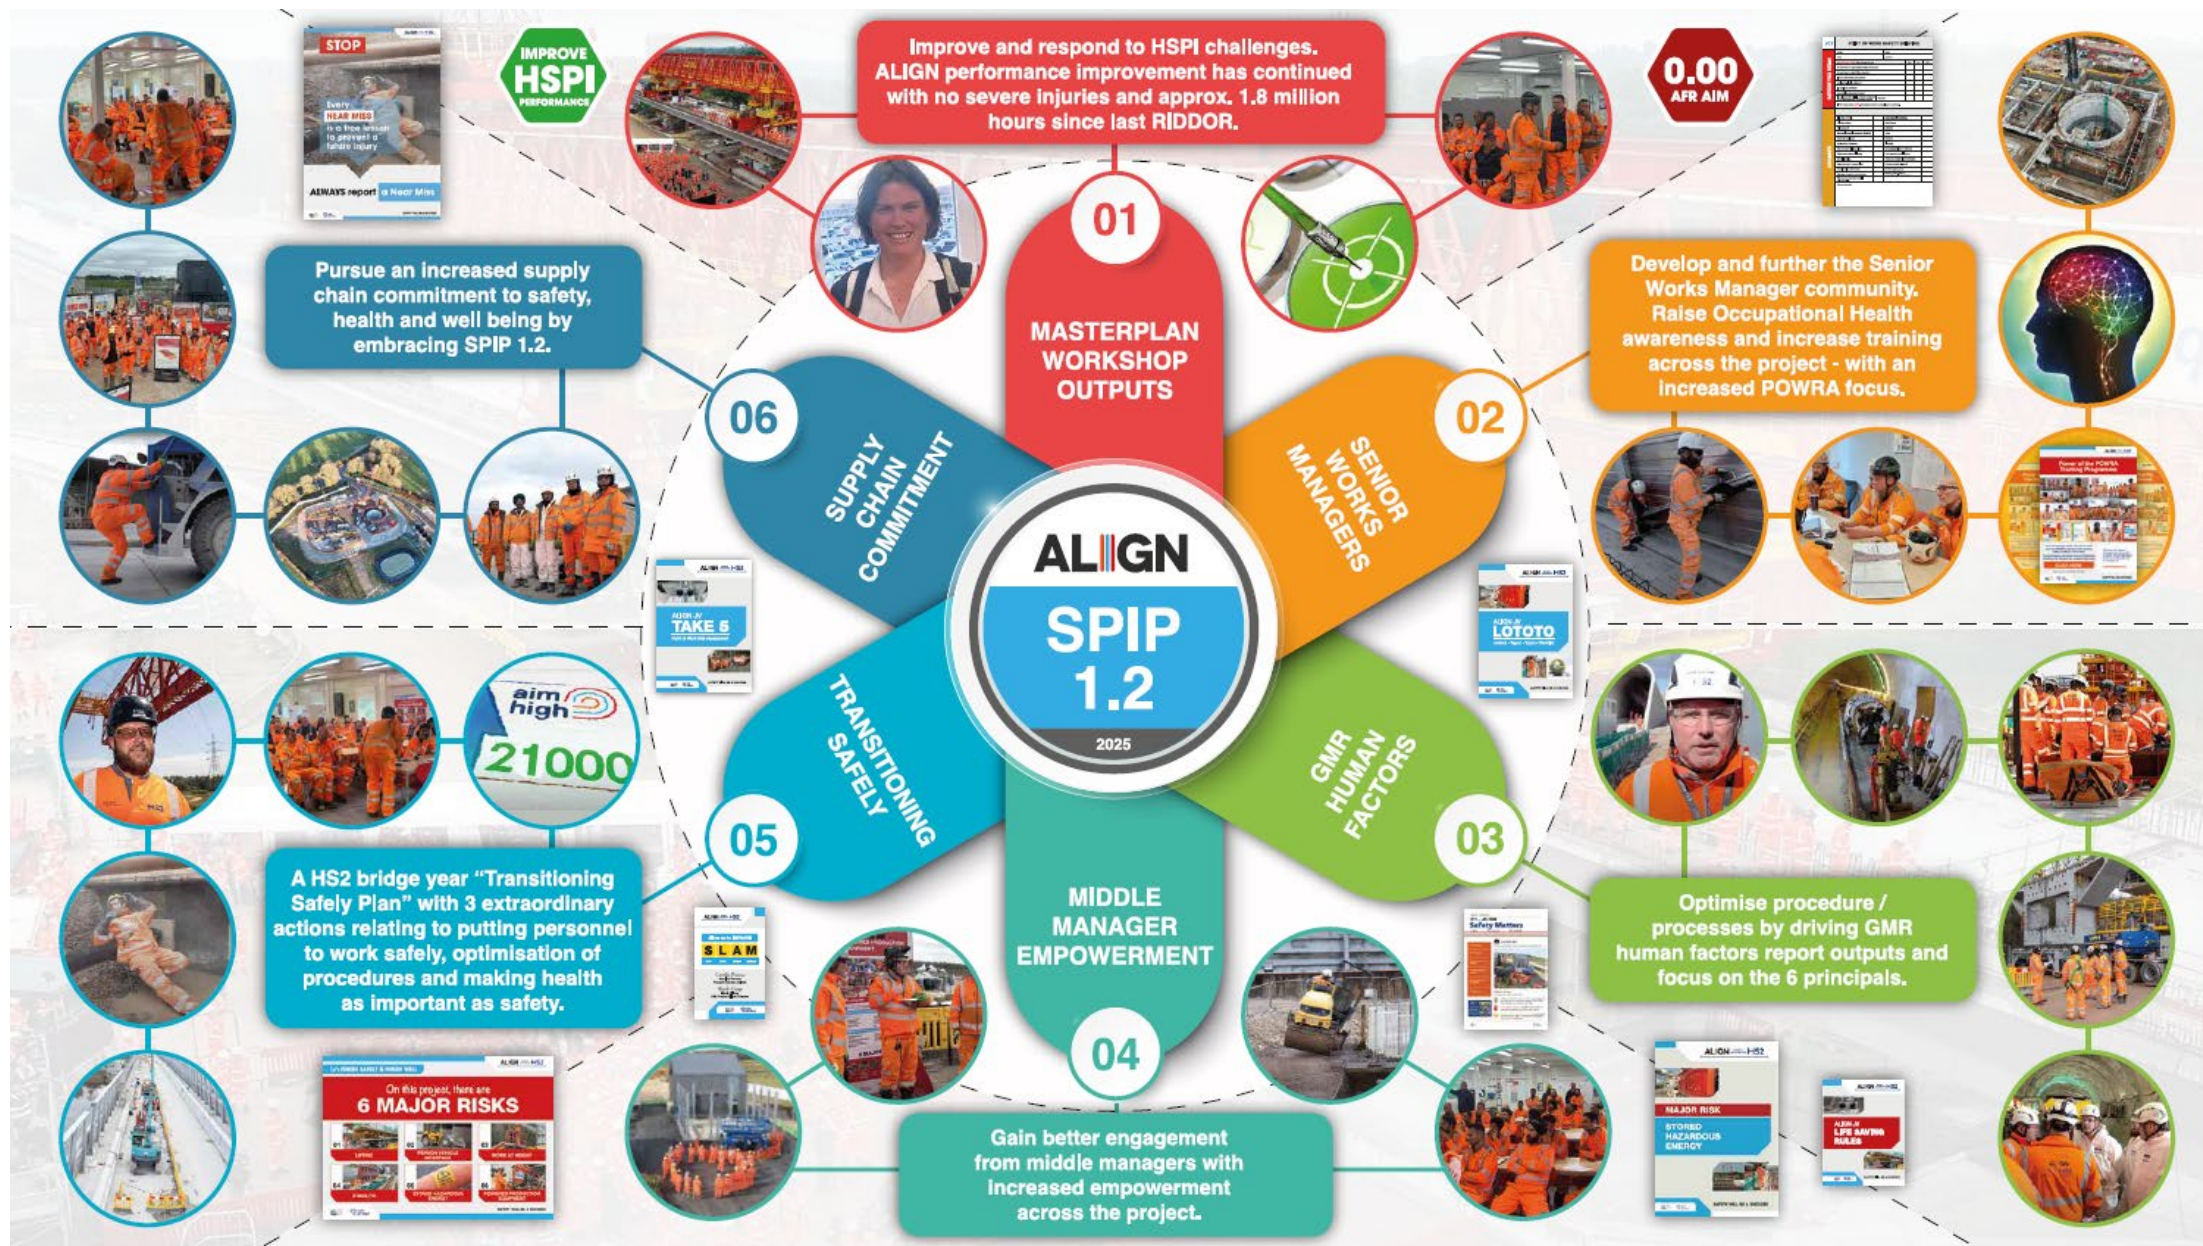

# Closure Summary

