

Management of unforeseen situations Health & Safety

Reference: BYTP-PRO-H&S-2114-vA

Company	Domain	Document type	No Sequence	Revision index	Langue
BYTP	H&S	PRO	2114	A	EN



BUILDING FOR LIFE

Revision	Date	Written by	Checked by	Approved by	Type of modification
A	04/04/2025	F.Martin	V.Avrillon	L.Knoll	Document created

Table of contents

1. Objective	2
2. Scope.....	2
3. Reference documents.....	2
4. Definitions and abbreviations	3
5. Roles and responsibilities	3
5.1. Project Director/Manager	3
5.2. Validators.....	3
5.3. Project Technical Manager	4
5.4. Health and Safety Manager.....	4
5.5. All Personnel	5
6. Steps of Unforeseen situation Management.....	5
6.1. Identify unforeseen situation.....	5
6.2. Protection of the area	6
6.3. Collective analysis.....	6
6.4. Levels of validation	6
6.5. Implementation of Actions	7
6.6. Communication	7
7. Archiving and traceability	7
8. Appendice	8
8.1. Annex 1 - Leaflet to safely manage unforeseen situation.....	8
8.2. Annex 2 - Poster who to contact in case of an unforeseen situation.....	9
8.3. Annexe 3 - Unforeseen situation management declaration form	10

1. Objective

The purpose of this document is to establish a clear, structured and effective organisation for managing unforeseen situations that may occur on construction sites.

This process aims to quickly identify unforeseen situations, implement appropriate actions to manage them and ensure traceability of decisions taken when required.

It defines the criteria and methods for distinguishing between informal and formal management approaches, according to the different types of unforeseen situations encountered.

The principles established in this document are integrated into the management plans of each BYTP project, considering local specificities, applicable regulations and contractual requirements.

2. Scope

This document applies to all BYTP personnel involved in projects/sites.

The project/site shares the BYTP culture for the management of unforeseen situations with its service providers and subcontractors, particularly the importance of detecting unforeseen situations and the subsequent STOP.

The project/site may, at its discretion and if organisationally feasible, make this procedure applicable for its service providers and subcontractors.

In the case of projects where BYTP is part of a joint venture (JV), a consortium, or is a co-contractor, the project-specific procedure will include at least the provisions described in this document, as well as any non-conflicting provisions from our partners. It should be adopted at the start of projects during health and safety initial briefings.

If any part of this document conflicts with a local requirement and is less stringent than that local regulation, then the corresponding section(s) of the local regulation shall apply.

3. Reference documents

- Safety Culture Tools - Axis 2 Managing the unforeseen in Safety
 - Generic leaflet
 - Employee leaflet
 - Validator leaflet
 - Good practice poster
 - Dangerous act poster
 - Poster - who to contact in case of an unforeseen situation
- Unforeseen situation management declaration form (BYTP-H&S-FOR-2115)

4. Definitions and abbreviations

Unforeseen situation An unforeseen situation is an unforeseen occurrence or situation that disrupts the originally planned course of a task

Level 1 Unforeseen situation Unforeseen situation with no impact on major risks

Level 2 Unforeseen situation Unforeseen situation with an impact on major risks or a minor impact on technical documentation

Level 3 Unforeseen situation Unforeseen situation with a significant impact on technical documentation (sizing, design, methods)

5. Roles and responsibilities

5.1. Project Director/Manager

The Project Director/Manager ensures the structured and effective management of unforeseen situations that may arise on their project. Their responsibilities include:

- Implementing, understanding, and applying the management of unforeseen situations in accordance with the procedures defined in this document
- Coordinating the necessary technical and human resources
- Validating the actions to be taken for level 3 unforeseen situations, which have a significant impact on the project's technical documentation (calculations, design or methods)
- Validating, if deemed necessary, the actions for level 2 unforeseen situations, which have a minor impact on technical documentation
- Collaborating with the Health and Safety Manager to ensure compliance with protocols and best practices for managing unforeseen situations

For large-scale projects and depending on the organisation in place, the Project Director/Manager may, if desired, delegate their validation responsibilities to their management line

5.2. Validators

Validators, designated by the Project Director/Manager, are involved in managing unforeseen situations according to three levels, based on their impact.

General responsibilities of validators:

- Ensure that their teams understand how to manage unforeseen situation and apply its principles

- Inform project management depending on the level of the unforeseen situation
- Supervise and ensure the effective implementation of decided actions
- Collaborate with the Health and Safety Manager to ensure compliance with the protocols for managing unforeseen situation

Level 1 Validator

- Handles unforeseen situations having no impact on major risks
- Validate the restart of activity after appropriate measures are implemented

Level 2 Validator

- Handles unforeseen situations having impact on major risks or having a minor impact on technical documentation
- Coordinates the necessary discussions to analyse and solve the situation
- Validates corrective measures and the restart of activity if he considers that the risks are under control

Level 3 Validator

- Manages unforeseen situations having a significant impact on technical documentation
- Supervises the management of the new approach and the necessary technical changes in coordination with the project's Technical Manager
- Completes and validates his section within the *Unforeseen situation management declaration form* (BYTP-H&S-FOR-2115) before any restart of activity

5.3. Project Technical Manager

The Project Technical Manager is mainly involved in level 3 unforeseen situations, which require changes to the technical documentation. His responsibilities are to:

- Analyse the impact of the unforeseen situation on the technical documentation (calculations, design, methods)
- Propose and validate the necessary technical modifications in coordination with the Project Director/Manager
- Supervise the update of technical documents before resuming activity

5.4. Health and Safety Manager

The project's Health and Safety Manager, or his equivalent (in the absence of a full-time H&S Manager at site), supports the implementation of unforeseen situation management according to the requirements defined in this document for the project(s) under his responsibility.

His responsibilities include:

- Assisting the Project Director/Manager in establishing an effective unforeseen situation management process
- Helping to detect unforeseen situations
- Collaborating with validators to ensure the proper resolutions of unforeseen situations
- Ensuring that the implemented actions comply with safety and risk prevention requirements

5.5. All Personnel

Every employee present on site (or project office) has an active role in the prevention and management of unforeseen situations. They must:

- Detect any unforeseen situation and step back from their current activity
- Stop the ongoing task if the unforeseen situation presents a risk
- Immediately inform the relevant validator, depending on the level of impact

6. Steps of Unforeseen situation Management

6.1. Identify unforeseen situation

The first challenge for those involved in an activity is to detect and become aware that they are facing an unplanned situation. The following questions should help identifying such unforeseen situation:

Human resources	Tasks	Work management
I am a member of a full team with all necessary competencies for achieving our tasks. Questions : 🟢 The team is complete 🟡 I don't know 🔴 Someone is missing ? Competencies ?	The tasks I have to achieve were explained by my hierarchy and I have understood what I have to do. Questions : 🟢 Understood 🟡 I don't know 🔴 I have no briefing	I know the planning, the tasks to achieve and coactivities scheduled. Questions : 🟢 Clear, defined and understood 🟡 I don't know 🔴 Unexpected coactivity ? Planning modified ?
Logistic	Equipment	External factor
Deliveries on site are scheduled. I am aware of the planning and delivery areas are available. Questions : 🟢 As planned 🟡 I don't know 🔴 Delayed ? Non organised ?	I have all the equipment I need and in good condition. Questions : 🟢 Adapted and functional 🟡 I don't know 🔴 Missing or faulty	I don't encounter unexpected obstacle during works and I don't notice worth weather condition. Questions : 🟢 None 🟡 I don't know 🔴 Something unexpected ? (weather, obstacle...)

See Appendix 1 - Leaflet for Unforeseen situation Management

As unforeseen situations are not of the same severity, they must be characterised to be handled at the appropriate level 1, 2, or 3.

When a method statement includes critical stop points or limit values, regular checks are necessary. Any deviation from these values must be considered as an unforeseen situation, requiring the activity to stop and the validator to be notified.

When an unforeseen situation is identified, the related person must immediately stop the ongoing activity to prevent any escalation of the situation and report the event to the level 1 or 2 validator for the relevant area.

6.2. Protection of the area

Once the unforeseen situation has been identified, the activity is stopped and the area is secured, if necessary, to prevent any risk of accident or escalation.

The relevant validator is immediately informed.

In the case of a major risk, the Health and Safety Manager must also be consulted immediately.

6.3. Collective analysis

The analysis must be collaborative and carried out as soon as possible, with the participation of the relevant validator(s), the responsible managers, and the Project Technical Manager for level 3 unforeseen situations.

The proposed solutions must comply with:

- BYTP Health and Safety standards
- Project-specific procedures
- Contractual and regulatory requirements applicable at site

6.4. Levels of validation

Depending on the nature and impact of the unforeseen situation, three levels of action validation are defined:

Level 1: Unforeseen situation with no impact on major risks

- Validation by the level 1 validator designated for the relevant area
- Restart of activity can be decided without formal documentation, unless specifically required by the project

Level 2: Unforeseen situation with an impact on major risks or a minor impact on technical documentation

- Validation by the level 2 validator designated for the relevant area, in collaboration with the H&S Manager
- Restart of activity can be decided without formal documentation, unless specifically required by the project

Level 3: Unforeseen situation with a significant impact on technical documentation (calculation, design, methods)

- Validation by the level 3 validator, in collaboration with the Project Technical Manager

- The resolution of the unforeseen situation requires formal validation/approval by the Project Director/Manager
- Mandatory traceability is required:
 - The *Unforeseen situation management declaration form*, based on Appendix 3, must be completed
 - Traceability is ensured using a dedicated project register

6.5. Implementation of Actions

Once validated, the defined actions must be implemented under the responsibility of works supervisory personnel.

The relevant validator ensures the effective application of the decided actions before authorising the activity to resume.

Post-implementation follow-up may be necessary, particularly for level 3 unforeseen situations, to assess the effectiveness of the measures taken.

6.6. Communication

Level 2 and 3 unforeseen situations that occurred the day before are systematically addressed during the pre-start briefings.

The objective of this communication is to:

- Inform all teams about the unforeseen situations encountered and the measures implemented
- Raise awareness among personnel about the identified risks and lessons learned
- Ensure proper understanding and application of corrective actions to prevent recurrence of the unforeseen situation

The team Leader/Foreman or the Health and Safety Prevention Manager, if present full-time at site, leads this discussion based on feedback from validators and operational teams.

For level 3 unforeseen situations, enhanced communication may be required, including a feedback report to be shared with project stakeholders.

7. Archiving and traceability

The project archives the *Unforeseen situation management declaration form* for level 3 unforeseen situations and maintains an associated register throughout the duration of the project, under the responsibility of the Project Director/Manager.

After the end of the project, the *Unforeseen situation management declaration forms* for level 3 unforeseen situations are kept according to the project's document retention period.

8. Appendice

8.1. Annex 1 - Leaflet to safely manage unforeseen situation

People to CONTACT

I share it during the next briefing

Detect unforeseen event

BEFORE TO START

- 1 I know the tasks I have to perform
- 2 I know the rules to respect
- 3 I have checked my material, my equipment and the environment

DURING WORKS

- 1 I don't put myself in danger
- 2 I look at my colleagues around me to check if they are not putting themselves in danger
- 3 I detect all unexpected or non usual situations

Human resources

I am a member of a full team with all necessary competencies for achieving our tasks.

Questions :

- ✓ The team is complete
- ✗ I don't know
- ✗ Someone is missing? Competencies?

Logistic

Deliveries on site are scheduled. I am aware of the planning and delivery areas are available.

Questions :

- ✓ As planned
- ✗ I don't know
- ✗ Delayed? Non organised?

Tasks

The tasks I have to achieve were explained by my hierarchy and I have understood what I have to do.

Questions :

- ✓ Understood
- ✗ I don't know
- ✗ I have no briefing

Equipment

I have all the equipment I need and in good condition.

Questions :

- ✓ Adapted and functional
- ✗ I don't know
- ✗ Missing of faulty

Work management

I know the planning, the tasks to achieve and coactivities scheduled.

Questions :

- ✓ Clear, defined and understood
- ✗ I don't know
- ✗ Unexpected coactivity? Planning modified?

External factor

I don't encounter unexpected obstacle during works and I don't notice weather condition.

Questions :

- ✓ None
- ✗ I don't know
- ✗ Something unexpected? (weather, obstacle...)

Safely manage unforeseen events together

I CONTINUE TO WORK

I ASK FOR MORE INFORMATION

I FACE AN UNFORESEEN (return the document)

SAFETY

We safely manage UNFORESEEN EVENT together !

1 IDENTIFY

- We detect an unforeseen event with the help of the tips on the other side.

2 MANAGE / PROTECT

- I protect the others and myself.
- We secure the zone / area concerned.

3 TOGETHER

- We think together to a solution in Compliance with the Life Saving Rules.

4 SHARE

- I never take a decision alone by myself whatever is my position in the organisation.
- We always contact the «people to CONTACT» to alert/share the solution we imagine.

5 VALIDATE

- We wait for the final validation before restarting any works.

6 UNANIMOUS


- We are all informed of the actions taken.
- The restart of the works is safe.

10 LIFE SAVING RULES AS THE LAST LINE OF DEFENCE TO AVOID A SEVERE ACCIDENT

- ✓ I ensure that the load being lifted is a **single unit**.
- ✓ I do not stand between a load and a **fixed obstacle**, or **under the load** when it is being **lifted up** or **lowered down**.
- ✓ I use lifting accessories that are **checked and suitable** for the load.
- ✓ I do not enter an **exclusion zone**.
- ✓ I respect the **traffic segregation lanes** for vehicles and pedestrians
- ✓ I do not go into the work zone of moving plant or vehicles without the **operator's acknowledgement**.
- ✓ I do not enter an **exclusion zone**.
- ✓ I do not **expose myself** to the risk of falling from an unprotected edge, and I **protect the openings** and open edges that I create.
- ✓ I do not enter an **exclusion zone**.
- ✓ I **stabilise** materials, plant and equipment at all times, and I ensure that the **support they rely on can take the load**.
- ✓ I do not enter an **exclusion zone**.
- ✓ I use **suitable equipment or tools** for the task and I **do not override** their safety systems.
- ✓ I do not enter an **exclusion zone**.
- ✓ I check that there is **no residual energy** before carrying out any work on networks or production equipment.
- ✓ I do not enter an **exclusion zone**.

8.2. Annex 2 - Poster who to contact in case of an unforeseen situation

MANAGING UNFORESEEN SITUATION ON OUR SITE

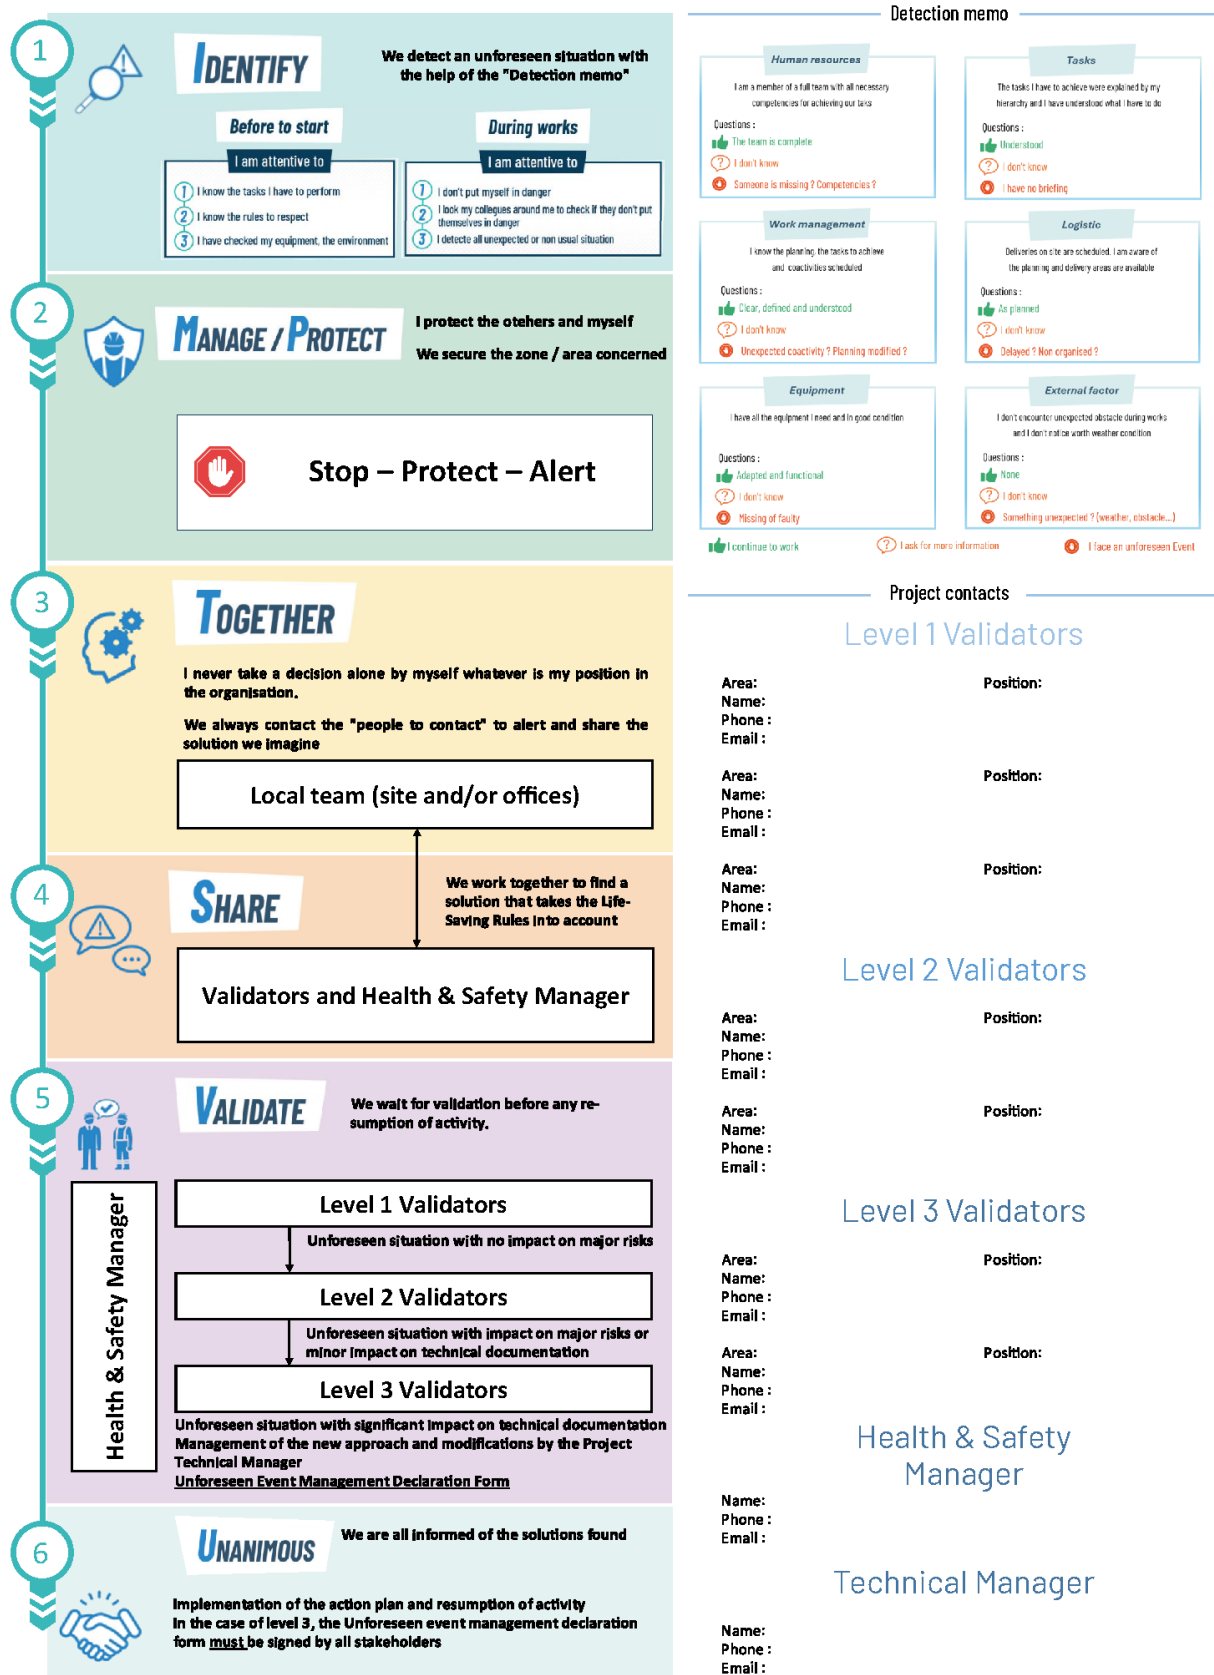

8.3. Annexe 3 – Unforeseen situation management declaration form



NAME OF THE LEAD CONTRACTOR / JOINT VENTURE
PROJECT NAME

PROJECT LOGO

UNEXPECTED SITUATION MANAGEMENT DECLARATION FORM				
Document reference number Date:			Date :	
Site: Requester: Position :		Date: Signature:		
<u>Title of the change:</u>				
<u>Description:</u>				
<u>Change request:</u>				
<u>List of modified documents:</u>				
<u>List of created documents:</u>				
By validating this unexpected situation management declaration, I confirm that the documentation has been updated according to the details mentioned above, that a risk analysis has been carried out under these new operating conditions, and that the associated activities may resume under this new configuration.				
Project Director's Name*:		Signature:		
Date:				
The activity is only authorised to start if all elements comply with the planned action and under the responsibility of the Project Director.				
Acknowledgement of the validation of this unexpected situation management declaration and the associated documentation by:**				
H&S Manager	Production Manager	Site supervisor	Site foreman	Team leader
Name	Name	Name	Name	Name
Date	Date	Date	Date	Date
Signature	Signature	Signature	Signature	Signature

*For large-scale projects and depending on the organisational structure in place, the Project Director/Manager may, if desired, delegate their validator responsibilities to their management line

**All signatures must be collected before resuming the activity.



Unexpected situation management declaration form
BYTP-FOR-H&S-2115-VA | 21-03-2025
Page 1 sur 1

