

Knowledge Management

Construction Site Feedback Report Process

Référence

Dom.		N° Séqu.					Ind.	Title	Language
KM	1	0	1	2	1		B	Construction site feedback report process	EN

Révision

Index	Date	Written by	Checked by	Approved by	Description of the adjustment
A	16/02/2022	Aba	PHV	PHV	First diffusion
B	04/10/2024	Aude Babled	PHV	PHV	Changes related to the responsibilities of REX stakeholders and consistency with the fundamentals of performance

Table of Contents

<i>Table of Contents</i>	2
1. Context.....	3
2. CSF report Structure	3
3. Responsibilities	6
4. Implementing rules	7
4.1 Identification of topics to be capitalised	7
4.2 Planning.....	7
4.3 Drafting of Synthesis reports or EOA report	7
4.4 Review	7
4.5 Reports follow-up	8
4.6 Final Review	8
Appendix 1 KM-10123-B CSF Planning and monitoring template	8
Appendix 2 KM-10162-A Missions of the KM Feedback manager	8
Appendix 3 KM-10161-1 KM tools	8
Appendix 4 KM-10122-B CSFR Recommendations	8

1. CONTEXT

The Construction Site Feedback Report (CSFR) is implemented in a process **as soon as** the construction site activity starts.

The CSFR process discussed here is one element among others in what is known, **in general, as REX (Return Of Experience)**.

The CSFR is produced during the implementation stage of our projects.

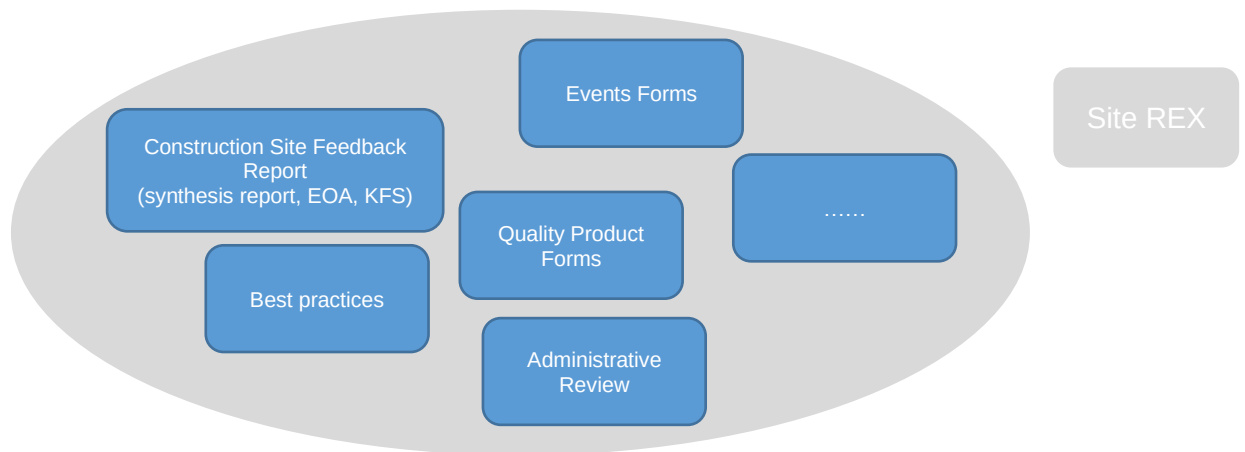


Fig.1. What the REX (Return on Experience) contains – execution stage

Nota: The development of a specific tender phase report is not addressed here.

2. CSF REPORT STRUCTURE

The **Construction Site Feedback Report (CSFR)** is the final state of the feedback in the execution phase of the project. This is the chapeau or the synthesis.

The table of contents of the CSF report consists of:

- Cross-cutting project chapters: project description, management, A&F, communication, HR, etc. CSF report outline,
- The compilation of the synthesis report of support services
- Synthesis report of construction work with Key Figures Sheet (KFS)
- End of activity reports (EOA report)

The **Synthesis Report**¹ are of various kinds:

- They concern the construction works as a whole
- They concern support services (safety, environment, quality, communication, etc.) and present the main features of the project (see forms).

The **Synthesis reports of construction works** are composed of²:

- defined transversal chapters (*see frames*),
- **KFS** (Key Figures Sheet), which define the nature and size of the construction work, and give the key figures,
- One or more EOAR (End of Activity Report), which enables you to reconstruct the resources required to complete an activity, and to compare with price studies and standards (MOSE+, for example),
- Appendices (execution documents, notable PowerPoint, etc.)

¹ Nota: The process used up to now referred to End of Activity Reports (EOAR) for feedback from support services, or construction works (a bridge, a tunnel, a station), then to Technical Information Sheets (TDS) for parts of construction works, details of an activity, etc.

Reflections on Performance Fundamentals, which incorporate the notion of feedback, have led us to modify this terminology. End of activity report becomes Synthesis report , Technical Information Sheets becomes End of activity report !

The general idea is that an end-of-activity report is now linked to a part of a construction work and not to the entire construction work. It is produced on an ongoing basis, must be self-supporting and to the point, and includes a comparison with Price Studies and MOSE+.

The synthetis Reportof construction work is a synthesis of the whole, dealing only with the major subjects not covered in the End of Activity Reports.

² You can find the different frames on the following link:

<https://bouyguesconstruction.sharepoint.com/sites/bytp446301100/Rex/Forms/AllItems.aspx>

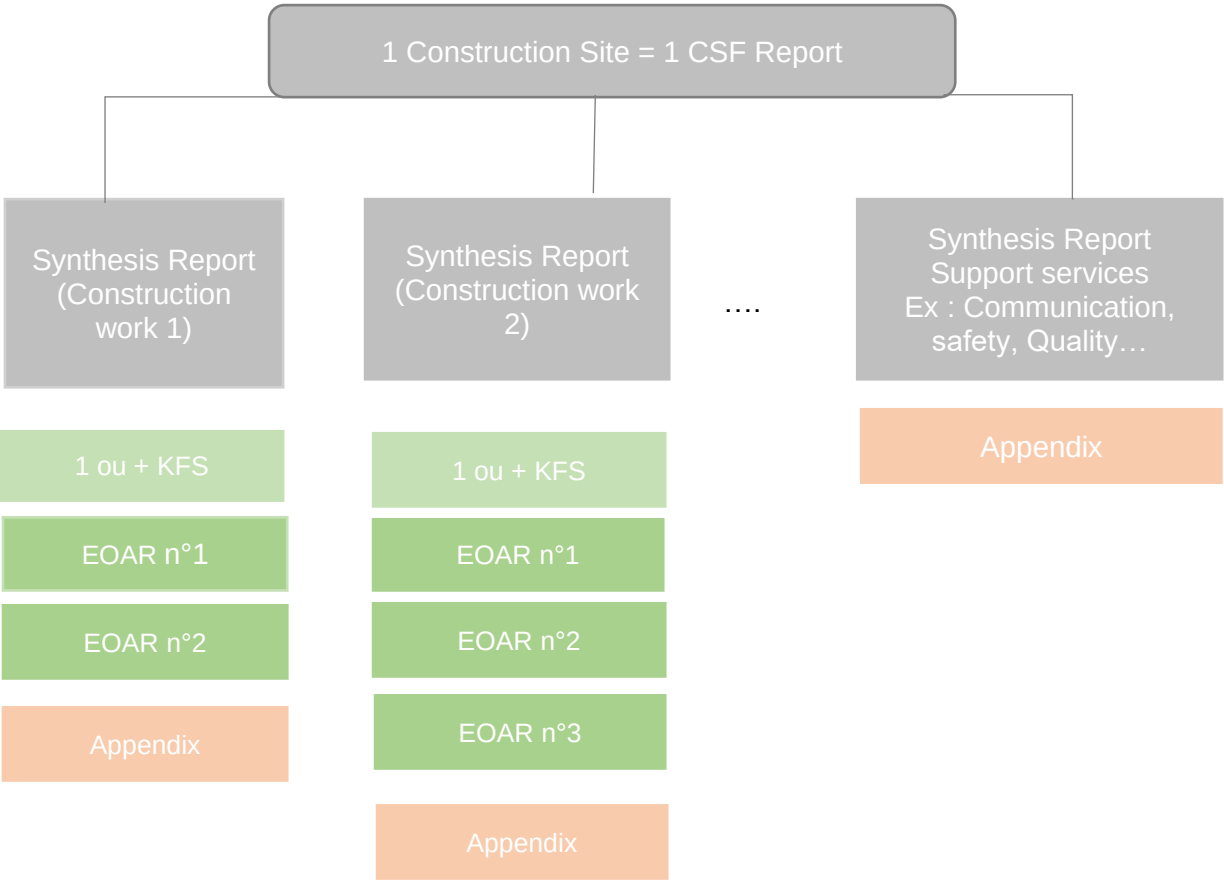


Fig.2. CSF process diagram

PROCESS Follow-up on Feedback project in progress

Swimlanes (Roles):

- Feedback Project writer
- Project management
- Project Feedback monitoring manager
- KM – Feedback manager
- Technical service & support services

Process Flow:

- Defining Feedback needs** (Project management, Technical service & support services)
- Designation of the project KM manager within the project** (Project management)
- Send activity forecasts & schedules to KM Feedback manager** (Project management to KM)
- Collects data for the Feedback as the activity progresses** (Feedback Project writer)
- Starts writing the end of activity reports no later than 80% of the activity and finishes no later than 3 months after the end of activity** (Feedback Project writer)
- Send to KM Feedback manager** (Feedback Project writer to KM)
- Write the final document** (Feedback Project writer)
- Internal project validation** (Project management)
- Document naming** (Feedback Project writer)
- Report forwarded to KM Feedback manager** (Feedback Project writer to KM)
- Write the final summary** (Project management)
- Storage – Provision – Company distribution** (KM)
- Rereads and provides feedback on the feedback (comments, questions,...)** (Technical service & support services)

Over time : Definition of feedback needs & production of frames as needed

4. IMPLEMENTING RULES

4.1 IDENTIFICATION OF TOPICS TO BE CAPITALISED

When a project is awarded, a KM Feedback manager is appointed within the KM team.

From the “Transfer” meeting till technical launch meeting, the list of specific requests and expectations in terms of feedback is specified by the Technical Department, skill networks & functional support services. It may be amended during the project and focuses on key topics.

During the worksite preparatory phase and starting phase the project team connects with the KM department and starts developing the construction site feedback report’s structure and the list of the EoA Reports.

A project feedback (REX) monitoring manager is appointed.

4.2 PLANNING

At the latest, by the 20% progress milestone, the project feedback monitoring manager draws up the schedule of the synthesis reports, EOARs and other documents to be capitalised.

The project management ensures that the preparation and issuing of the EOA reports is planned in line with the project time schedule.

This time schedule of EOARs is **updated throughout the project** depending on the newly identified topics considered as important to capitalise. The the project feedback monitoring manager reminds the EOA editors of their progress.

4.3 DRAFTING OF SYNTHESIS REPORTS OR EOA REPORT

At 80% progress milestone, the EOARs’ editor starts drafting the end-of-activity report. This process is repeated throughout the execution phase of the project for all topics identified as required in an activity report. For the drafting, the data to be collected can be photos, videos, key documents... which will become support documents attached to the EOA report.

The report must be completed within **3 months of the end of the activity**.

4.4 REVIEW

A **review and checking workflow** takes place internally with the project manager. The report is then sent to the KM department who put it **online** for knowledge sharing.

Nota: The EOA reports are reviewed by KM and or Technical Department through a sample basis. and according the importance of the topic and the salient points associated with it. The KM department informs the project team and the EOA report editor whether the EOA report has been reviewed in detail or not.

If the project teams deems that the subject deserves to be better or more widely known within the company, then the team in charge of the activity will organise a webinar which will then be capitalised based on a database and made available for replay.

4.5 REPORTS FOLLOW-UP

Every three months, the project Feedback monitoring manager sends the REX progress report to the KM Feedback manager.

The project management ensures that this process is respected.

At the time of the 20%, 50%, etc... milestones a chapter is dedicated to CSF/EOA reports and more broadly to the KM within the Reporting Documentation. It provides an update on the progress of CSF/EOA, a summary of events and notable points in terms of KM – elements to be shared, negative or positive, good practices, etc. It is presented in a A4 format at most. The KM department can then manage the sharing of the related knowledge.

4.6 FINAL REVIEW

The final review³ takes place at the closing of the execution phase. It aims to review the lessons learnt from feedback – topics addressed all along the project or at the end – and to take stock of the actions taken – or to be taken – as a result of these lessons.

NB: The company uses the REX in the broadest sense to change its processes, ways of doing things and procedures in order to avoid repeating mistakes or to make the most of successes.

This review must be the subject of a meeting during which:

- The project manager presents its Construction Site Feedback report and the key points considered as important and significant for BYTP
- The KM department take stock of the elements resulting from the worksites' support and the monitoring of the actions taken or to be taken
- The Technical Department, Skills Networks and other processes REX representatives are present if necessary. They provide their insight into the REX and the actions to be implemented.
- The General Management and operations management are invited to the meeting.
- A brief, action-oriented report is drawn up for each meeting.

APPENDIX 1 KM-10123-B CSF PLANNING AND MONITORING TEMPLATE

APPENDIX 2 KM-10162-A MISSIONS OF THE KM FEEDBACK MANAGER

APPENDIX 3 KM-10161-1 KM TOOLS

APPENDIX 4 KM-10122-B CSFR RECOMMENDATIONS

³ This meeting is sometimes referred to as the 100% of progress milestone meeting (e.g. BYTPRF practice)

